

Contractor: Cleary Construction, Inc.

Plant: Beaver Dam



Slack: 1.24"


1. JBS-1155 SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


15) MH Step ML-10-TDS-NCR - 10"

0 lb

Structure Total: 27728 lb

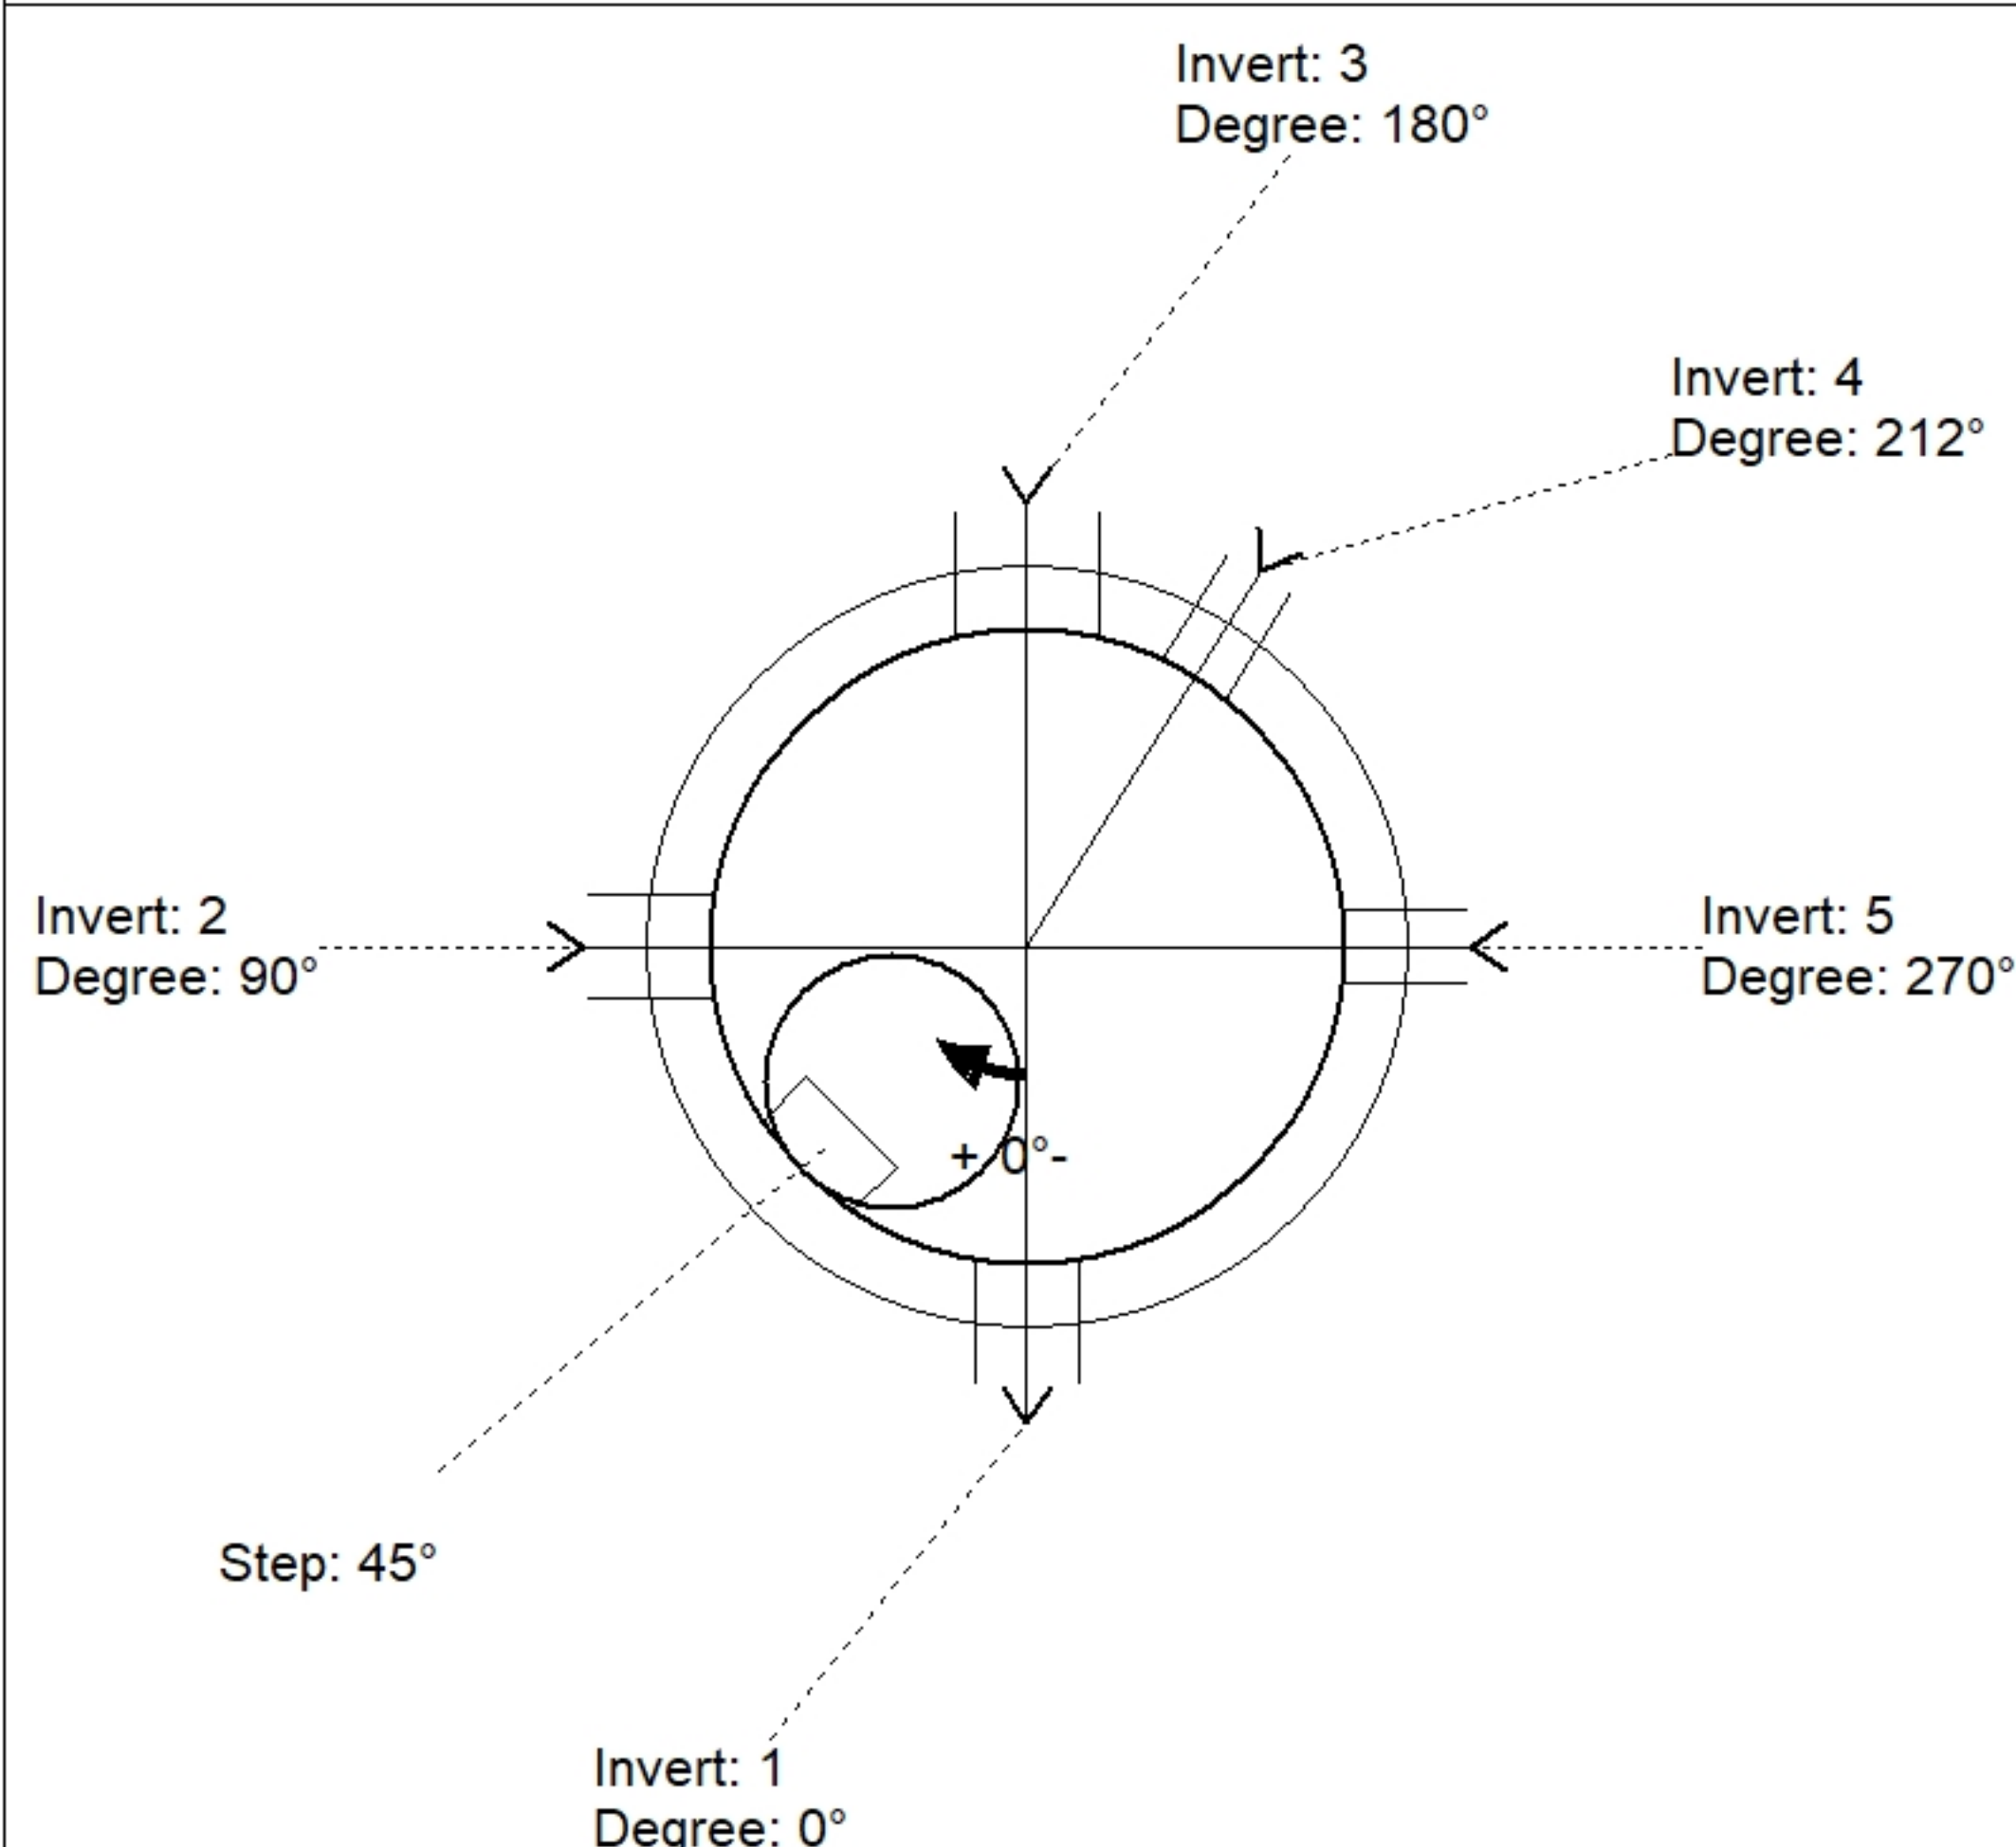

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	543.08'							
Reducer								
Invert 1	526.06'	0°	8" PVC SDR26	8.5"	9.75"	A-Lok 0285	1.125"	P1
Invert 2	536.26'	90°	8" PVC SDR26	8.5"	9.75"	A-Lok 0285	40.775"	P3
Invert 3	526.16'	180°	12" PVC SDR26	12.5"	13.75"	A-Lok 0410	2.325"	P1
Invert 4	535.46'	212°	6" PVC SDR26	6.25"	7"	A-Lok 0200	31.55"	P3
Invert 5	534'	270°	6" PVC SDR26	6.25"	7"	A-Lok 0200	14.03"	P3
Invert 6								
Invert 7								
Invert 8								

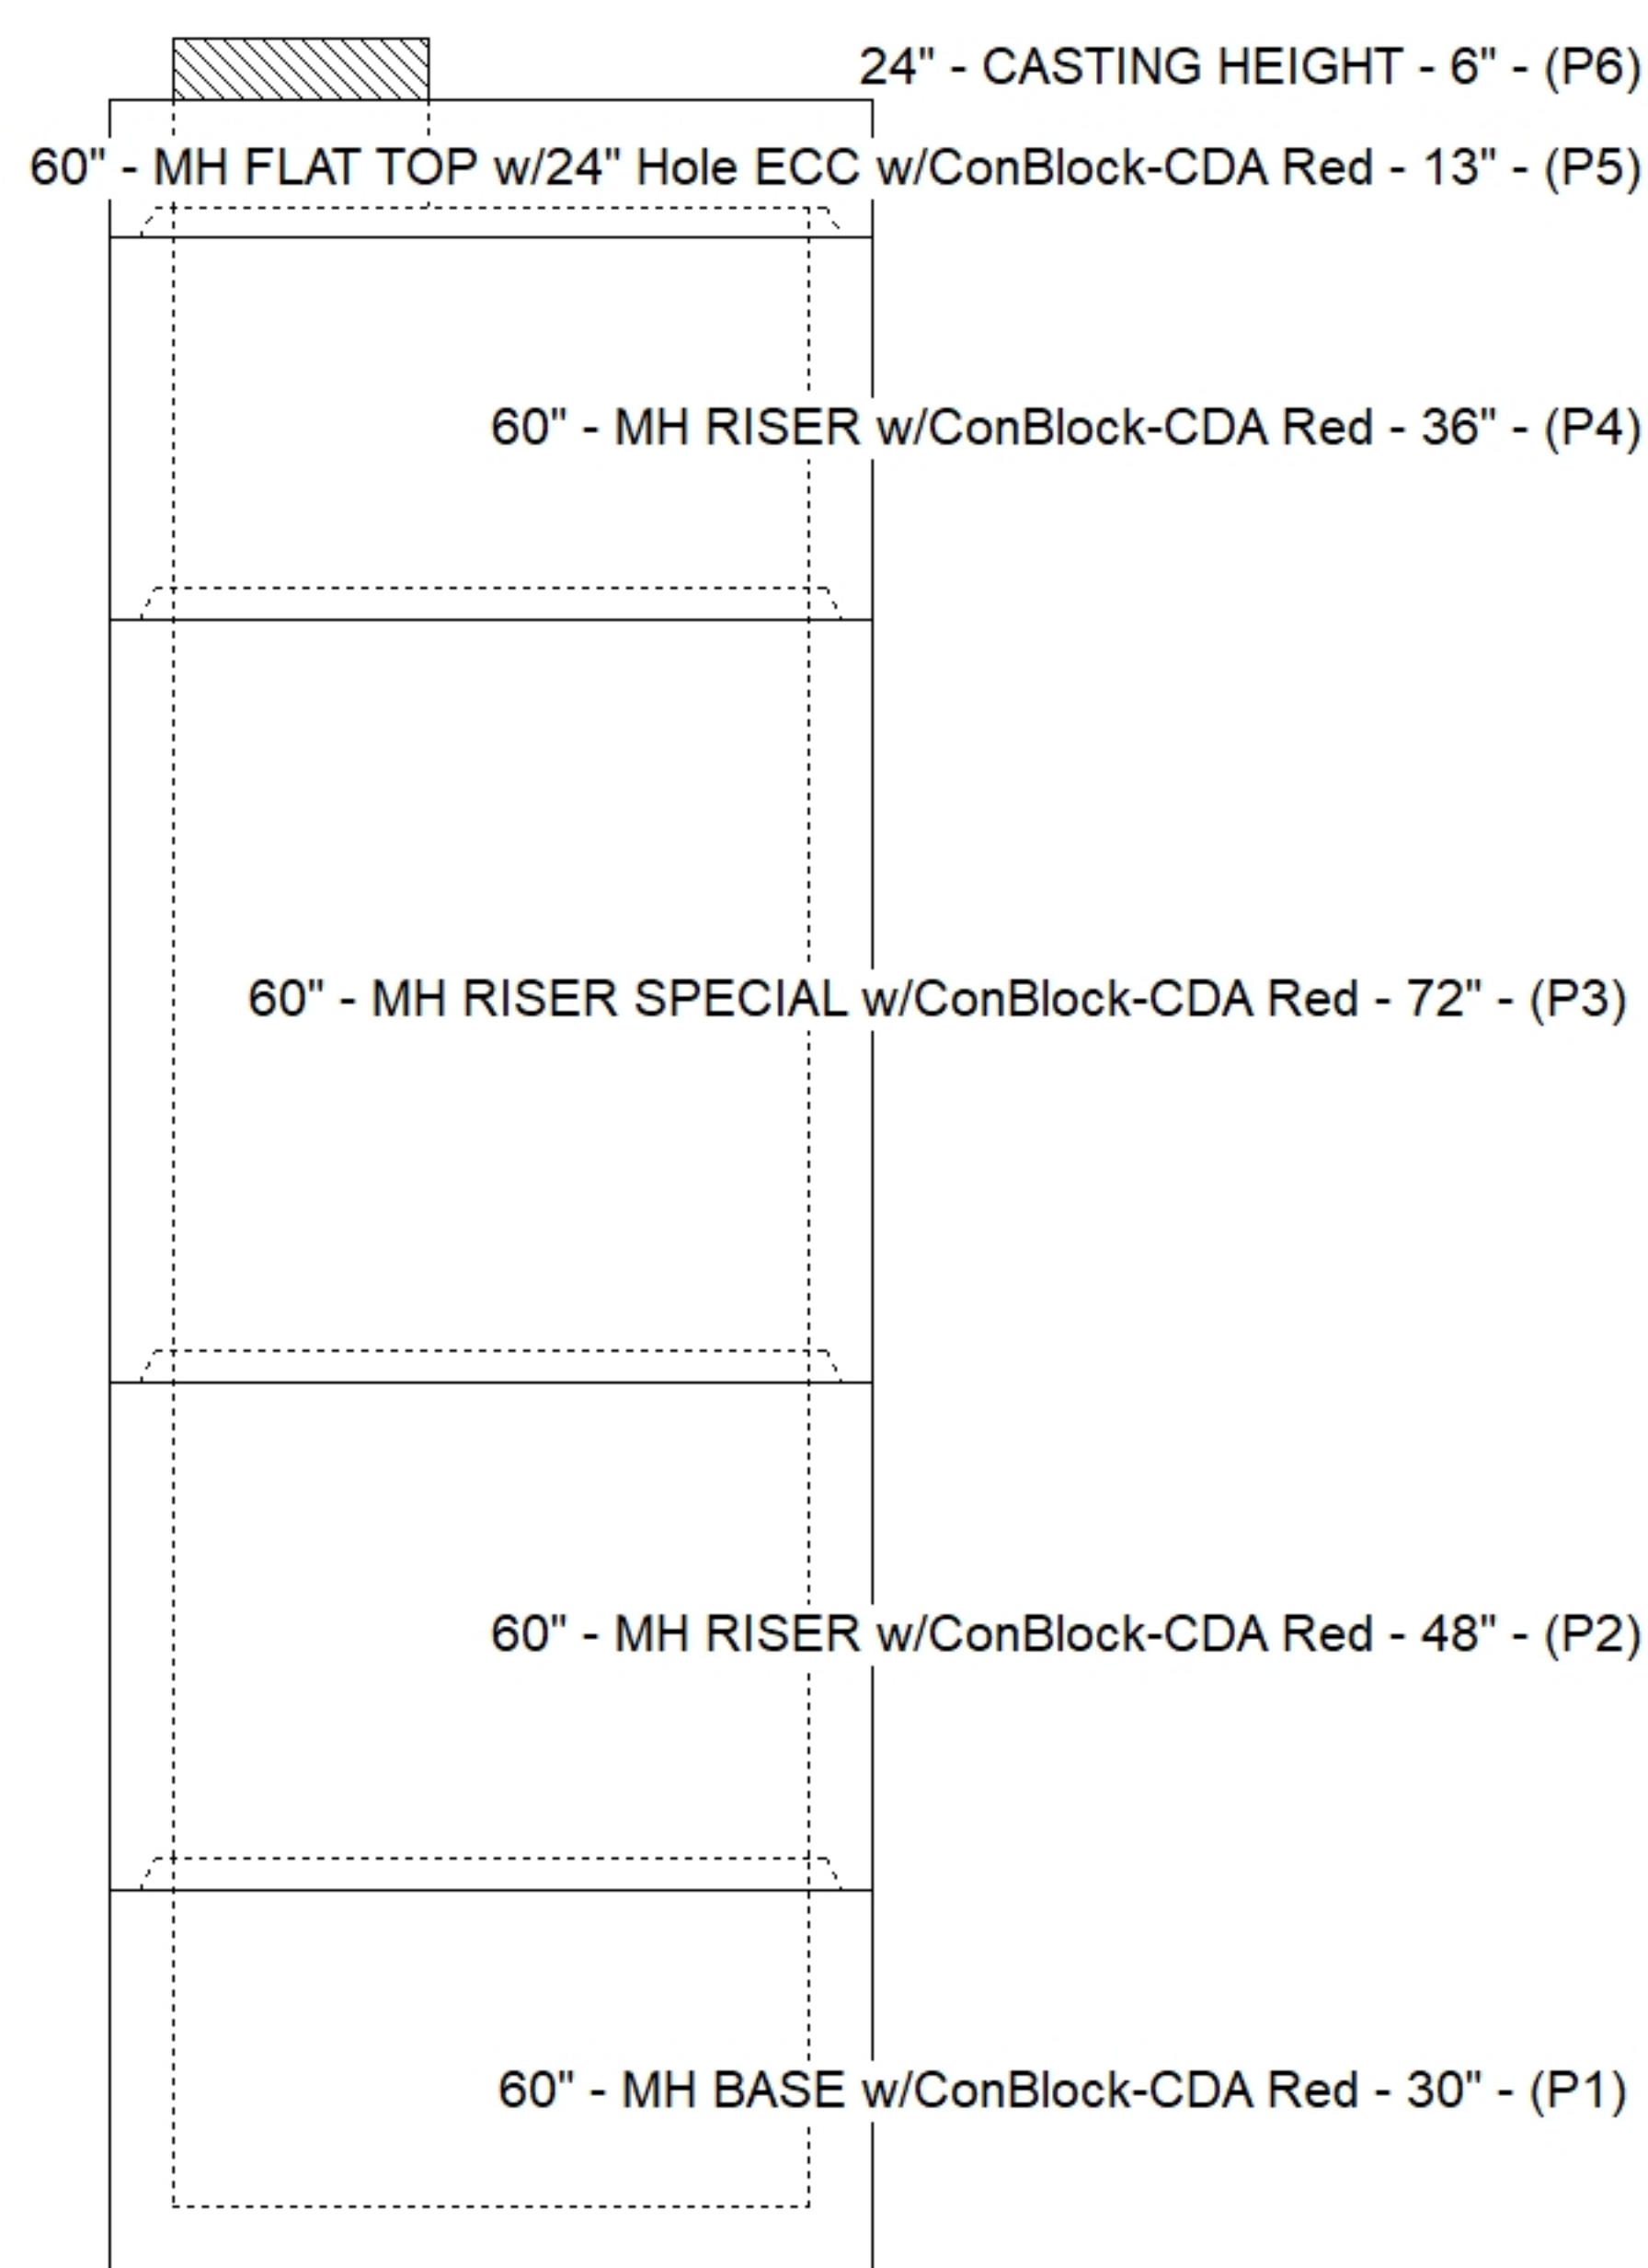

SUBMITTAL
APPROVED BY:
