

Job Name: 26-1508BC - Ferdinand State Park Culverts Replacement
 Job Location: Ferdinand, IN
 Contractor: WB Koester Construction, LLC

Plant: 100

9/15/2026 1:35:28 PM

Tech: Jared - F
 PC: E. Bradley









Structure ID: CV-2 Box Culvert

P8 BC048060-08W08T08F-09H

BOX CULVERT (08W/08F/08T) T/F T/F

NOTES:

1. BOX CULVERT IS DESIGNED PER INDOT STANDARD SPECIFICATIONS IN ACCORDANCE W/ AASHTO LRFD 9TH EDITION.
2. LOAD REQUIREMENTS = HL93.
3. COVER DEPTH = 2' TO 5'.
4. CONCRETE: 5,000 PSI AT 28 DAYS.
5. TYPE 2 WATERPROOFING MEMBRANE TO BE PROVIDED & INSTALLED BY OTHERS.
6. REINFORCING PER ASTM C1577 (GRADE 60).
7. BOX CULVERT TO BE SEALED WITH CS-102 ROLL & CS-212 12" WRAP W/ CS-75 PRIMER (SUPPLIED BY ICAST).
8. CONNECTION OF THE CUTOFF WALLS TO THE BOX CULVERT END SECTIONS TO BE PERFORMED IN THE FIELD BY OTHERS W/ DRILL & DOWEL METHOD.
9. WEIGHT = 10,265 LBS

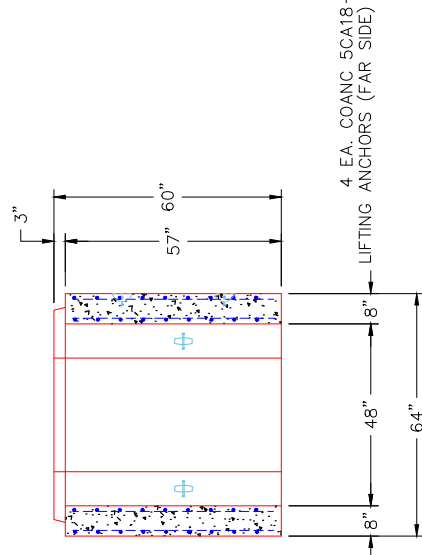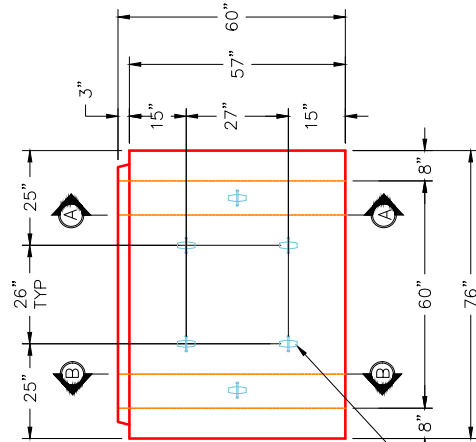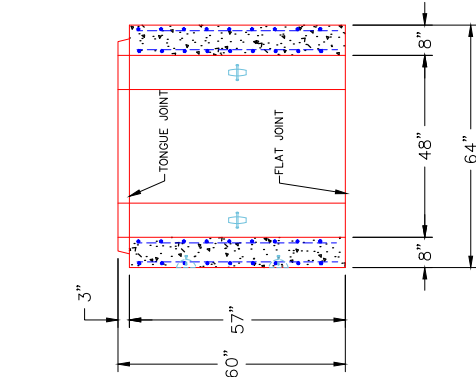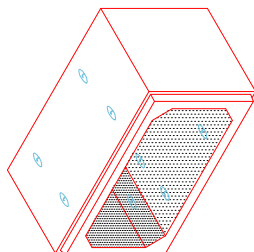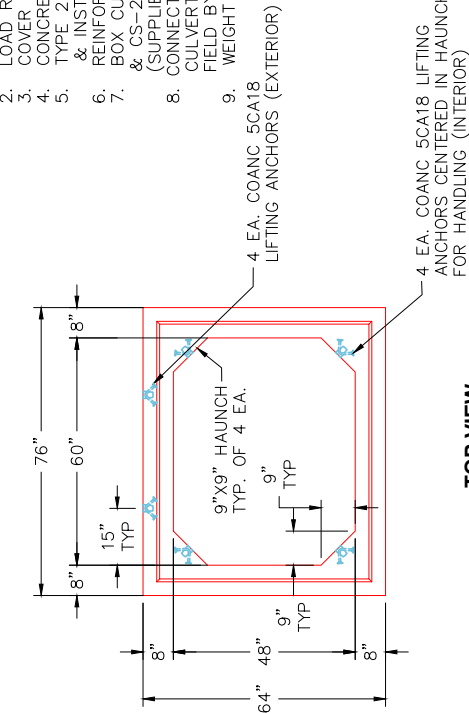

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: Flat

Wall Thickness: 8"
 Floor Height: 0"

Height (Int): 57"
 Height (Ext): 57"

Weight (Net): 10263 lb
 Volume (Net): 2.62cu.yd

Job Name: 26-1508BC - Ferdinand State Park Culverts Replacement
Job Location: Ferdinand, IN
Contractor: WB Koester Construction, LLC

Plant: 100

9/15/2026 1:35:28 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: CV-2 Box Culvert

P8 BC048060-08W08T08F-09H

BOX CULVERT (08W/08F/08T) T/F T/F

INFRASTRUCTURE PRECAST (ICAST)

Project : Ferdinand State Forest Culvert

Task :

Job No. : 26-1508BC

Client: W.B. Koester

File: 5x4 BC Four Sided - 26-1508BC Ferdinand State Forest

Sht _____ of _____

By: J. Horsley

Ck: _____

9/22/2026 10:54:52 AM

Page 1 of 4

Spec.: LRFD 9th ed.
Type of Culvert: Precast

Physical Dimensions

Clear Span: 5'-0"
Clear Height: 4'-0"
Top Slab: 8"
Bottom Slab: 8"
Ext. Wall: 8"
Fill Depth Range
Maximum: 3.99 ft
Minimum: 2.00 ft
Increment: 0.50 ft
Length: 5'-9"
Skew Angle: 0.00 deg
Bottom Slab Support: Full Slab
Top Haunch, Width: 9"
Top Haunch, Height: 9"
Bottom Haunch, Width: 9"
Bottom Haunch, Height: 9"

Material Properties

Concrete
Strength, f'c: 5.000 ksi
Density: 0.150 kcf
Elasticity, Ec: 4592 ksi
Type: Normal wt
Steel
Yield, fy: 60 ksi
Allow Stress: 36 ksi
Elasticity, Es: 29000 ksi
Soil
Density: 0.120 kcf
Exposure Factor
User-Defined: 1.00
Reinforcement Covers
Ext. Cover Top Slab: 2"
Ext. Cover Bottom Slab: 1 1/2"
Ext. Cover Walls: 1 1/2"
Int. Cover Walls: 1 1/2"
Int. Cover Top Slab: 2"
Int. Cover Bottom Slab: 2"



Controlling Ratings

Inventory Rating: 1.64
Operating Rating: 2.13

Loads

Live Load
Vehicle Names: KY HL-93
Traffic Direction: Parallel
Eq. Height of Soil: Calculated
Dead Load
Future Wearing Surface: 0.000 klf
Additional Dead Load: 0.000 klf
Concentrated Loads: none

Interior Water Pressure: no
Exterior Water Pressure: no

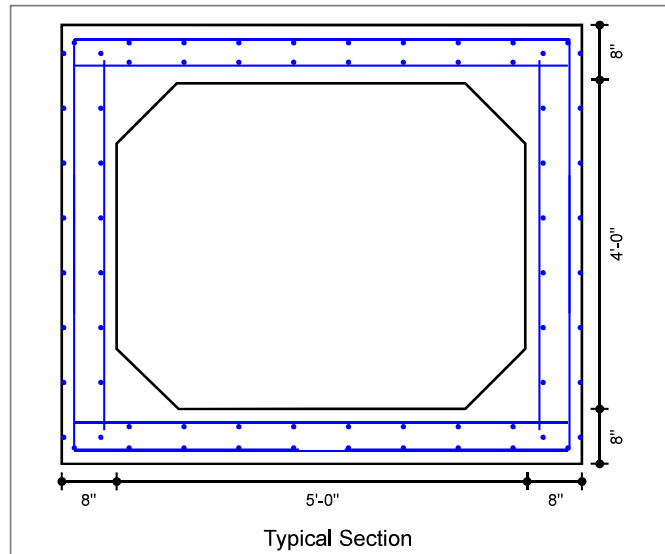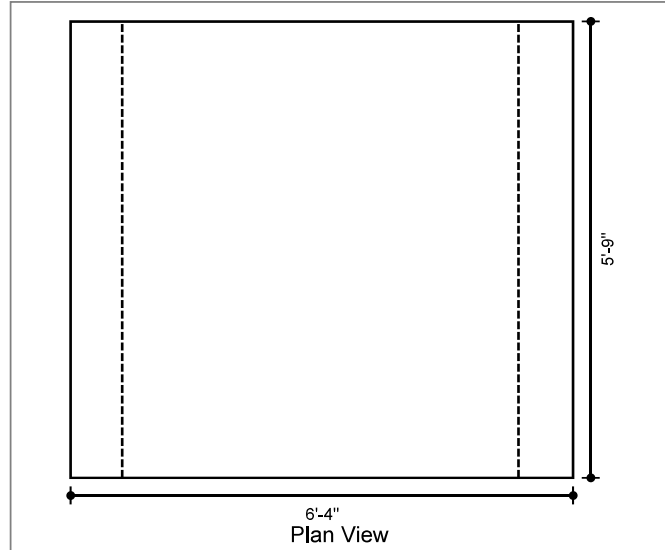

Lateral Soil Loads
Eq. Fluid Press. Max: 60.00 pcf
Eq. Fluid Press. Min: 30.00 pcf

Job Name: 26-1508BC - Ferdinand State Park Culverts Replacement
Job Location: Ferdinand, IN
Contractor: WB Koester Construction, LLC

Plant: 100

9/15/2026 1:35:28 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: CV-2 Box Culvert

P8 BC048060-08W08T08F-09H

BOX CULVERT (08W/08F/08T) T/F T/F

INFRASTRUCTURE PRECAST (ICAST)

Project : Ferdinand State Forest Culvert

Task :

Job No. : 26-1508BC

Client: W.B. Koester

File: 5x4 BC Four Sided - 26-1508BC Ferdinand State Forest



Sht ____ of ____
By: J. Horsley
Ck: _____
9/22/2026 10:54:53 AM
Page 2 of 4

Concrete Summary

Volume of Concrete: 0.552 cy/ft Total Volume of Concrete: 3.174 cy

Reinforcing Steel Bar Schedule (lb)

Location	Mark	Qty	Size	Spacing	Type	Length	Hor. Leg	Ver. Leg	Tot. Weight
Top Slab(Int)	A100 (AS2)	9	5	8"	S	6'-0"	--	--	56.0
Bot Slab(Int)	A200 (AS3)	9	5	8"	S	6'-0"	--	--	56.0
Top Slab(Ext)	A300 (AS7)	9	5	8"	S	6'-0"	--	--	56.0
Bot Slab(Ext)	A400 (AS8)	9	5	8"	S	6'-0"	--	--	56.0
Corner(Top)	A1 (AS1)	18	5	8"	L	6'-5"	3'-1"	3'-4"	120.0
Corner(Bot)	A2 (AS1)	18	5	8"	L	6'-1"	2'-9"	3'-4"	114.0
Wall(Int)	B1 (AS4)	18	5	8"	S	4'-6"	--	--	84.0
Longit. Top (Int)	C100 (AS5)	8	5	8"	S	5'-8"	--	--	47.0
Longit. Bot (Int)	C200	8	5	8"	S	5'-8"	--	--	47.0
Longit. Top (Ext)	C1 (AS6)	10	5	8"	S	5'-8"	--	--	59.2
Longit. Bot (Ext)	C1 (AS6)	10	5	8"	S	5'-8"	--	--	59.2
Longit. Wall (Ext)	C1 (AS6)	16	5	8"	S	5'-8"	--	--	94.7
Longit. Wall (Int)	C1 (AS6)	16	5	8"	S	5'-8"	--	--	94.7
									944

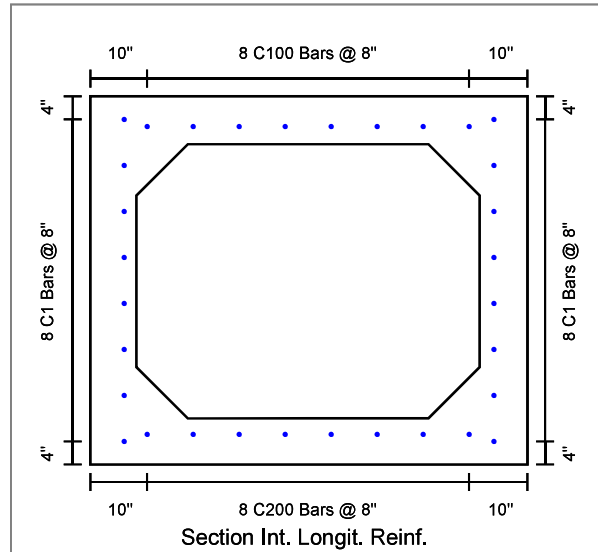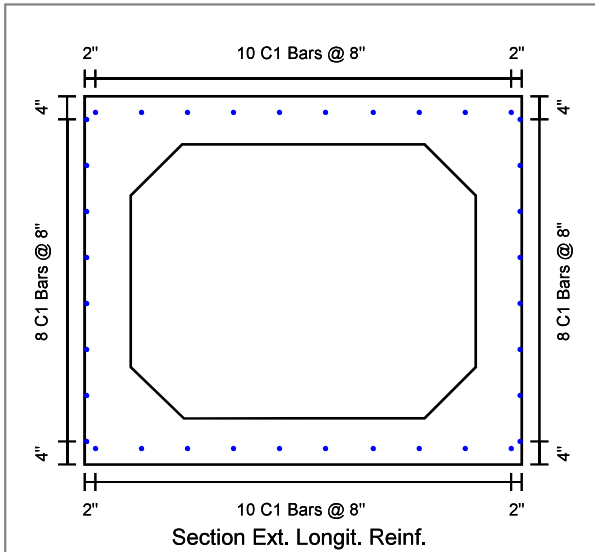

Job Name: 26-1508BC - Ferdinand State Park Culverts Replacement
Job Location: Ferdinand, IN
Contractor: WB Koester Construction, LLC

Plant: 100

9/15/2026 1:35:28 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: CV-2 Box Culvert

P8 BC048060-08W08T08F-09H

BOX CULVERT (08W/08F/08T) T/F T/F

INFRASTRUCTURE PRECAST (ICAST)

Project : Ferdinand State Forest Culvert

Task :

Job No. : 26-1508BC

Client: W.B. Koester

File: 5x4 BC Four Sided - 26-1508BC Ferdinand State Forest


Sht. _____ of _____

By: J. Horsley


Ck: _____

9/22/2026 10:54:53 AM


Page 1 of 4

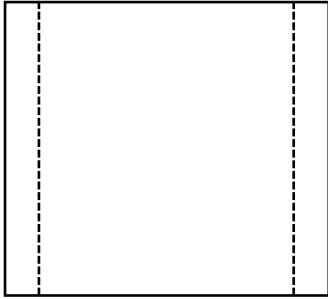


Ext. Wall Reinf.

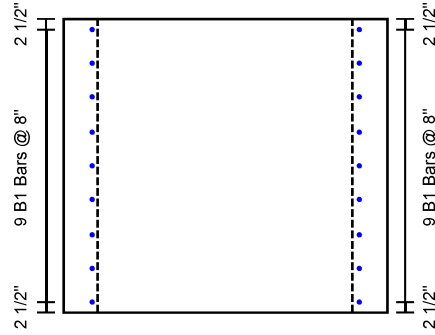


Int. Wall Reinf.

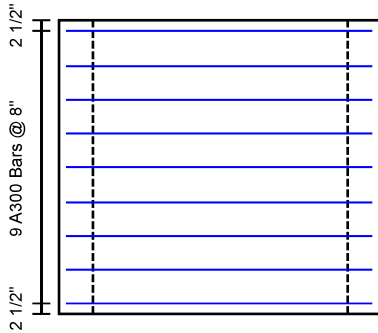


Top Slab Ext. Reinf.

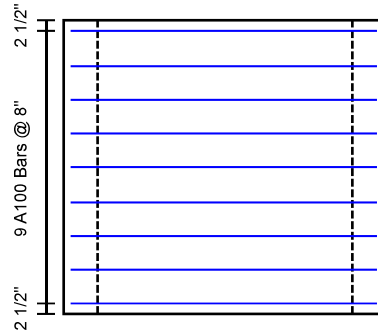

Top Slab Int. Reinf.

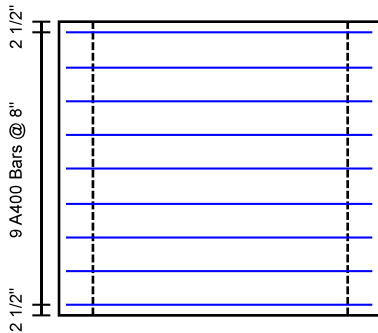

Bottom Slab Ext. Reinf.

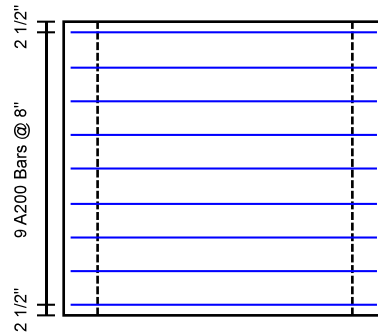

Bottom Slab Int. Reinf.

Job Name: 26-1508BC - Ferdinand State Park Culverts Replacement
Job Location: Ferdinand, IN
Contractor: WB Koester Construction, LLC

Plant: 100

9/15/2026 1:35:28 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: CV-2 Box Culvert

P8 BC048060-08W08T08F-09H

BOX CULVERT (08W/08F/08T) T/F T/F

INFRASTRUCTURE PRECAST (ICAST)

Project : Ferdinand State Forest Culvert

Task :

Job No. : 26-1508BC

Client: W.B. Koester

File: 5x4 BC Four Sided - 26-1508BC Ferdinand State Forest


Sht ____ of ____

By: J. Horsley


Ck: _____

9/22/2026 10:54:53 AM

Page 1 of 4

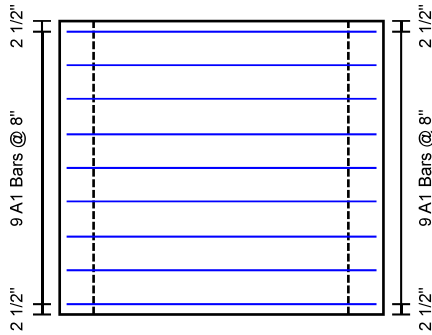

Top Slab Corner Reinf.

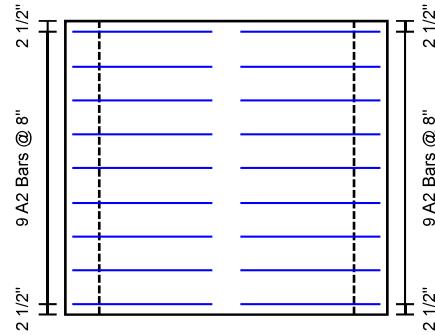

Bottom Slab Corner Reinf.
