

Job Name: 26-1545 - KYTC Boone Co. Camp Ernst Roundabout (ID 3002312)
Job Location: Burlington, KY
Contractor: Lawrence Construction & Leasing, Inc.

Plant: 100

5/13/2026 2:22:13 PM

Tech: J.Horsley

PC: J. Jarvis



Structure ID: D5-8 MHA

P2 MH048LD12ECC

MH FLAT LID w/24in ECC Hole F/G


- P4) 24" - CASTING HEIGHT - 8"
P3) 24" - GRADE RING F/F - 3"
P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12"
P1) 48" - MH BASE T/n - 36"
1) CASTING - HOE KY-510 F/C (KY TY.2)
1) 48" - Conseal CS-102 1.00"
2) Hole - 20
3) MH Step ML-10-TDS-NCR - 10"

0 lb
202 lb
1561 lb
3575 lb
510 lb
0 lb
0 lb
0 lb


Structure Total: 5848 lb

Structure Notes: **KYTC STATE PROJECT**

1. PER KYTC MH A / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60.)

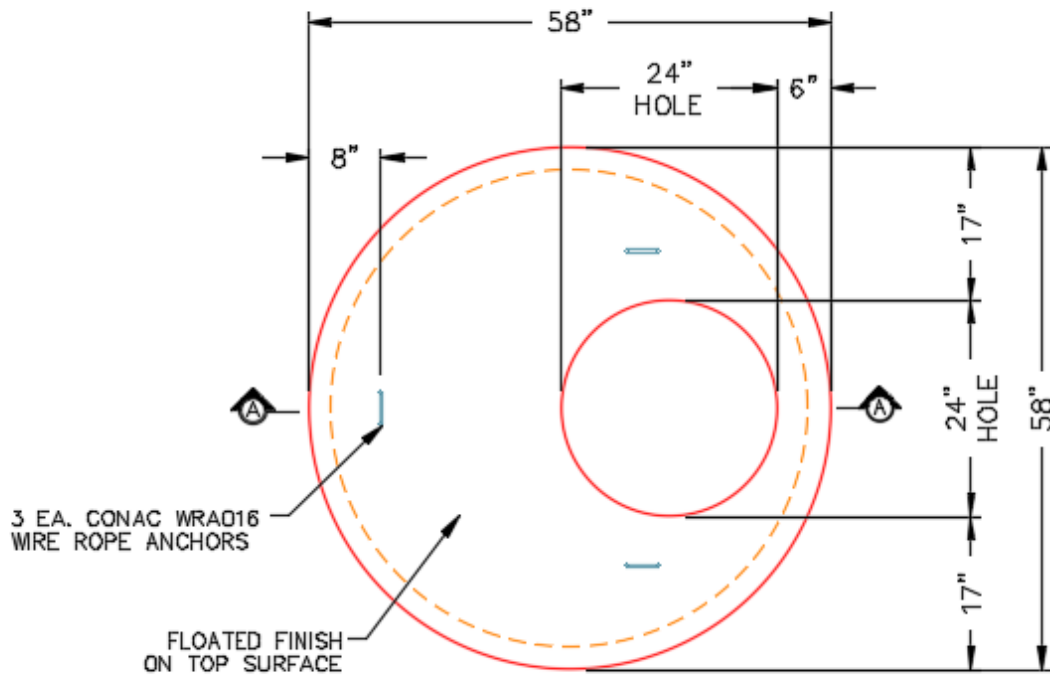

PLAN VIEW

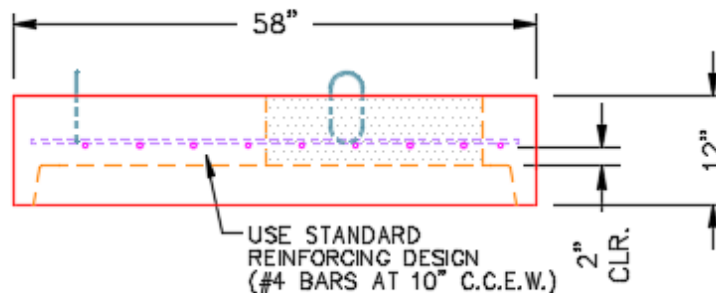

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.4cu.yd
