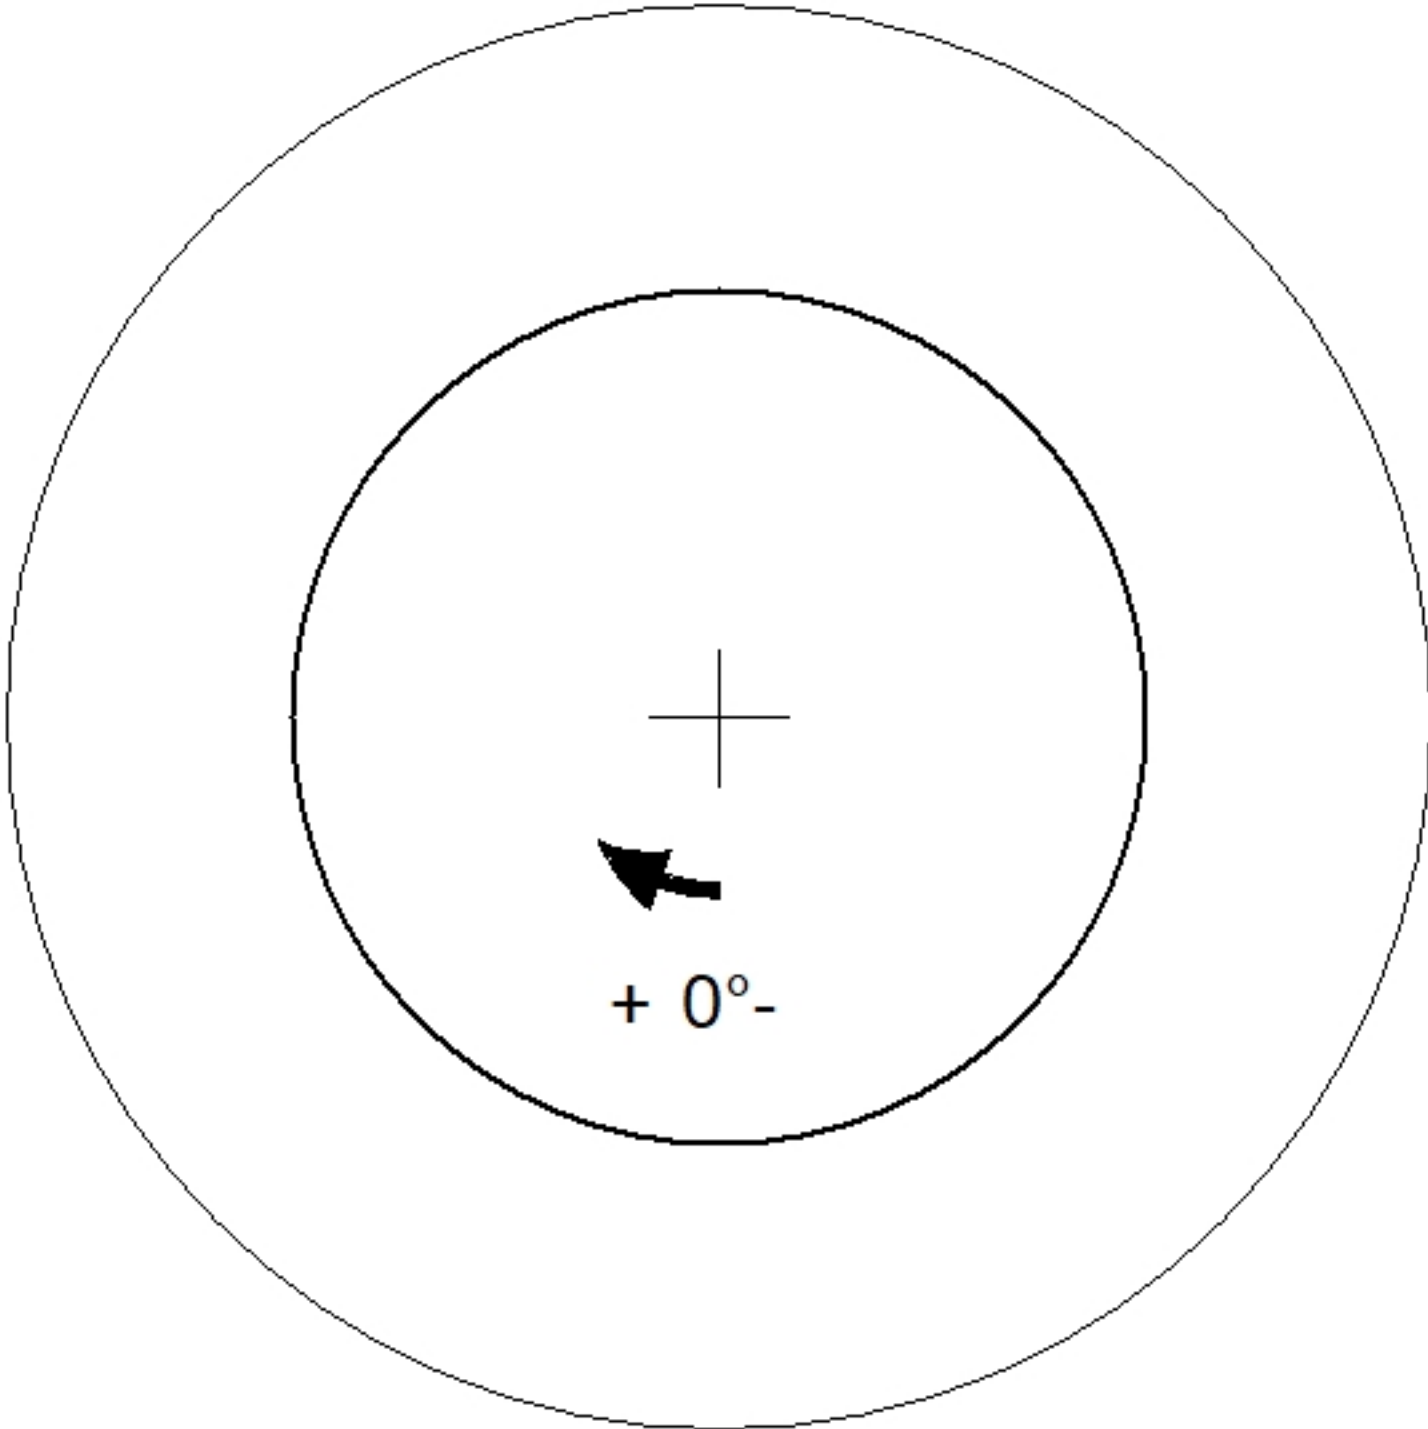


Job Name: 26-1545 - KYTC Boone Co. Camp Ernst Roundabout (ID 3002312)		Plant: 100	Tech: J.Horsley	
Job Location: Burlington, KY Contractor: Lawrence Construction & Leasing, Inc.		5/13/2026 2:22:13 PM	PC: J. Jarvis	
Structure ID: D5-8 MHA				
P3 GR3		GRADE RING F/F		
P4) 24" - CASTING HEIGHT - 8" P3) 24" - GRADE RING F/F - 3" P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12" P1) 48" - MH BASE T/n - 36" 1) CASTING - HOE KY-510 F/C (KY TY.2) 1) 48" - Conseal CS-102 1.00" 2) Hole - 20 3) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 1561 lb 3575 lb 510 lb 0 lb 0 lb 0 lb ----- Structure Total: 5848 lb	Structure Notes: **KYTC STATE PROJECT** 1. PER KYTC MH A / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60.)	
				
24" - GRADE RING F/F - 3" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 3"	Weight (Net): 202 lb Volume (Net): 0.05cu.yd
