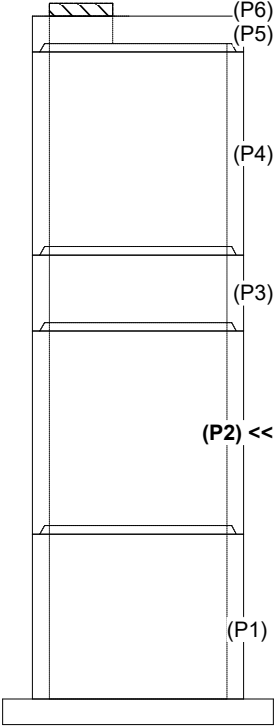





Job Name: 26-1549 Cowan St. Trunk Sewer Job Location: Nashville, TN Contractor: Garney Companies, Inc.					Plant: 100 8/24/2026 11:21:22 AM		Tech: Jared - A PC: Jay Ross Jarvis						
Structure ID: MH-8-11 SS-MH													
P2 MH084RS96X			MH RISER w/XYPEX										
P6) 30" - CASTING HEIGHT - 6" P5) 84" - MH FLAT TOP w/2X 30" Holes ECC w/XYPEX - 17" P4) 84" - MH RISER w/XYPEX - 96" P3) 84" - MH RISER w/XYPEX - 36" P2) 84" - MH RISER w/XYPEX - 96" P1) 84" - MH BASE w/FLANGE (12F/14EF) w/XYPEX - 78" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE XYPEX C-1000 RED 1) SECONDARY POUR - EXT. FLANGE 2) CASTING - JBS 1312 WT F/C SANITARY 4) 84" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1840						0 lb 6992 lb 18626 lb 6985 lb 18626 lb 24093 lb 0 lb 0 lb 0 lb 0 lb 600 lb 0 lb 2 lb ----- 75924 lb		Structure Notes: . PLAN LABEL: MH-8 1. JBS 1312 WT F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = XYPEX C-1000 RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .24) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W. 6. ANY REQUIRED INTERIOR COATINGS TO BE SUPPLIED & APPLIED BY OTHERS. 7. **NO STEPS**					
Rim: 412.61' Rim to Invert: 27.25' Slack: 0.5" Sump: 2.5" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 96" Height (Ext): 96"		Weight (Net): 18626 lb Volume (Net): 4.76cu.yd			
