


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/23/2026 3:01:04 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 37887-149 MHC											
P4 MH048RS72		MH RISER T/G									
P8) 24" - CASTING HEIGHT - 4" P7) 24" - GRADE RING F/F - 4" P6) 48" - ECC CONE w/ 24" HOLE F/G - 42" P5) 48" - MH RISER T/G - 72" P4) 48" - MH RISER T/G - 72" P3) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 12" P2) 48" x 48" - BOX RISER 8inW F/G - 36" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF T/n - 48" 2) 48" x 48" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 40 1) Hole - 18 24) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 3200 lb 5030 lb 5030 lb 2302 lb 5216 lb 11975 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE KY-206 F/C (KY TY1)). 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE(8"WD x 12" THICK). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As.12) - RISER/WALLS (As.12) - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..				
Rim: 764.77' Rim to Invert: 24.32' Slack: 1.84" Sump: 0" Step Position: 90°					Structure Total: 33023 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

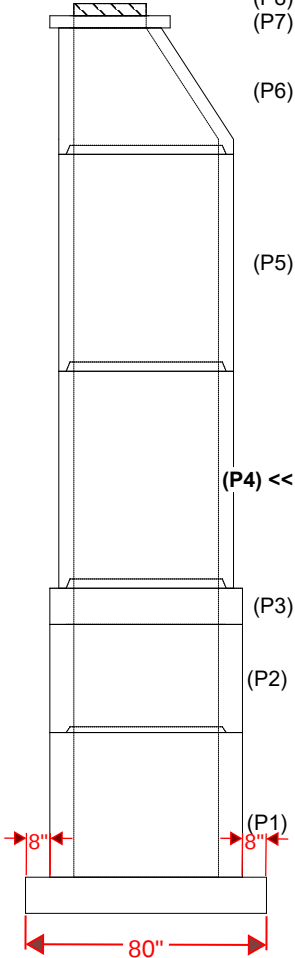

(P8)
(P7)

(P6)

(P5)


(P4) <<

(P3)
(P2)

(P1)

80"
8" 8"

RIGHT-SIDE UP VIEW (int. dimensions)

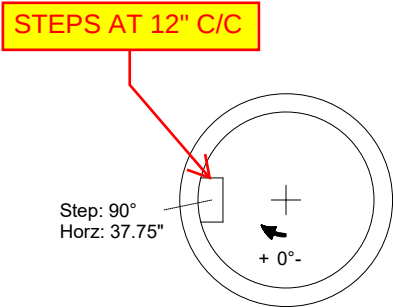


STEPS AT 12" C/C

Step: 90°
Horz: 37.75"

+ 0°-

INSIDE WALL DIMENSIONS

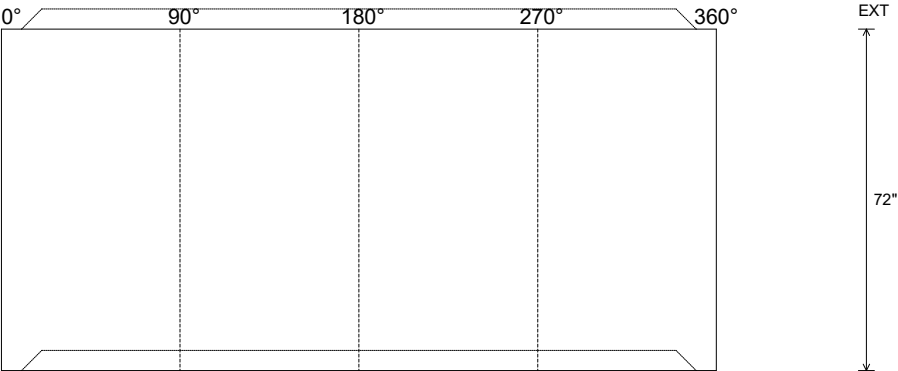

(P4)

EXT 72"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 5030 lb Volume (Net): 1.28cu.yd
----------------------------------	------------------------------------	--	--	--
