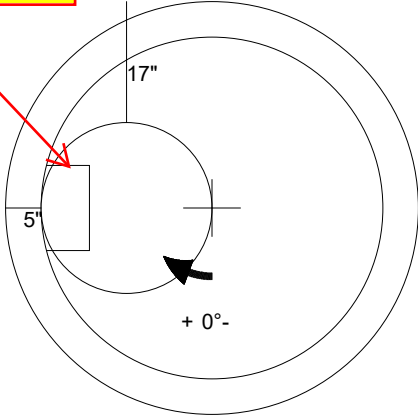



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.		Plant: 100 7/23/2026 3:00:51 PM	Tech: Jared - F PC: T. Ryan		
Structure ID: 37887-149 MHC					
P6 MH048CN42		ECC CONE w/ 24" HOLE F/G			
P8) 24" - CASTING HEIGHT - 4" P7) 24" - GRADE RING F/F - 4" P6) 48" - ECC CONE w/ 24" HOLE F/G - 42" P5) 48" - MH RISER T/G - 72" P4) 48" - MH RISER T/G - 72" P3) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 12" P2) 48" x 48" - BOX RISER 8inW F/G - 36" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF T/n - 48" 2) 48" x 48" - Conseal CS-102 1.00" 3) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 40 1) Hole - 18 24) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 3200 lb 5030 lb 5030 lb 2302 lb 5216 lb 11975 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 33023 lb		Structure Notes: ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE KY-206 F/C (KY TY1)). 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE(8"WD x 12" THICK). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As.12) - RISER/WALLS (As.12) - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..	
STEPS AT 12" C/C 					
 48" - ECC CONE w/ 24" HOLE F/G - 42" - (P6)					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
