

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Peewee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

Tech: Jared - F

7/24/2026 2:10:33 PM

PC: T. Ryan



Structure ID: 14150-18 CBIA-3

P2 BX036048-08TS024036

CB FT REDUCER 24"X36" HOLE T/F

P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10"
P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18"
P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE T/F - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 44"
1) CASTING - HOE KY-206 F/C (KY CBI A)
1) 36" x 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 28
1) Hole - 22
1) Hole - 6
1) Hole - 18

3398 lb
5270 lb
1654 lb
7038 lb
206 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 17566 lb


Structure Notes:

**** KYTC STATE PROJECT ****


1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT)
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

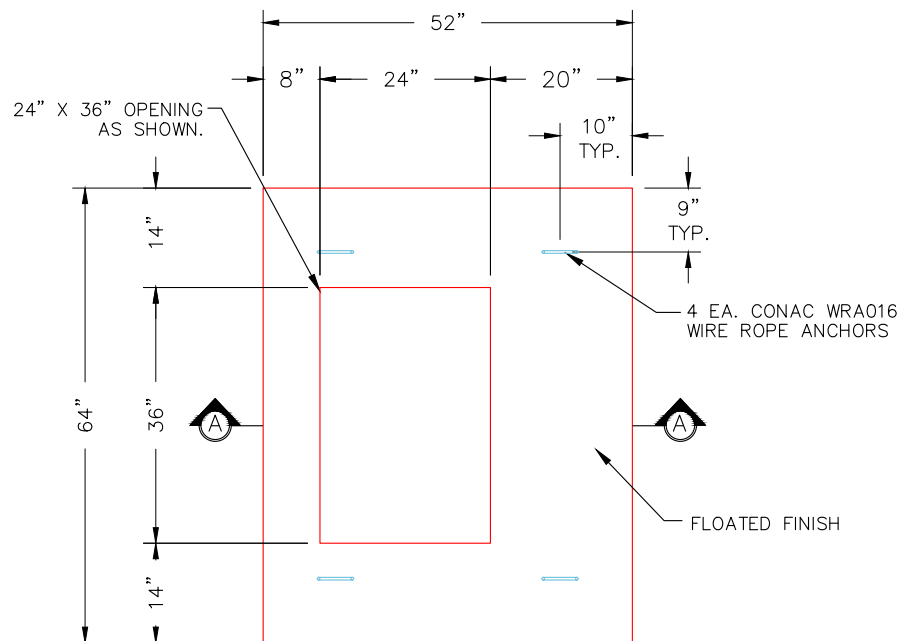

PLAN VIEW

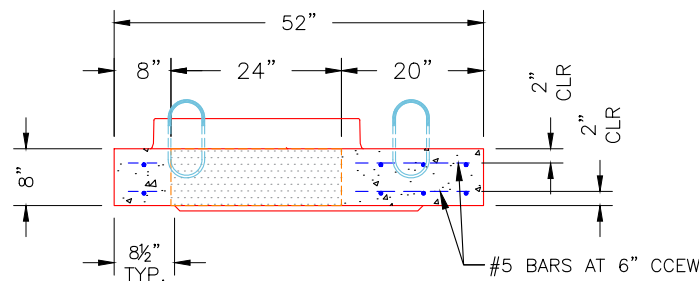

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (DOUBLE MAT) (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1654 lb
Volume (Net): 0.42cu.yd
