


Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.				Plant: 100 7/24/2026 2:03:53 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: 14675-25 CBIA-23										
P1 BX2436-08BVF				BOX BASE 8inW, 8inF, Variable Ht T/n						
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 29" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18 1) Hole - 6				3400 lb 5270 lb 4166 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 13041 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 785.24' Rim to Invert: 5.02' Slack: 3.24" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	780.22'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2	781.89'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	19"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

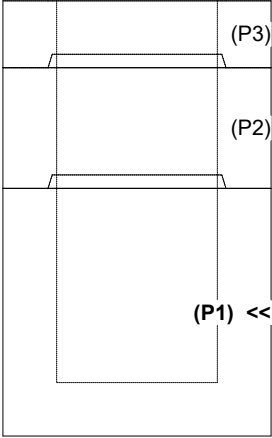


(P3)

(P2)

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

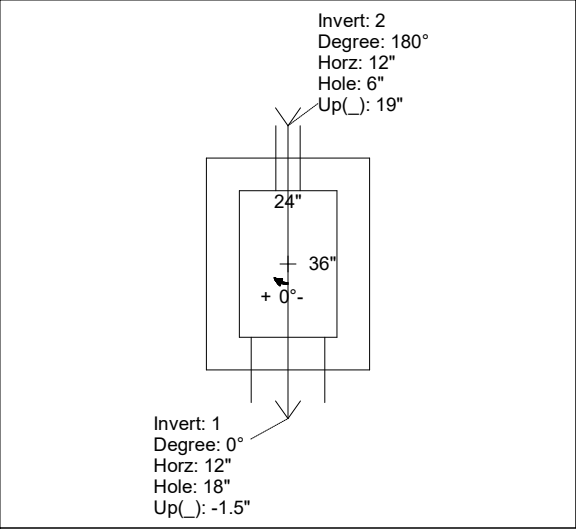

Invert: 2
Degree: 180°
Horz: 12"
Hole: 6"
Up(_): 19"

Invert: 1
Degree: 0°
Horz: 12"
Hole: 18"
Up(_): -1.5"


UPSIDE-DOWN VIEW (int. dimensions)

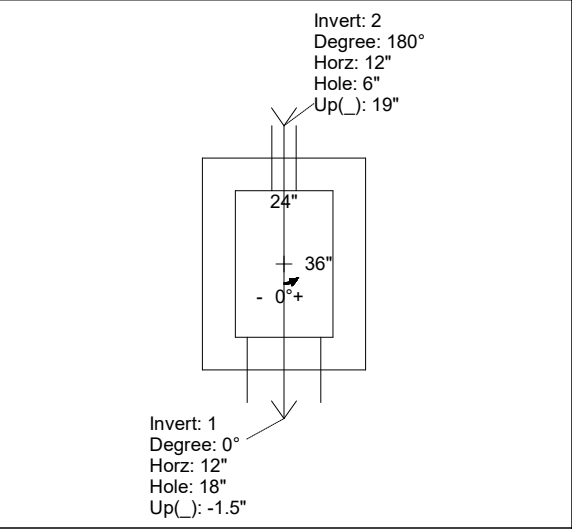

Invert: 2
Degree: 180°
Horz: 12"
Hole: 6"
Up(_): 19"

Invert: 1
Degree: 0°
Horz: 12"
Hole: 18"
Up(_): -1.5"

INSIDE WALL DIMENSIONS

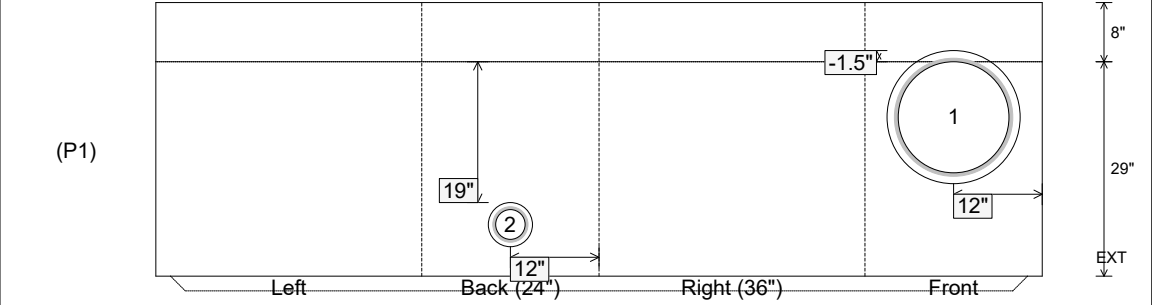

(P1)

Left Back (24") Right (36") Front

19" 12" 12" 12"

8" 29"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 29" Height (Ext): 37"	Weight (Net): 4166 lb Volume (Net): 1.06cu.yd
----------------------------------	---------------------------------	--	--	--
