

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Structure ID: **15510-105 DBI3 - 9A**

Spec: KYTC

Type: DBI TYPE 3

Size: 36" x 36"

Rim: 787.58'

Invert: 784.58'

Rim to Invert: 3'

Sump: 0"

Floor (Top): 784.58'

Floor Height: 8"

Floor (Bot): 783.913'

Overall Height: 3.667'

Slack: 0"

Structure Notes:

****KYTC STATE PROJECT****

1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C).
4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"

P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 28"

1) 36" x 36" - Conseal CS-102 1.00"

1) Hole - 22


0 lb

4868 lb

0 lb

0 lb



Structure Total: 4868 lb

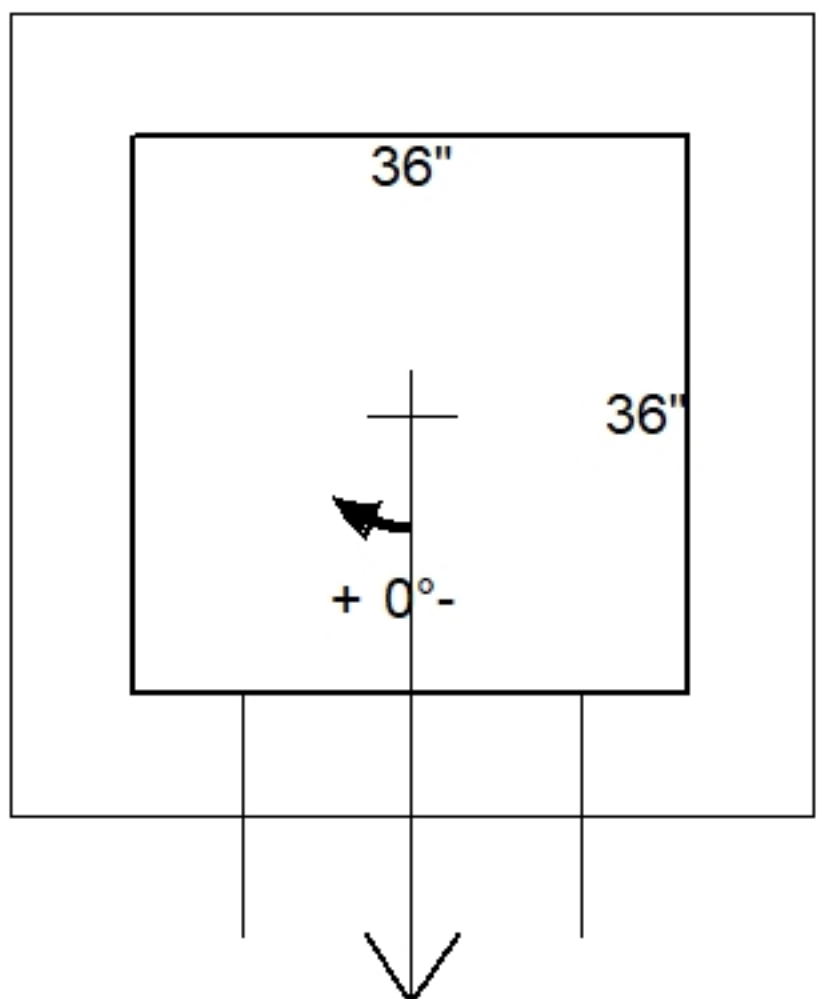

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	787.58'							
Reducer								
Invert 1	784.58'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

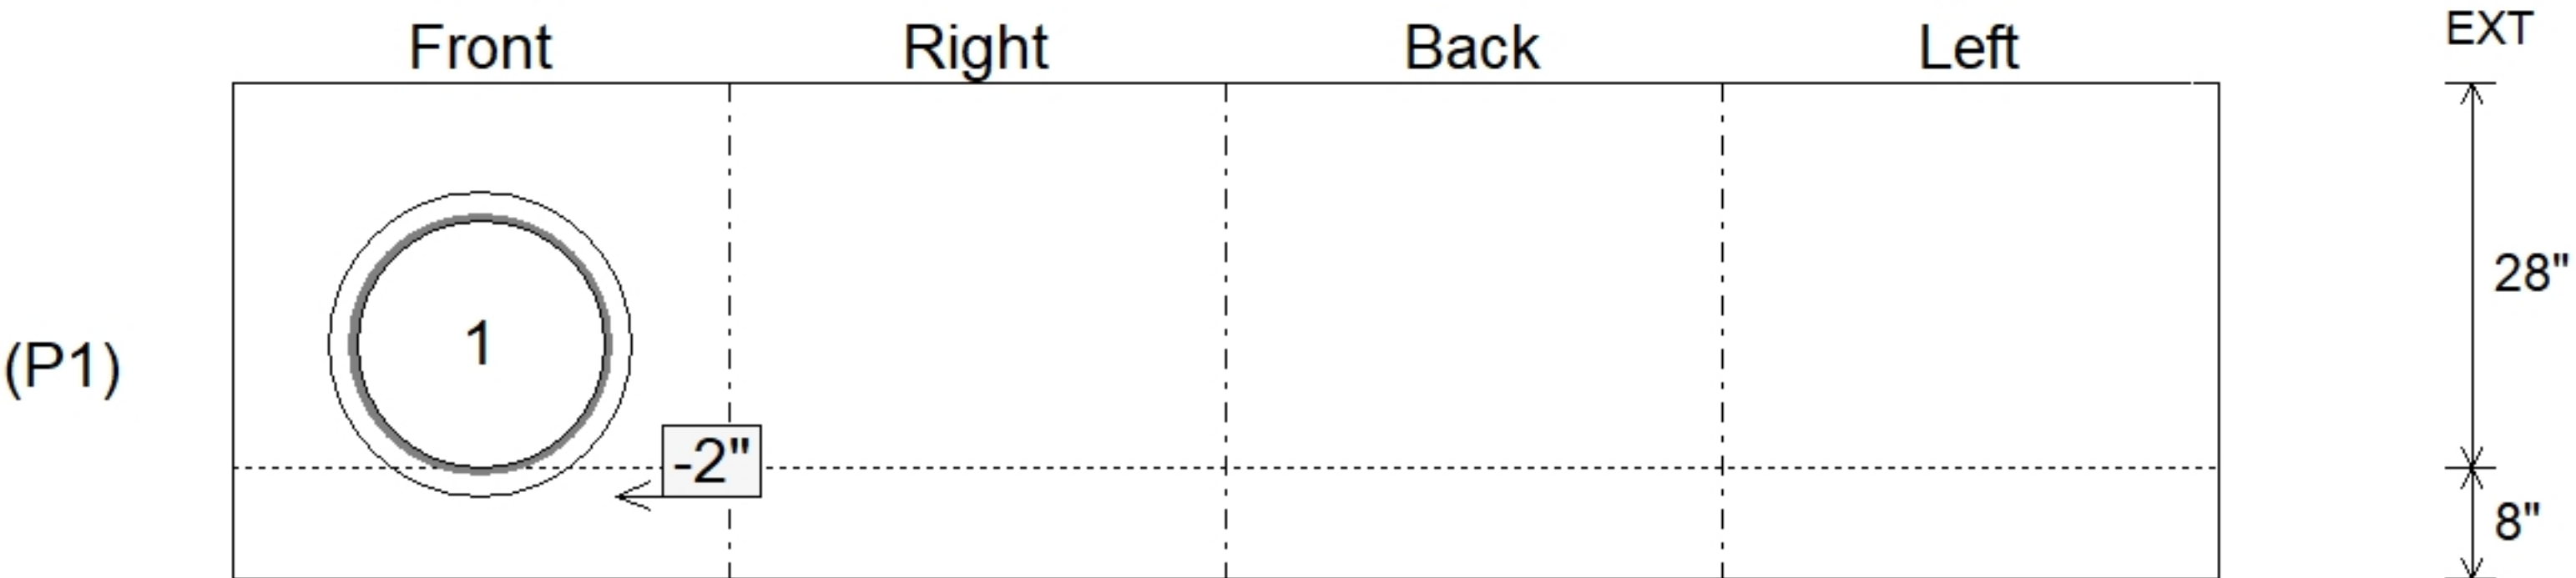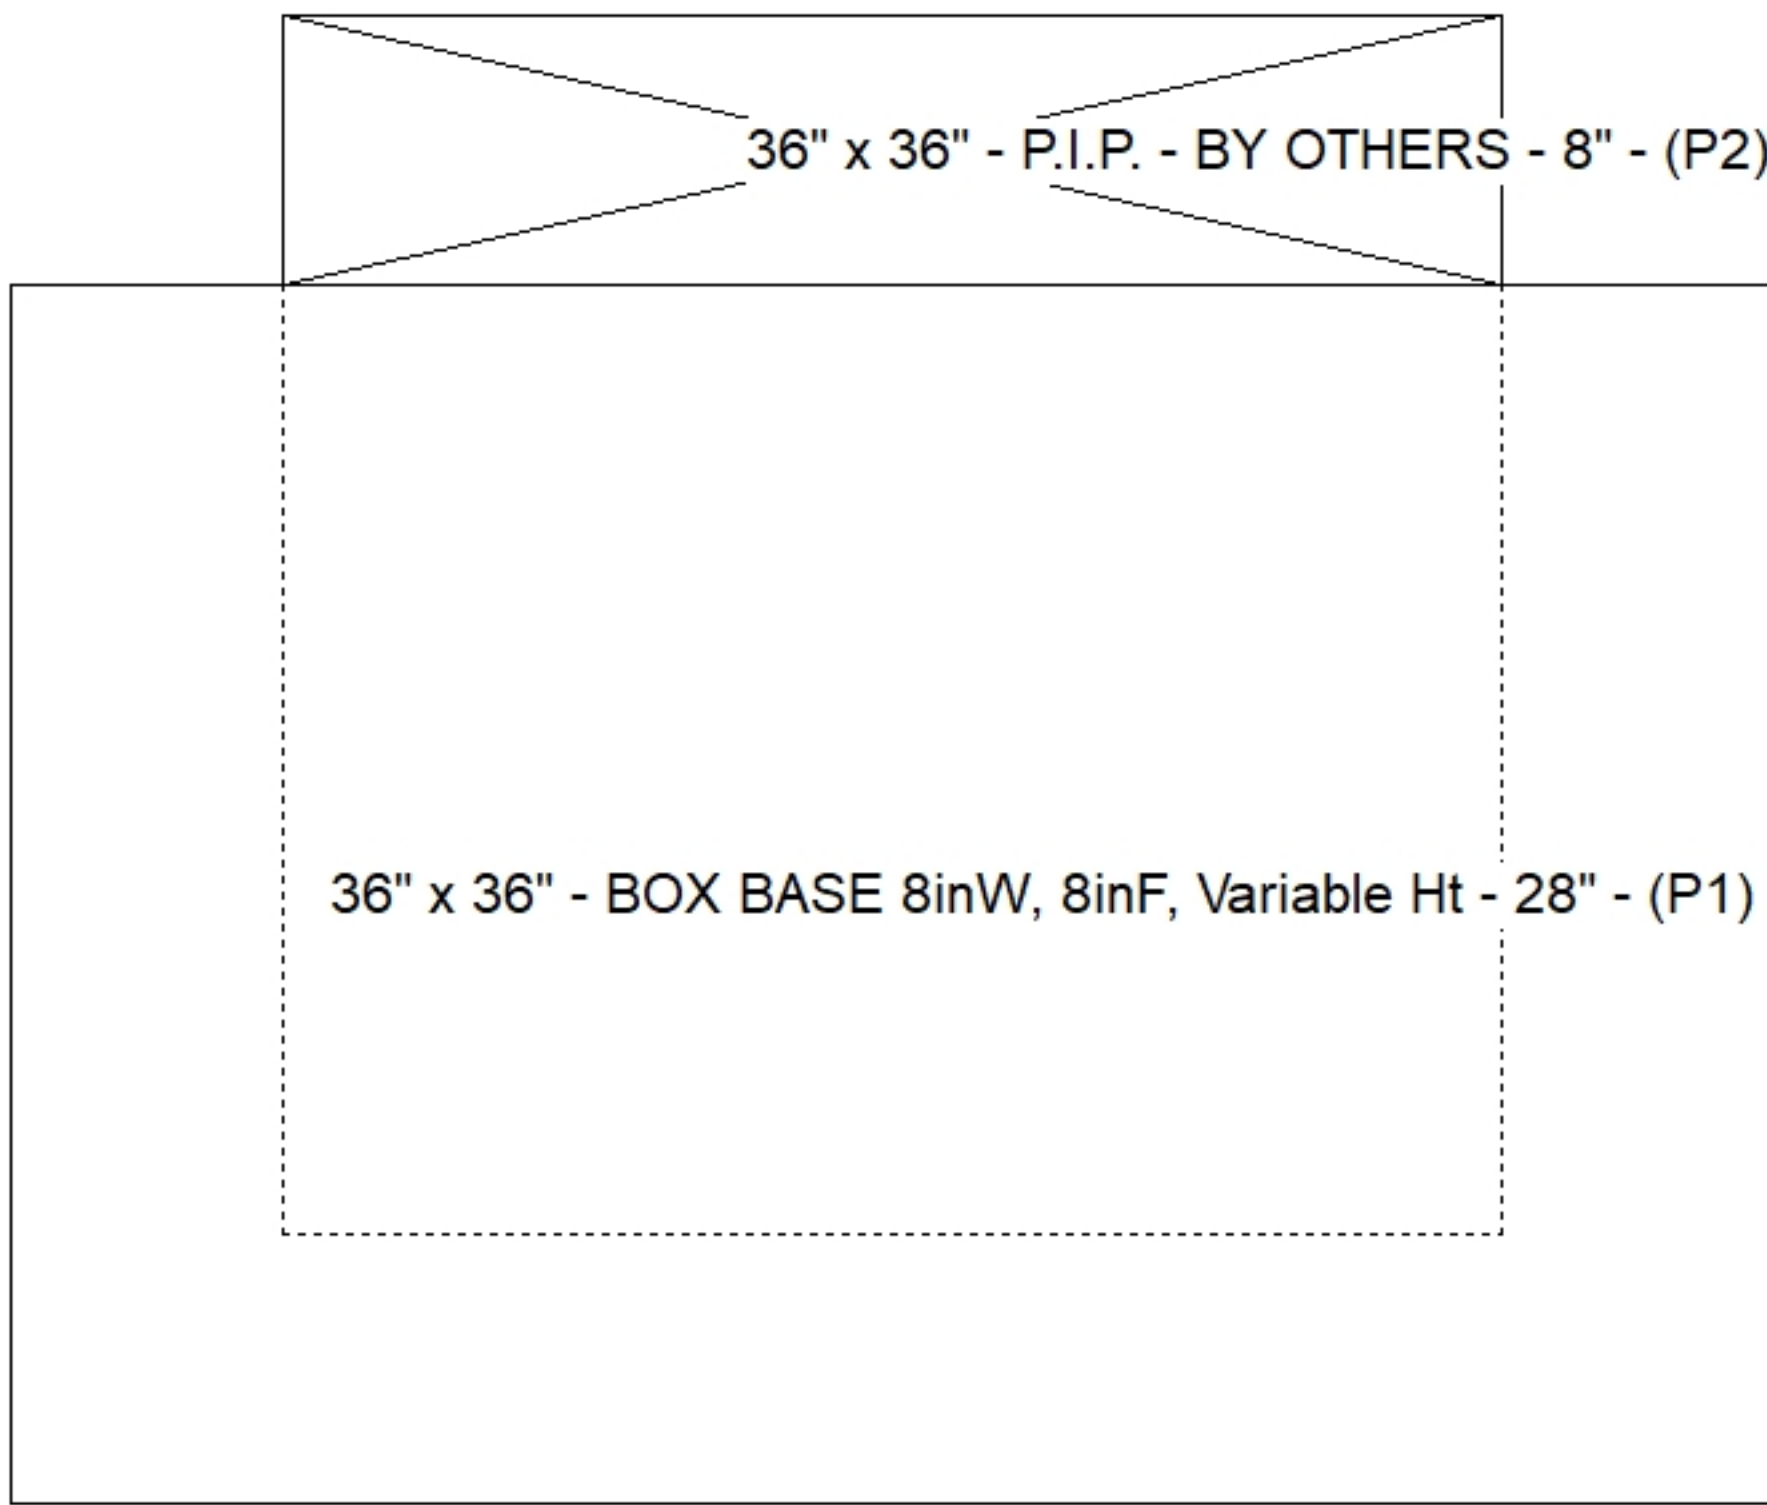

Submittal Drawing
7/29/2026 12:08:51 PM

SUBMITTAL
APPROVED BY:
