
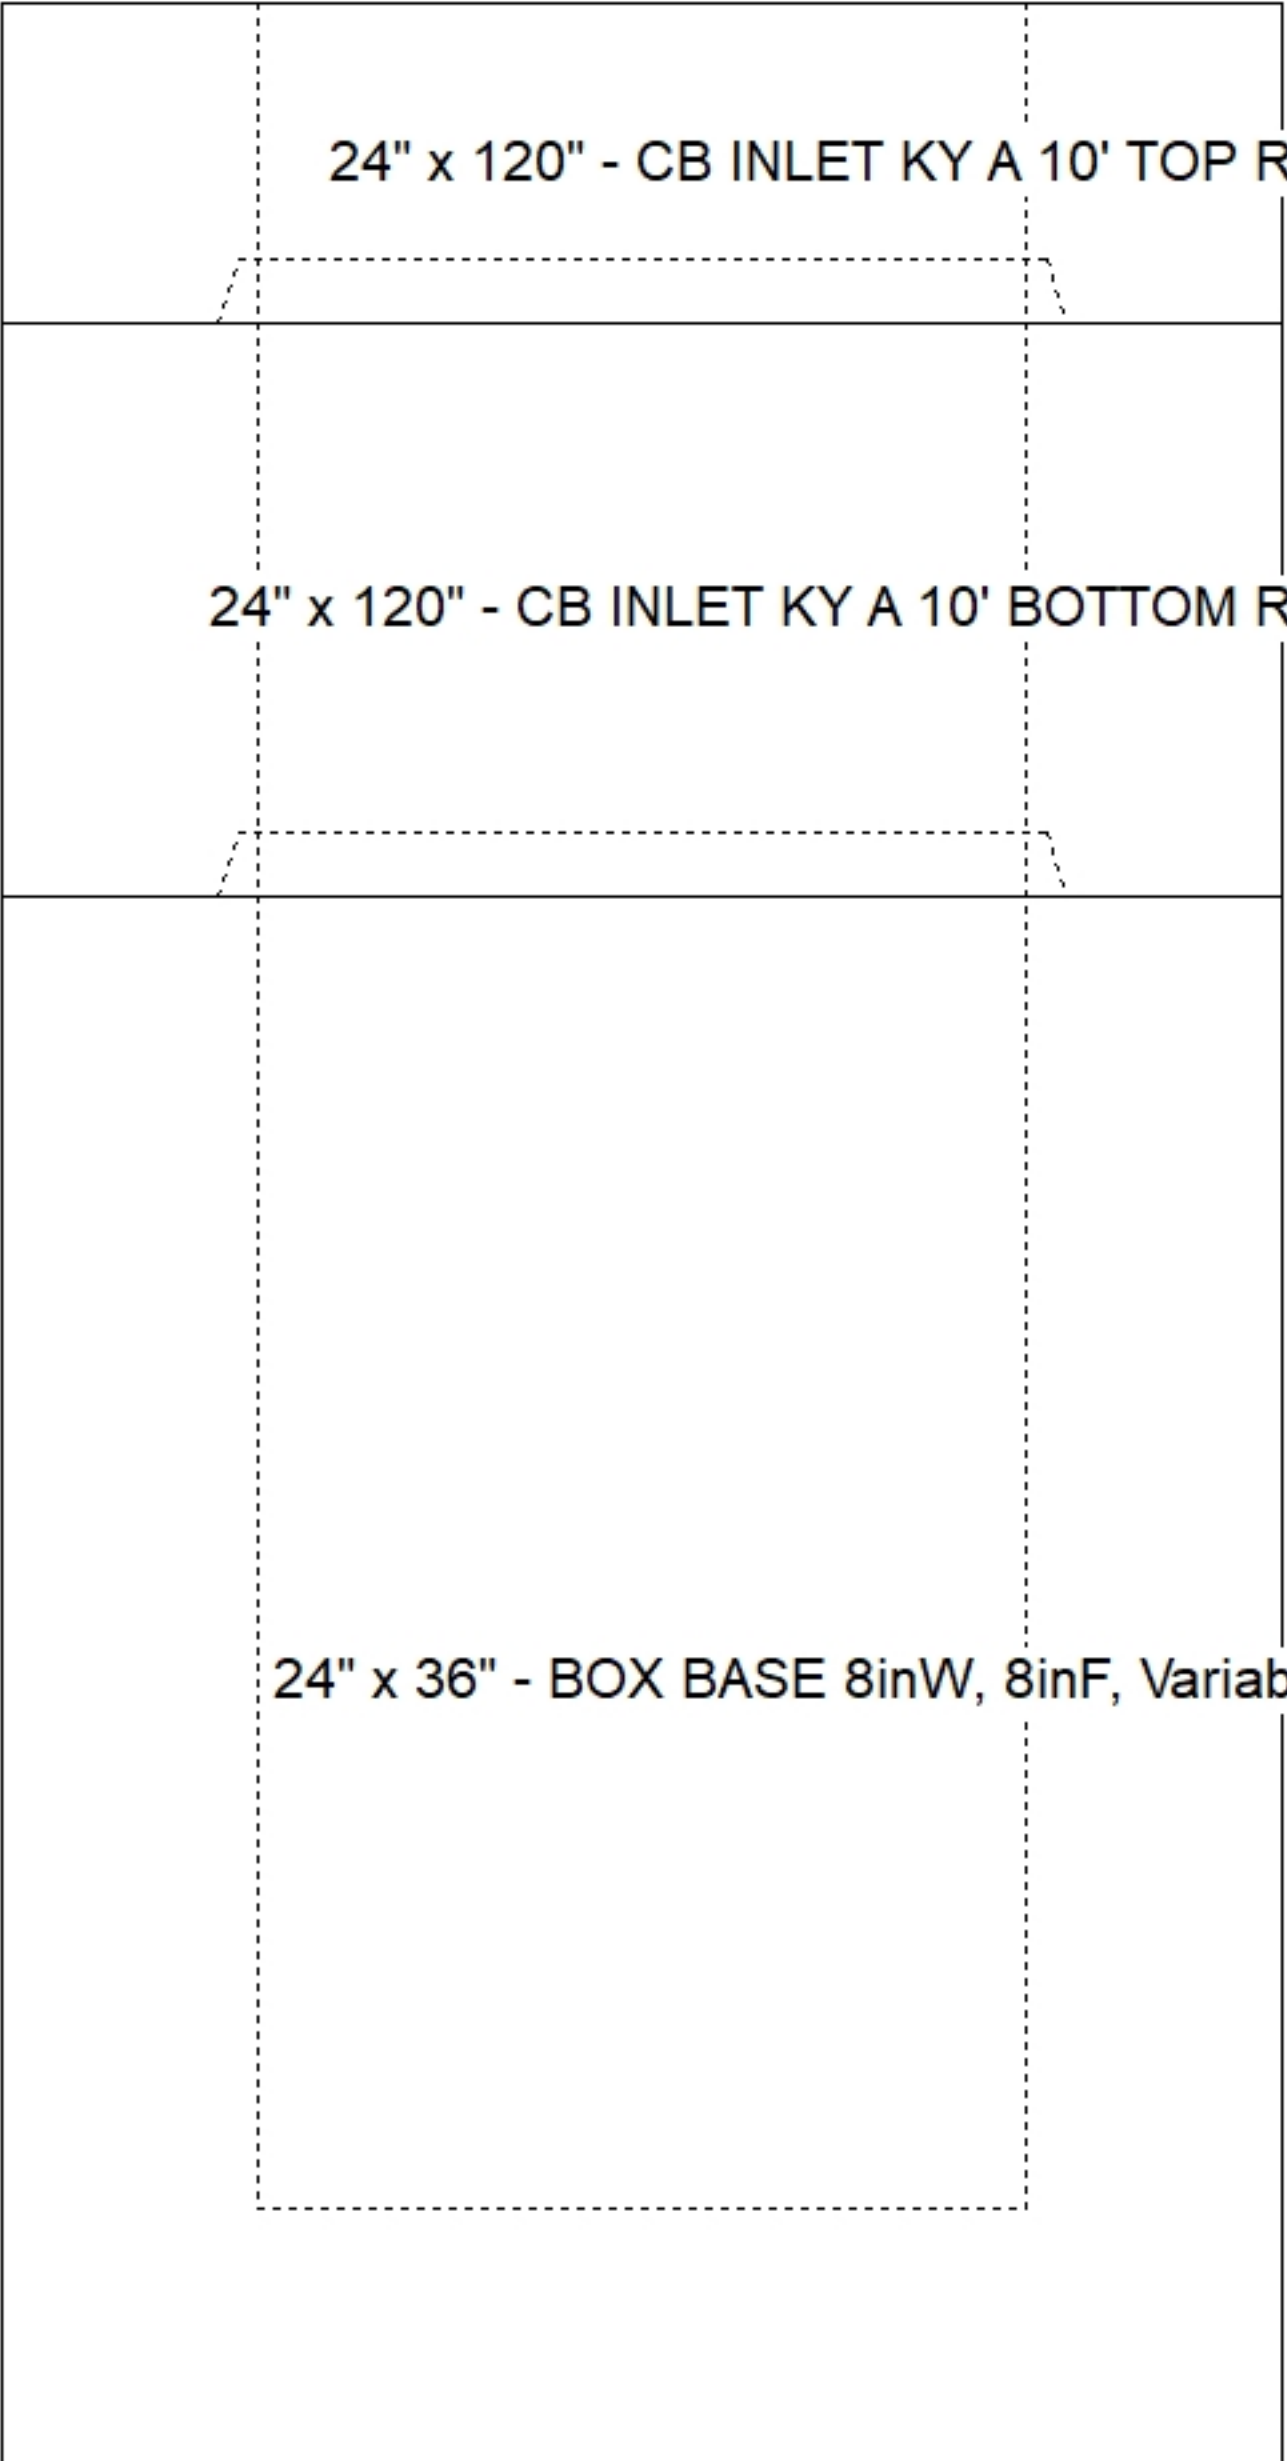
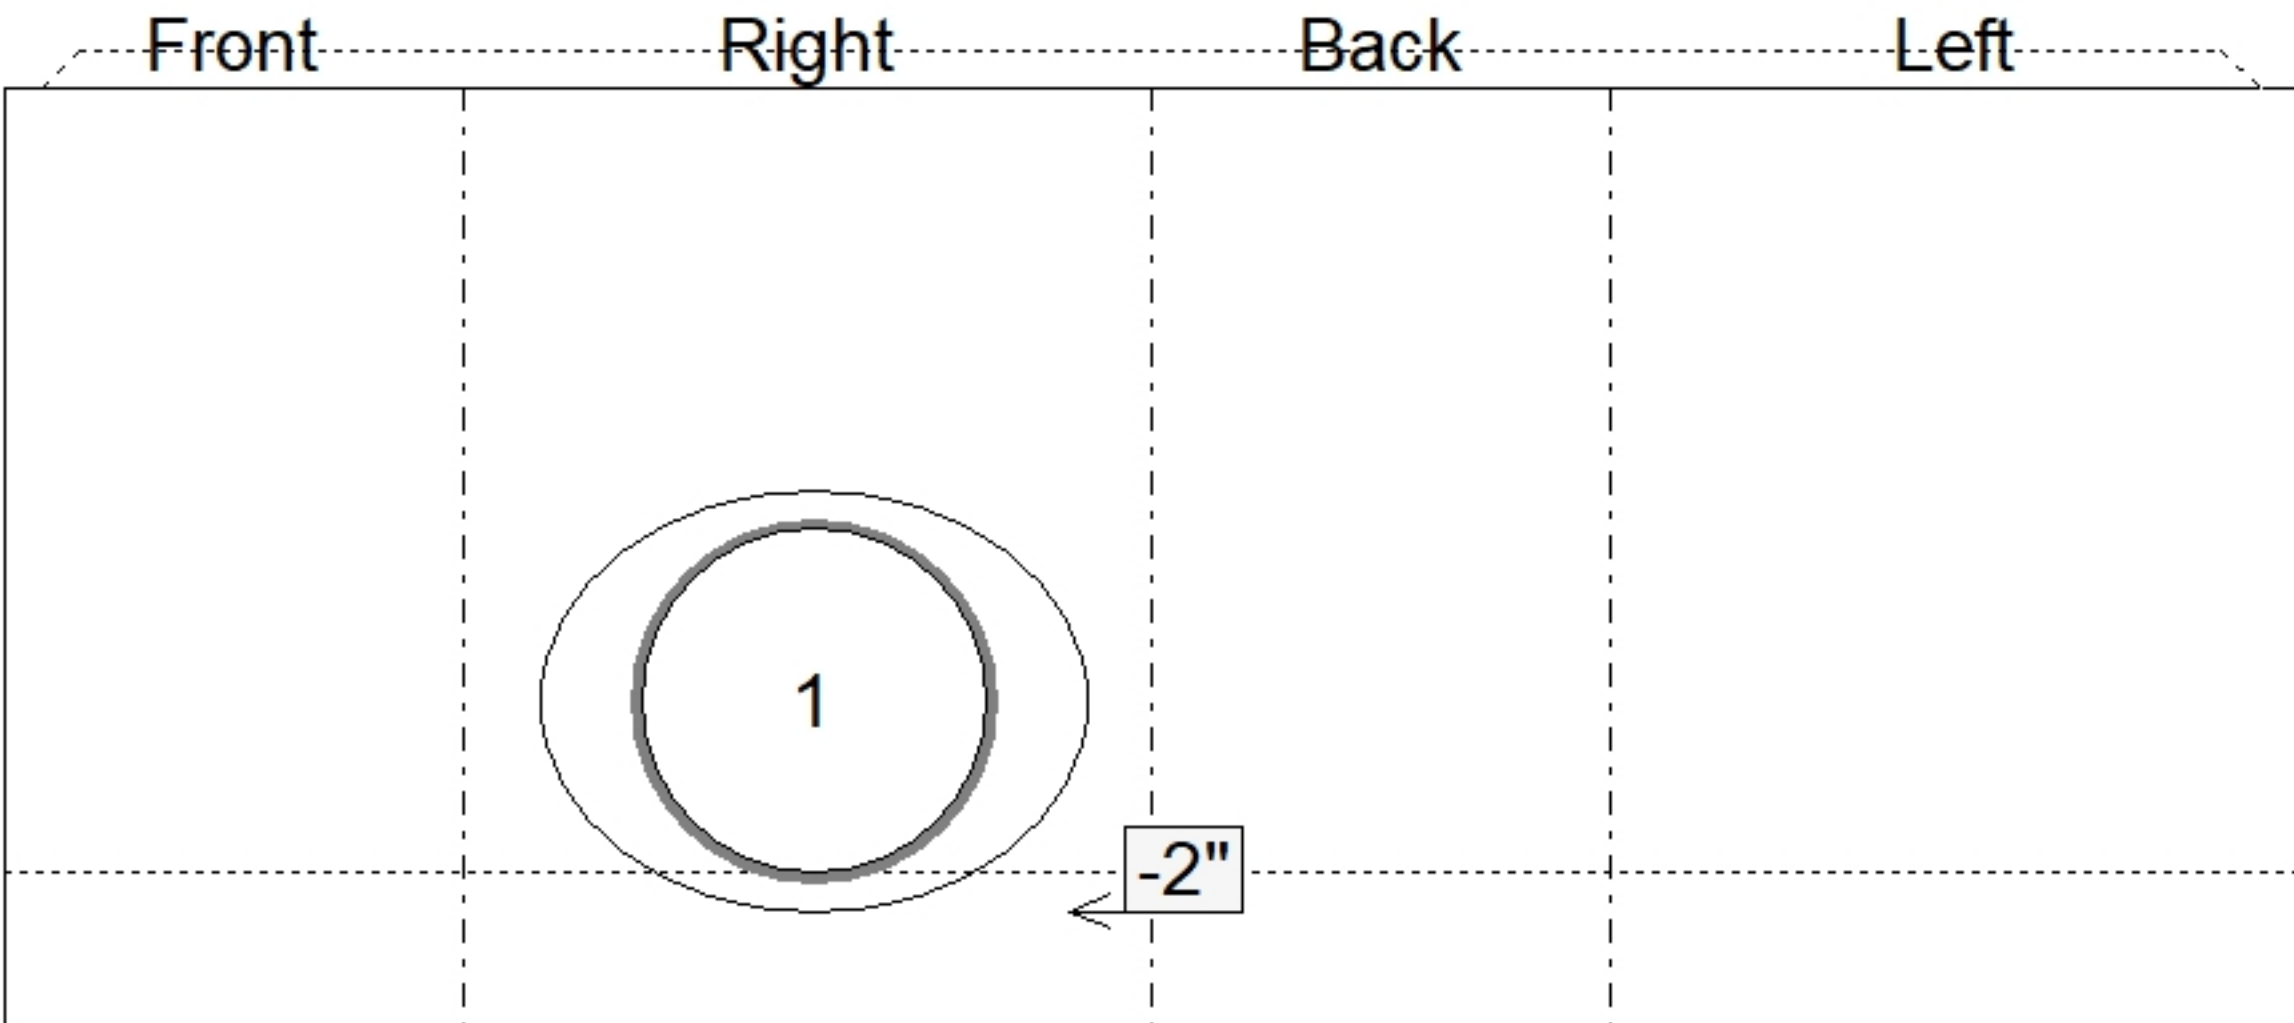


Job Name: 26-1635 - KYTC Oldham Co (261505) - P3 Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.				PC: T. Ryan TECH: Jared - F Plant: 100																																																																																																										
Structure ID: 35531-58 CBIA Spec: KYTC Type: CBI TYPE A (10') Size: 24" x 36"				Rim: 791.32' Invert: 785.25' Rim to Invert: 6.07'		Sump: 0" Floor (Top): 785.25' Floor Height: 8"		Floor (Bot): 784.583' Overall Height: 6.417' Slack: 3.84"																																																																																																						
Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). . REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				STRUCTURE SUMMARY: P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"3398 lb P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"5270 lb P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 41"5247 lb 1) CASTING - HOE KY-206 F/C (KY CBI A)206 lb 1) 24" x 36" - Conseal CS-102 1.00"0 lb 1) Hole - 220 lb Structure Total: 14120 lb																																																																																																										
 Invert: 1 Degree: 50°				<table><tr><th>Position</th><th>Elev</th><th>Angle</th><th>Pipe</th><th>Pipe OD</th><th>Hole</th><th>Connector</th><th>Up ()</th><th>Ref</th></tr><tr><td>Rim</td><td>791.32'</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Reducer</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 1</td><td>785.25'</td><td>50°</td><td>18" CMP</td><td>19"</td><td>22"</td><td>Hole 22</td><td>-2"</td><td>P1</td></tr><tr><td>Invert 2</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 3</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 4</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 5</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 6</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 7</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 8</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr></table>								Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref	Rim	791.32'								Reducer									Invert 1	785.25'	50°	18" CMP	19"	22"	Hole 22	-2"	P1	Invert 2									Invert 3									Invert 4									Invert 5									Invert 6									Invert 7									Invert 8								
Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref																																																																																																						
Rim	791.32'																																																																																																													
Reducer																																																																																																														
Invert 1	785.25'	50°	18" CMP	19"	22"	Hole 22	-2"	P1																																																																																																						
Invert 2																																																																																																														
Invert 3																																																																																																														
Invert 4																																																																																																														
Invert 5																																																																																																														
Invert 6																																																																																																														
Invert 7																																																																																																														
Invert 8																																																																																																														
				Default - Interior Dimensions  Submittal Drawing 7/29/2026 12:08:29 PM SUBMITTAL APPROVED BY:																																																																																																										
