

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100




Slack: 3.84"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

14100 Hz

Structure Total: 14198 lb

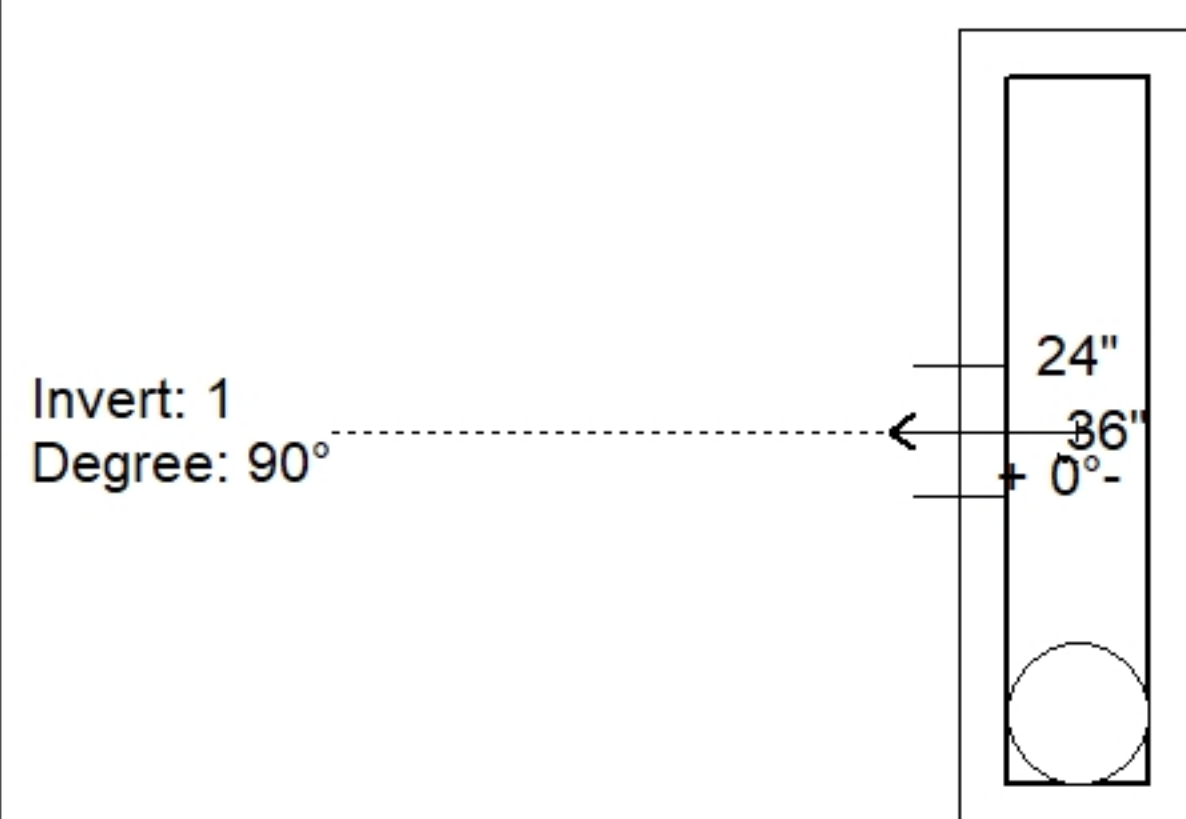


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	794.09'							
Reducer								
Invert 1	788.02'	90°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 41" - (P1)

Default - Interior Dimensions

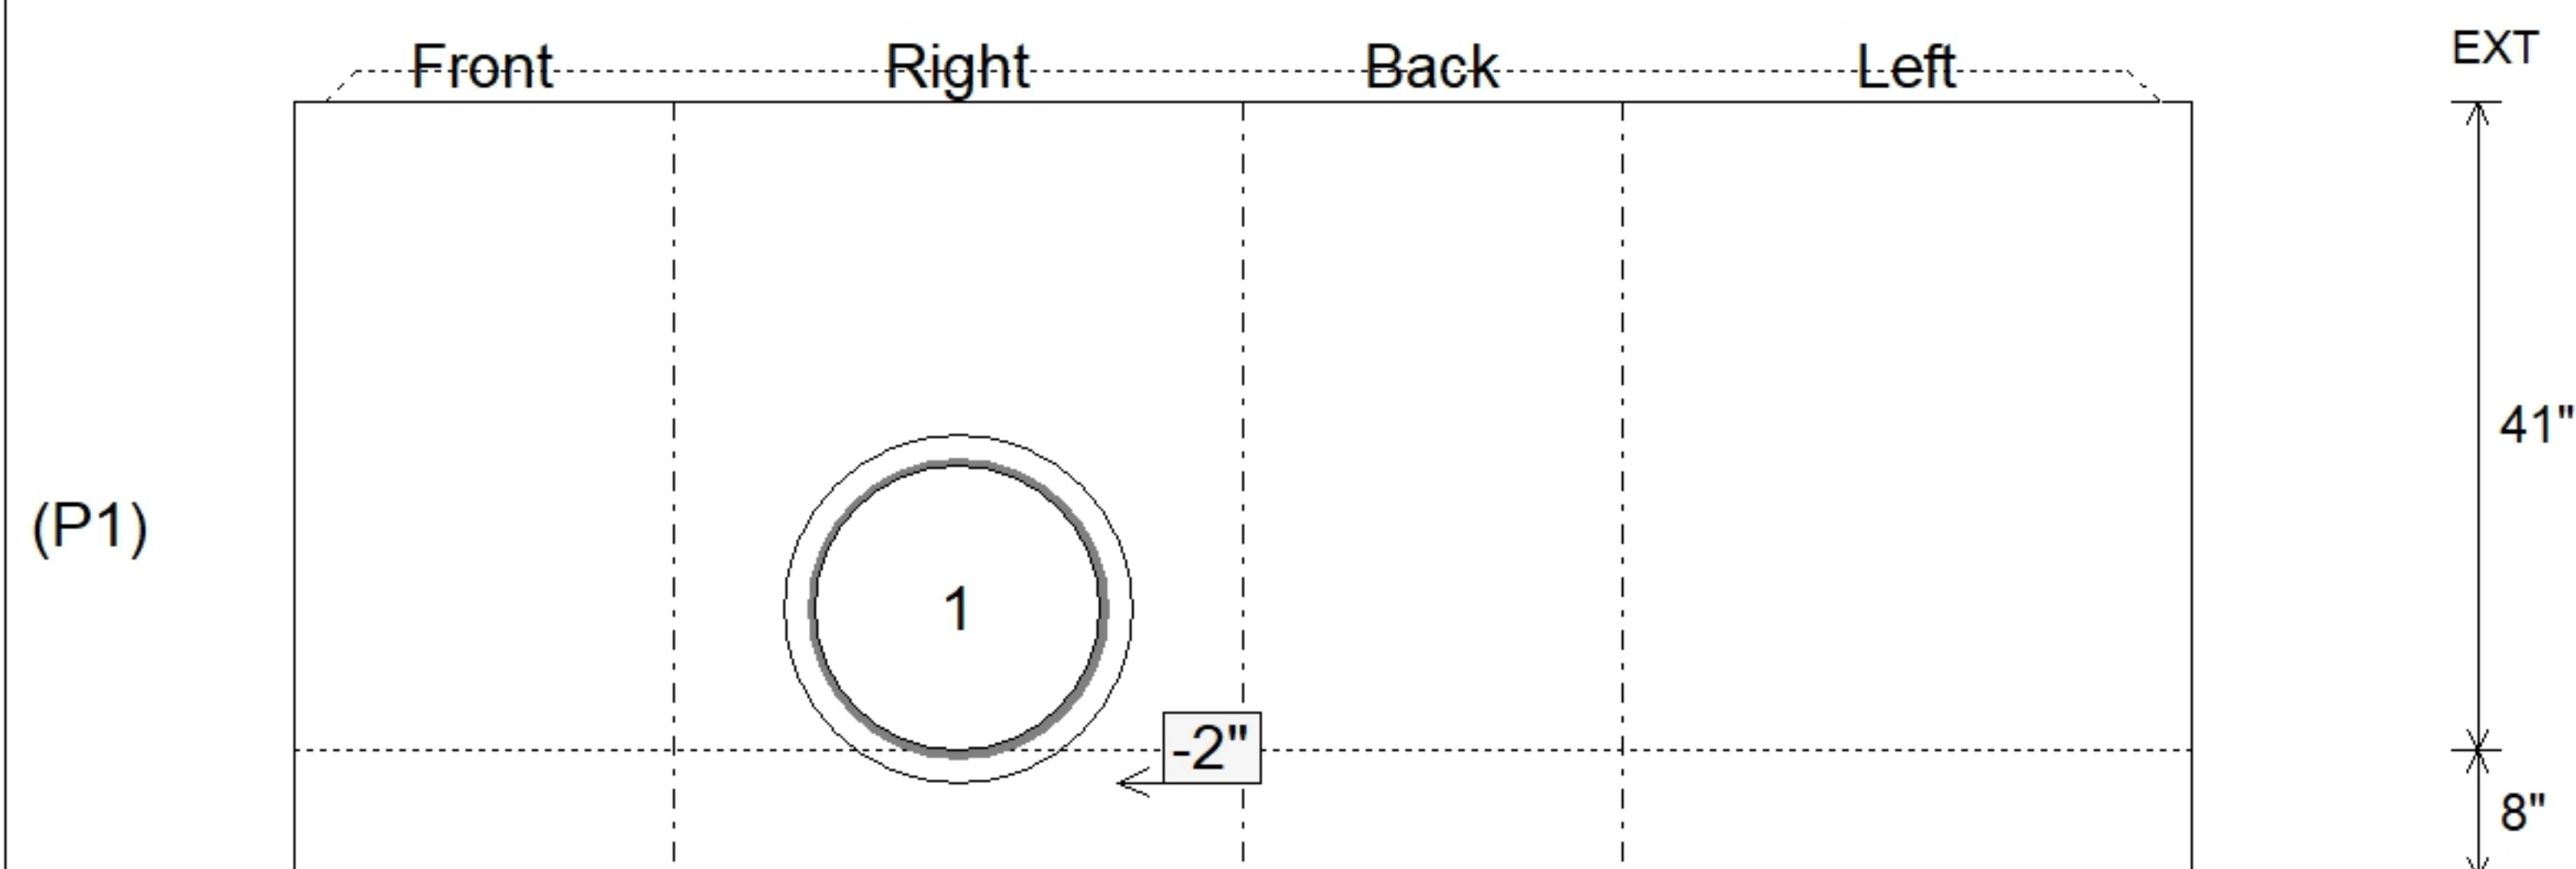

SUBMITTAL
APPROVED BY:
