

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100





Slack: 4.04"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

107.15


Structure Total: 14127 lb



24" x 36" - BOX BASE 8inW, 8inF - 42" - (P1)

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⎵)	Ref
Rim	821.46'							
Reducer								
Invert 1	815.29'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	815.29'	170°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

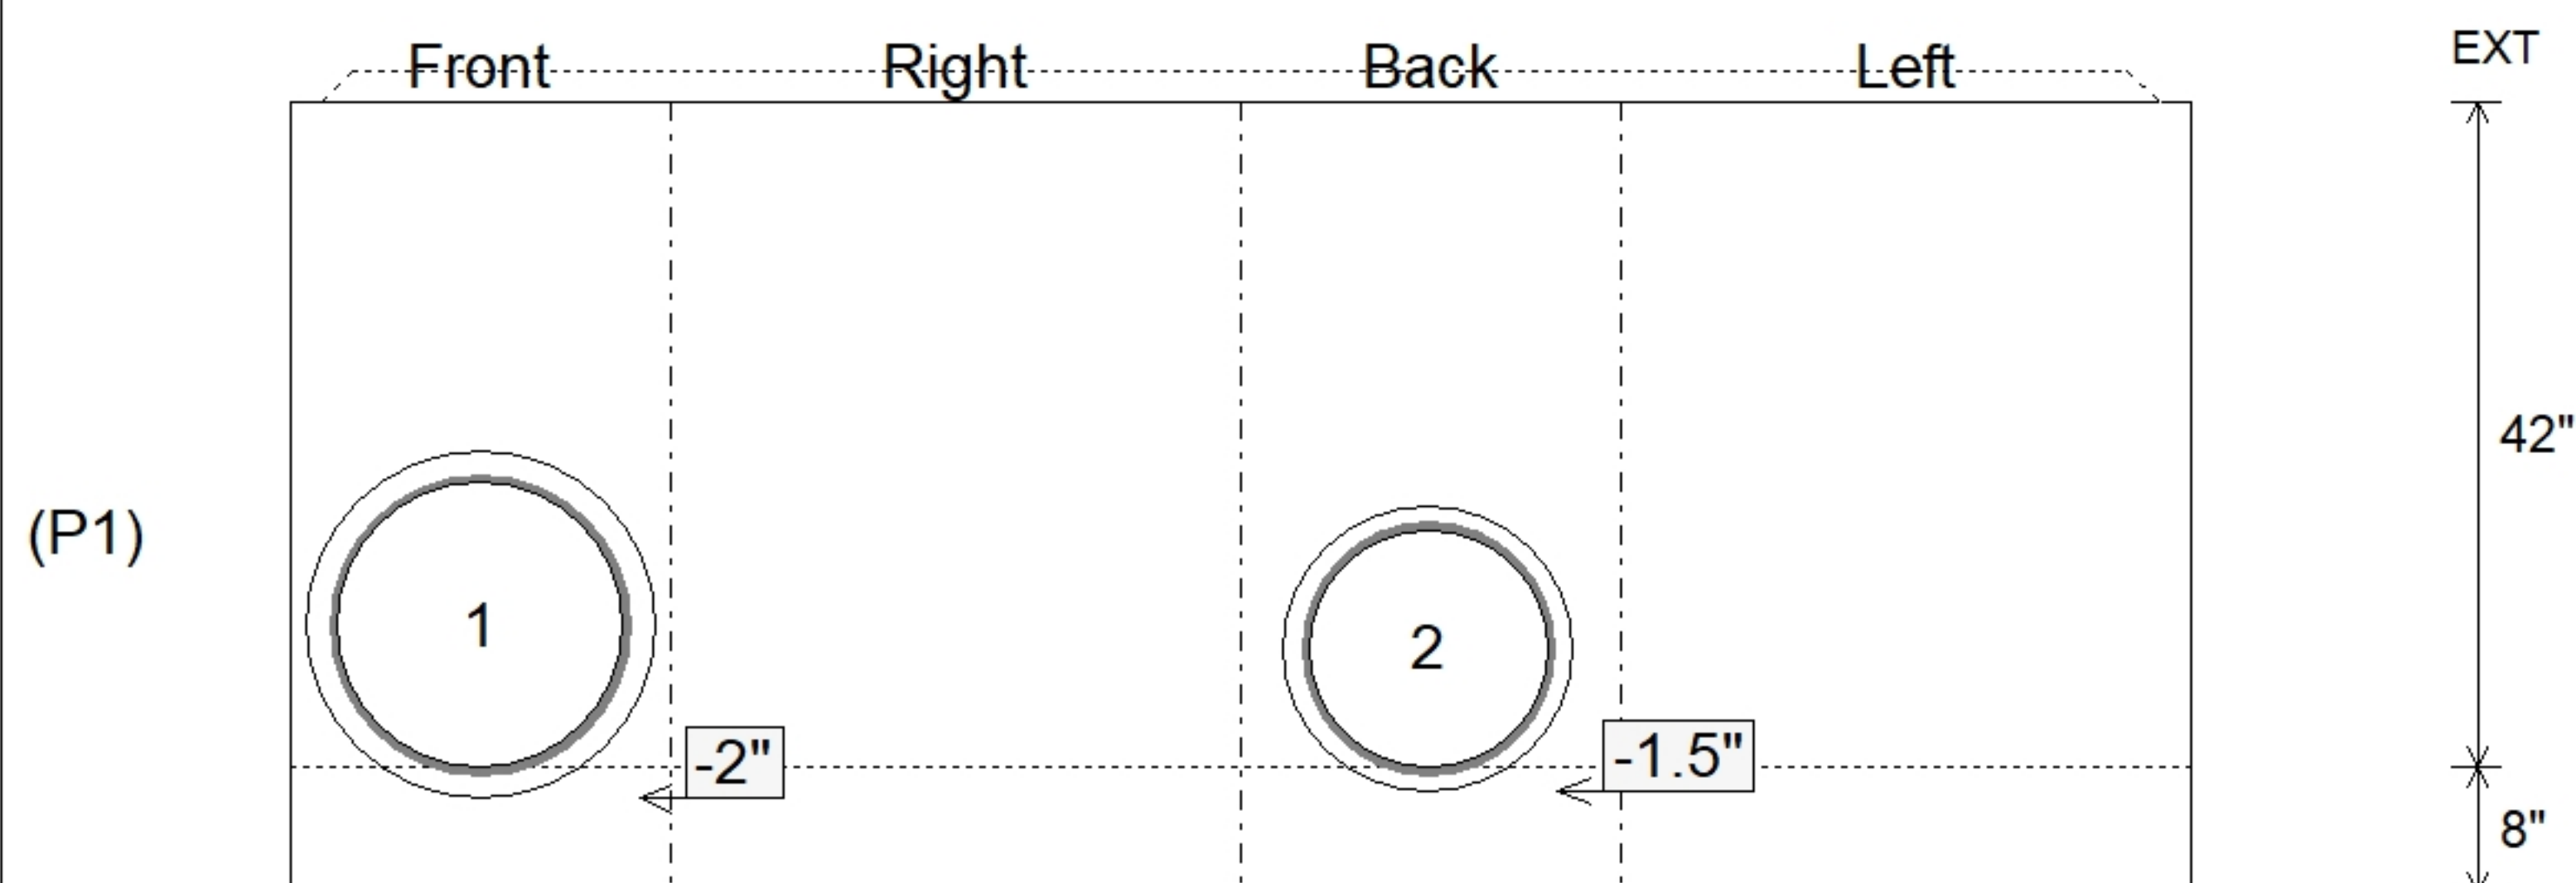

SUBMITTAL
APPROVED BY:
