


**Contractor: Cleary Construction, Inc.**

Plant: 100




Slack: 2.24"


Structure Total: 13433 lb

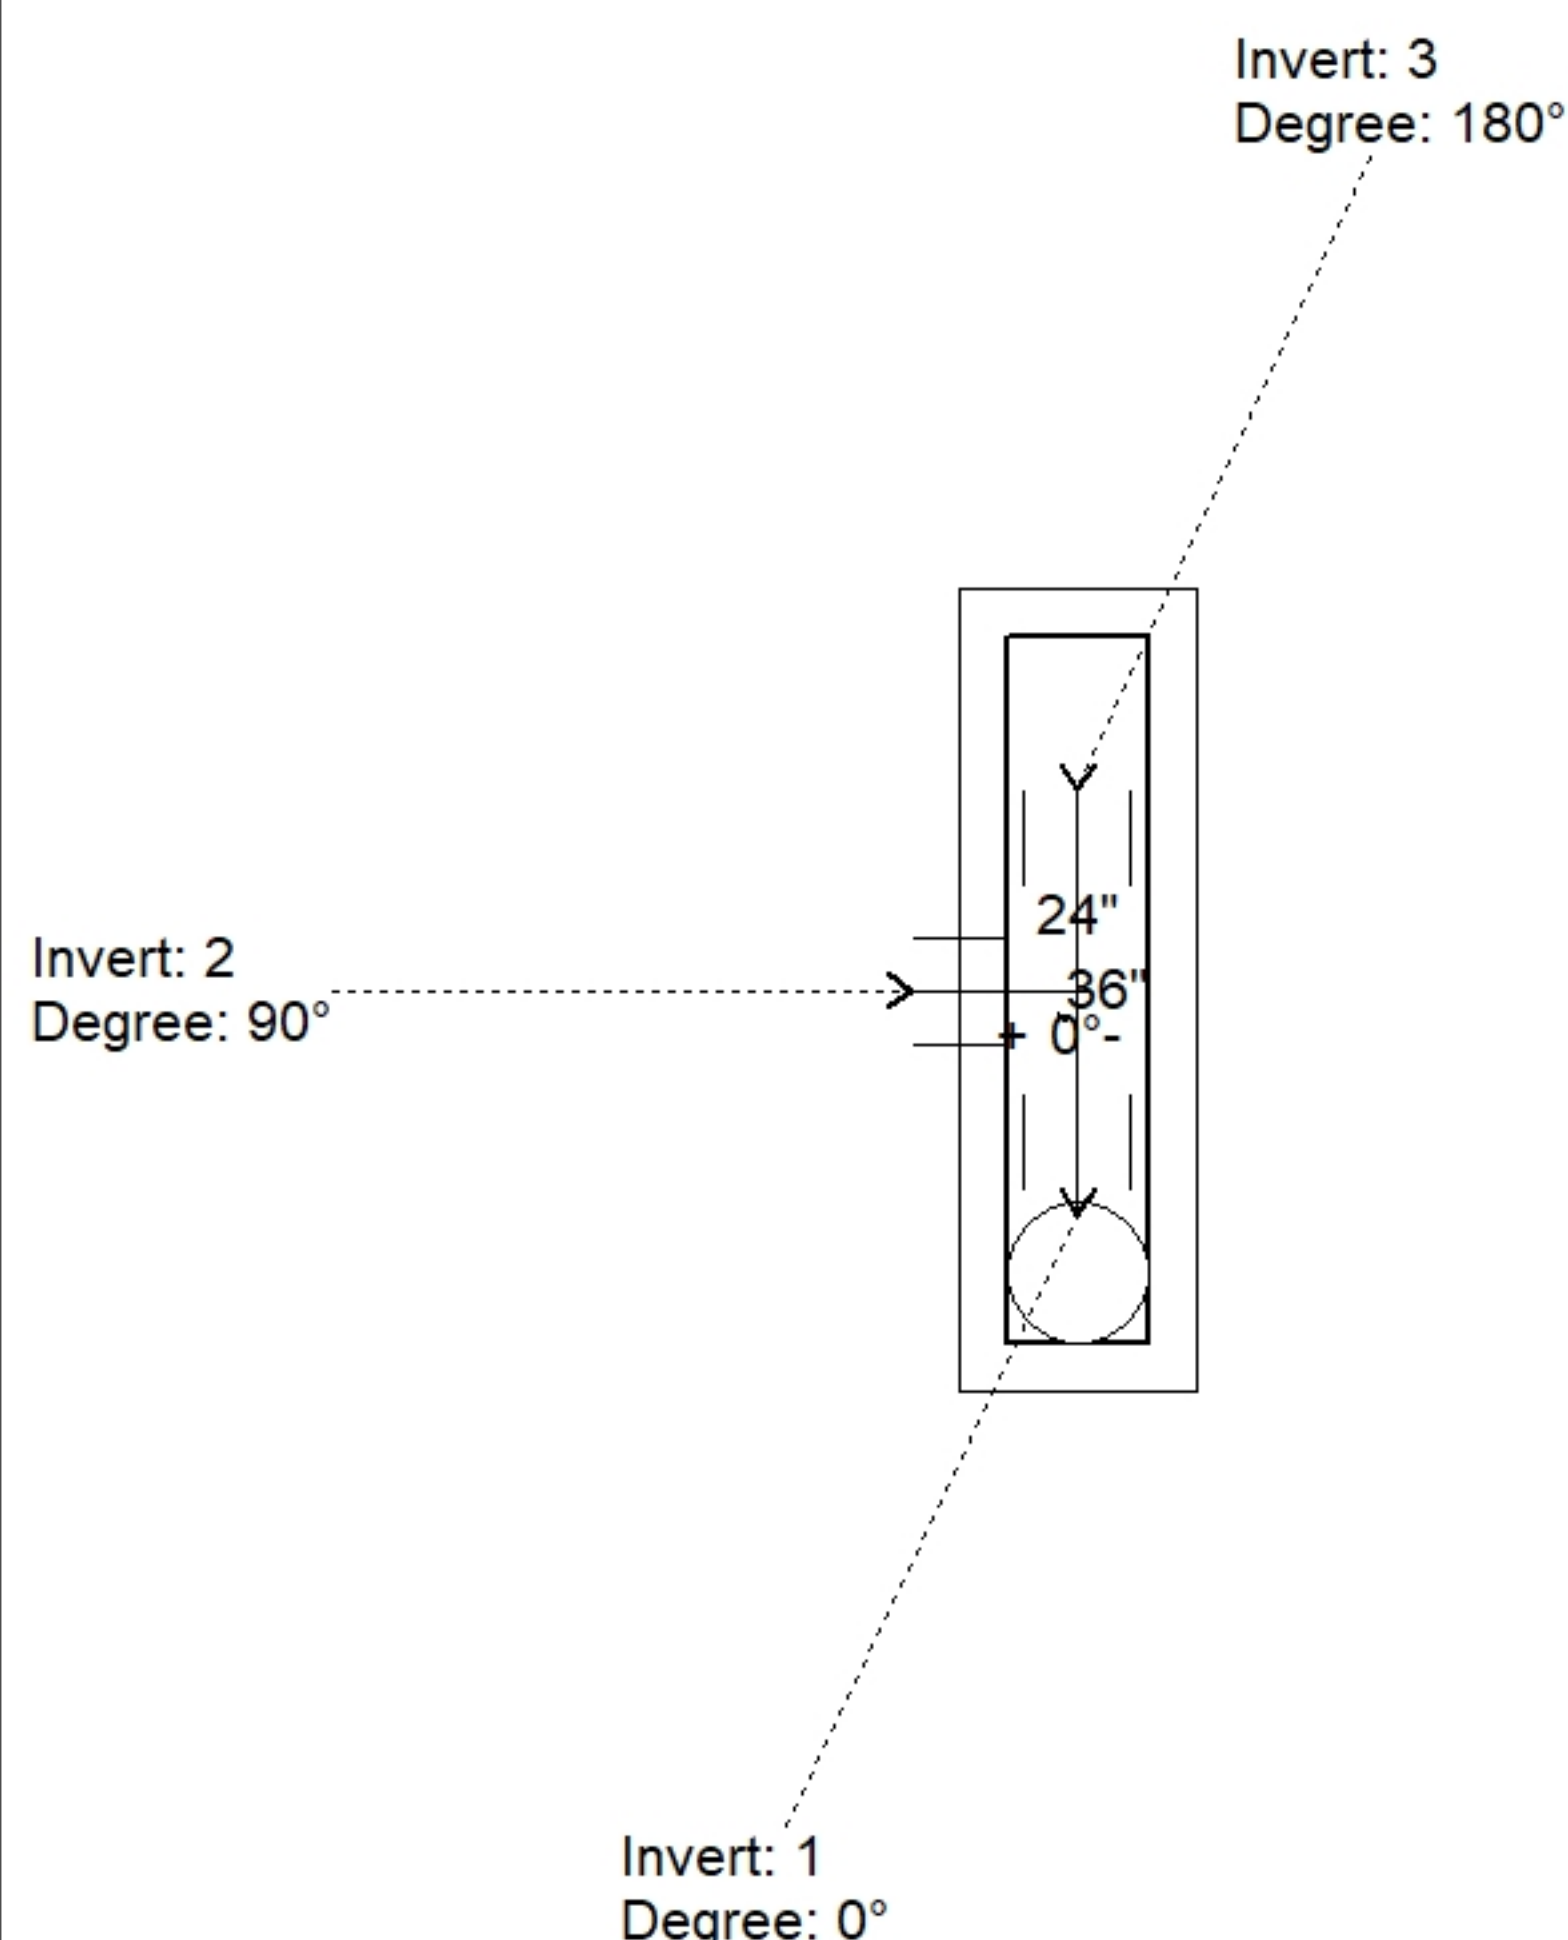

| Position | Elev    | Angle | Pipe    | Pipe OD | Hole | Connector | Up (⌵) | Ref |
|----------|---------|-------|---------|---------|------|-----------|--------|-----|
| Rim      | 797.85' |       |         |         |      |           |        |     |
| Reducer  |         |       |         |         |      |           |        |     |
| Invert 1 | 792.33' | 0°    | 15" CMP | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 2 | 792.33' | 90°   | 15" CMP | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 3 | 792.33' | 180°  | 15" CMP | 16"     | 18"  | Hole 18   | -1.5"  | P1  |
| Invert 4 |         |       |         |         |      |           |        |     |
| Invert 5 |         |       |         |         |      |           |        |     |
| Invert 6 |         |       |         |         |      |           |        |     |
| Invert 7 |         |       |         |         |      |           |        |     |
| Invert 8 |         |       |         |         |      |           |        |     |

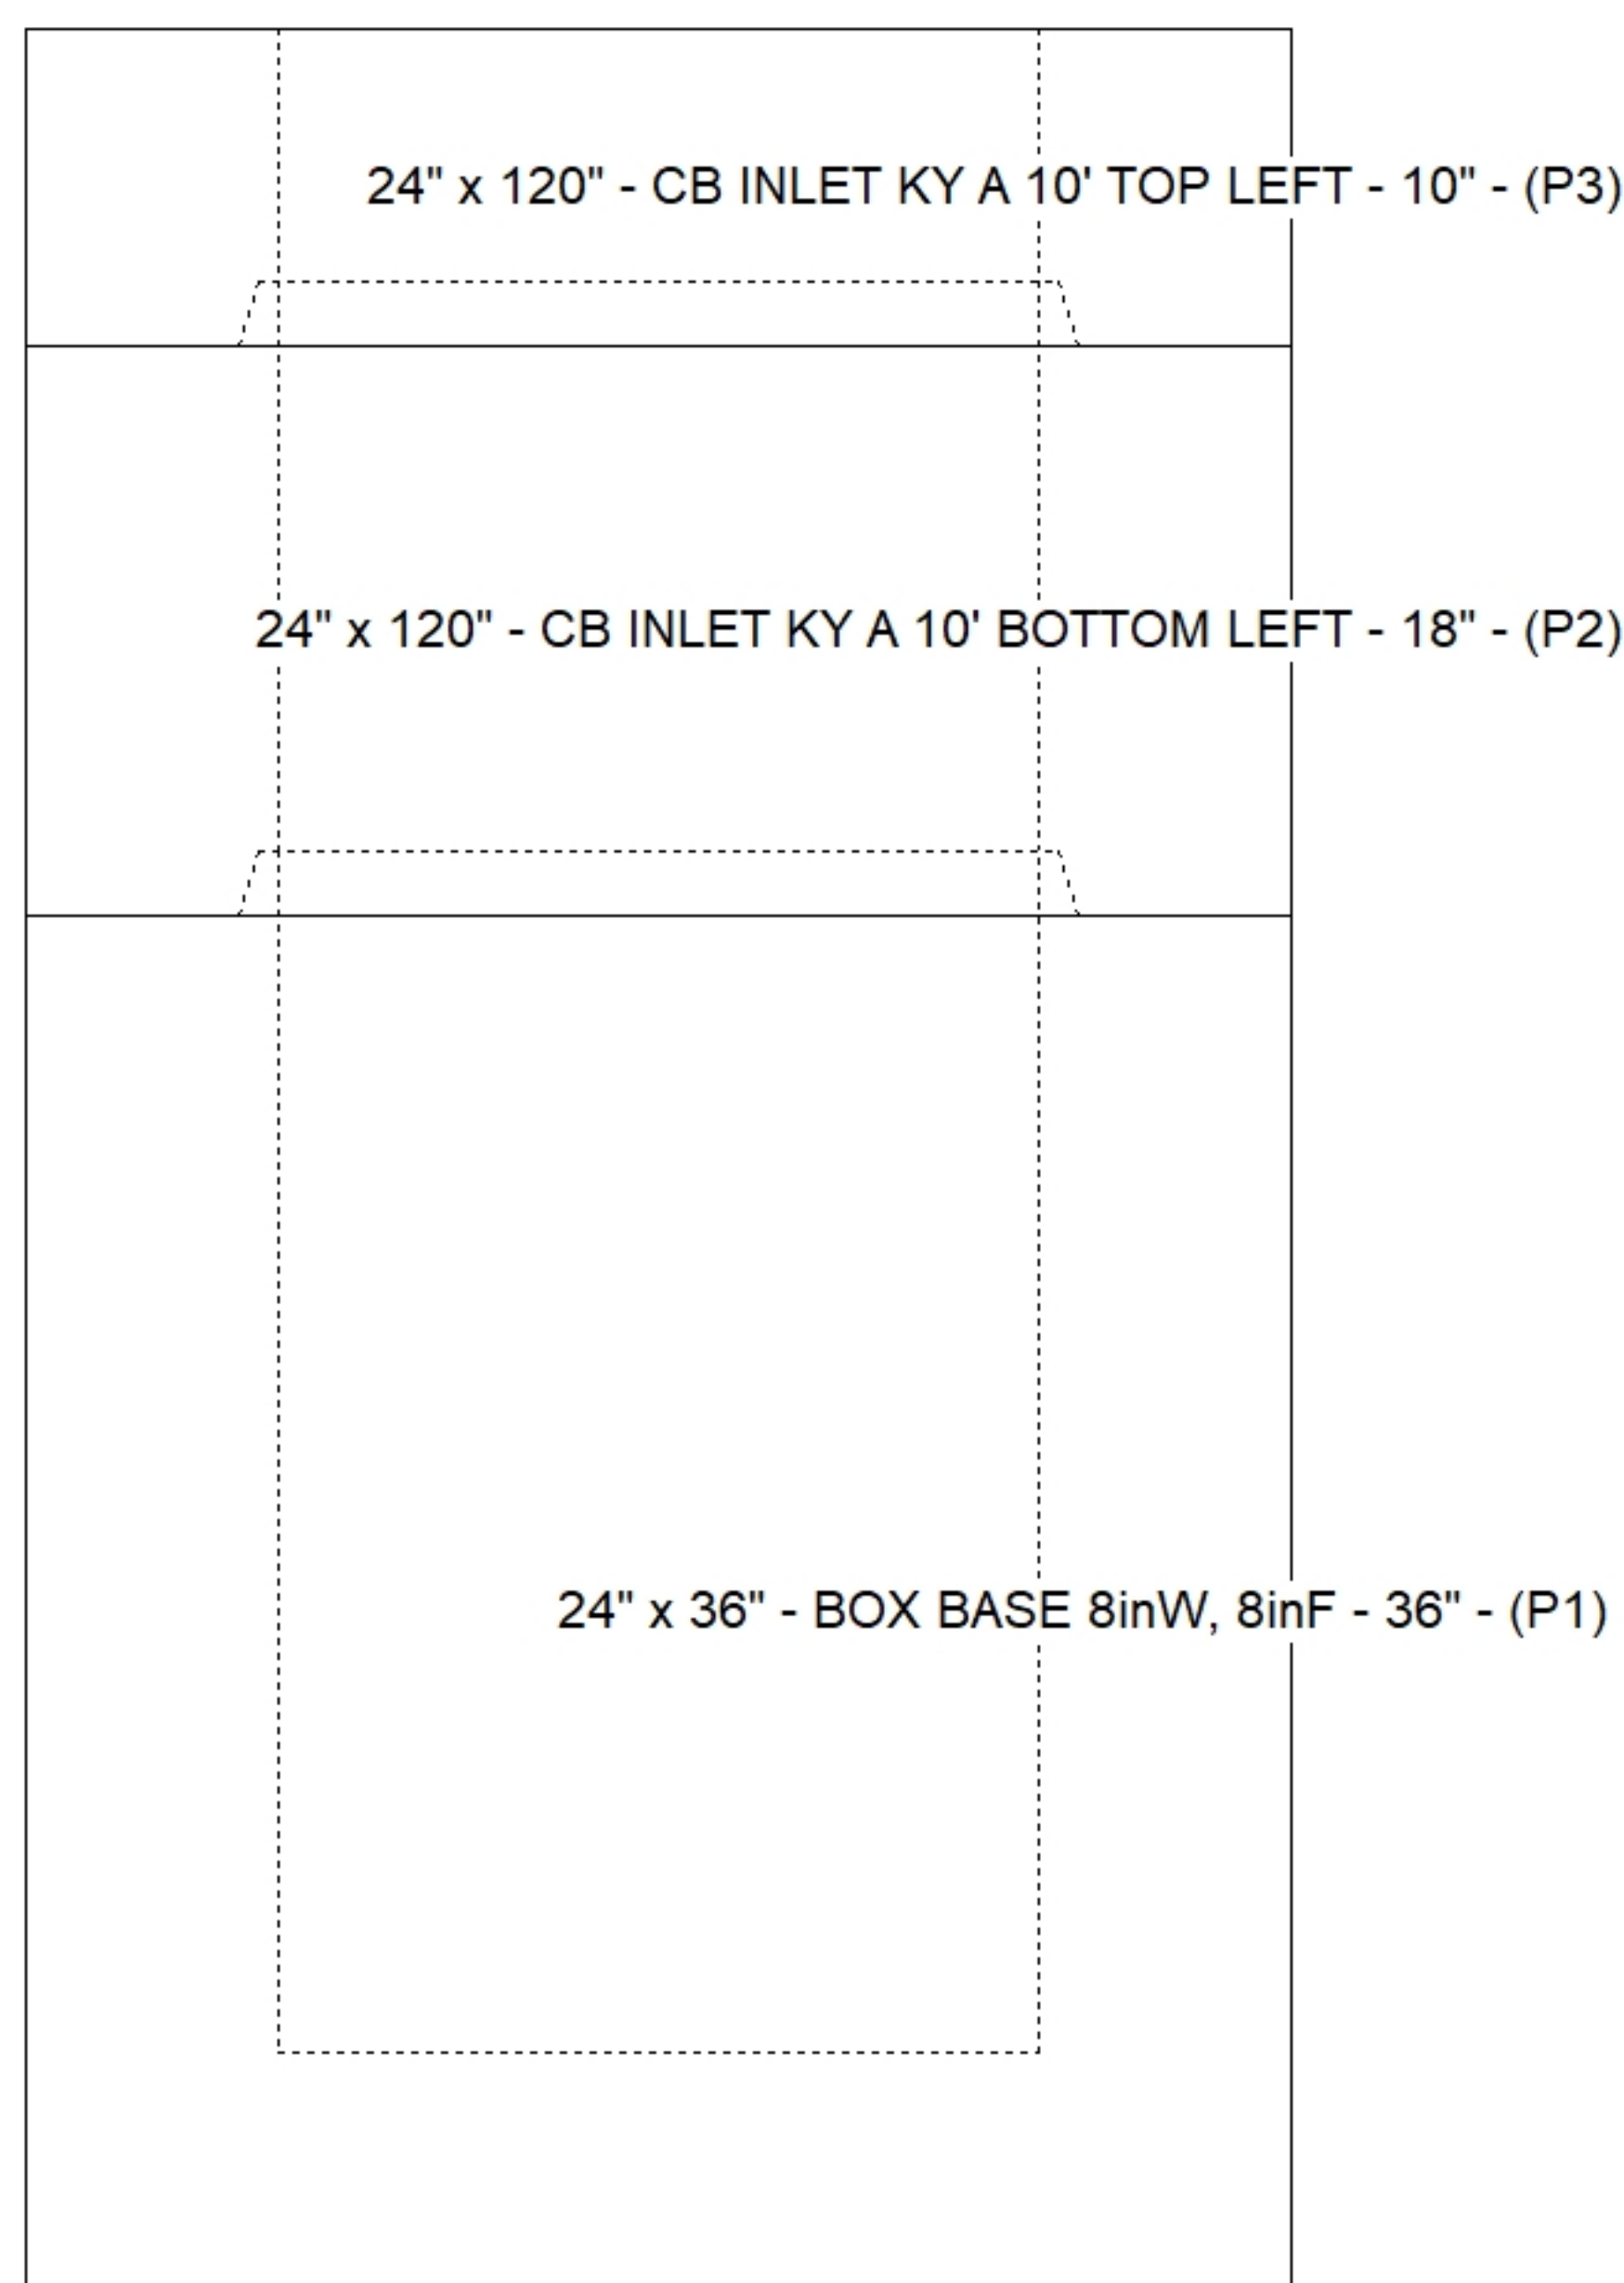

### Default - Interior Dimensions

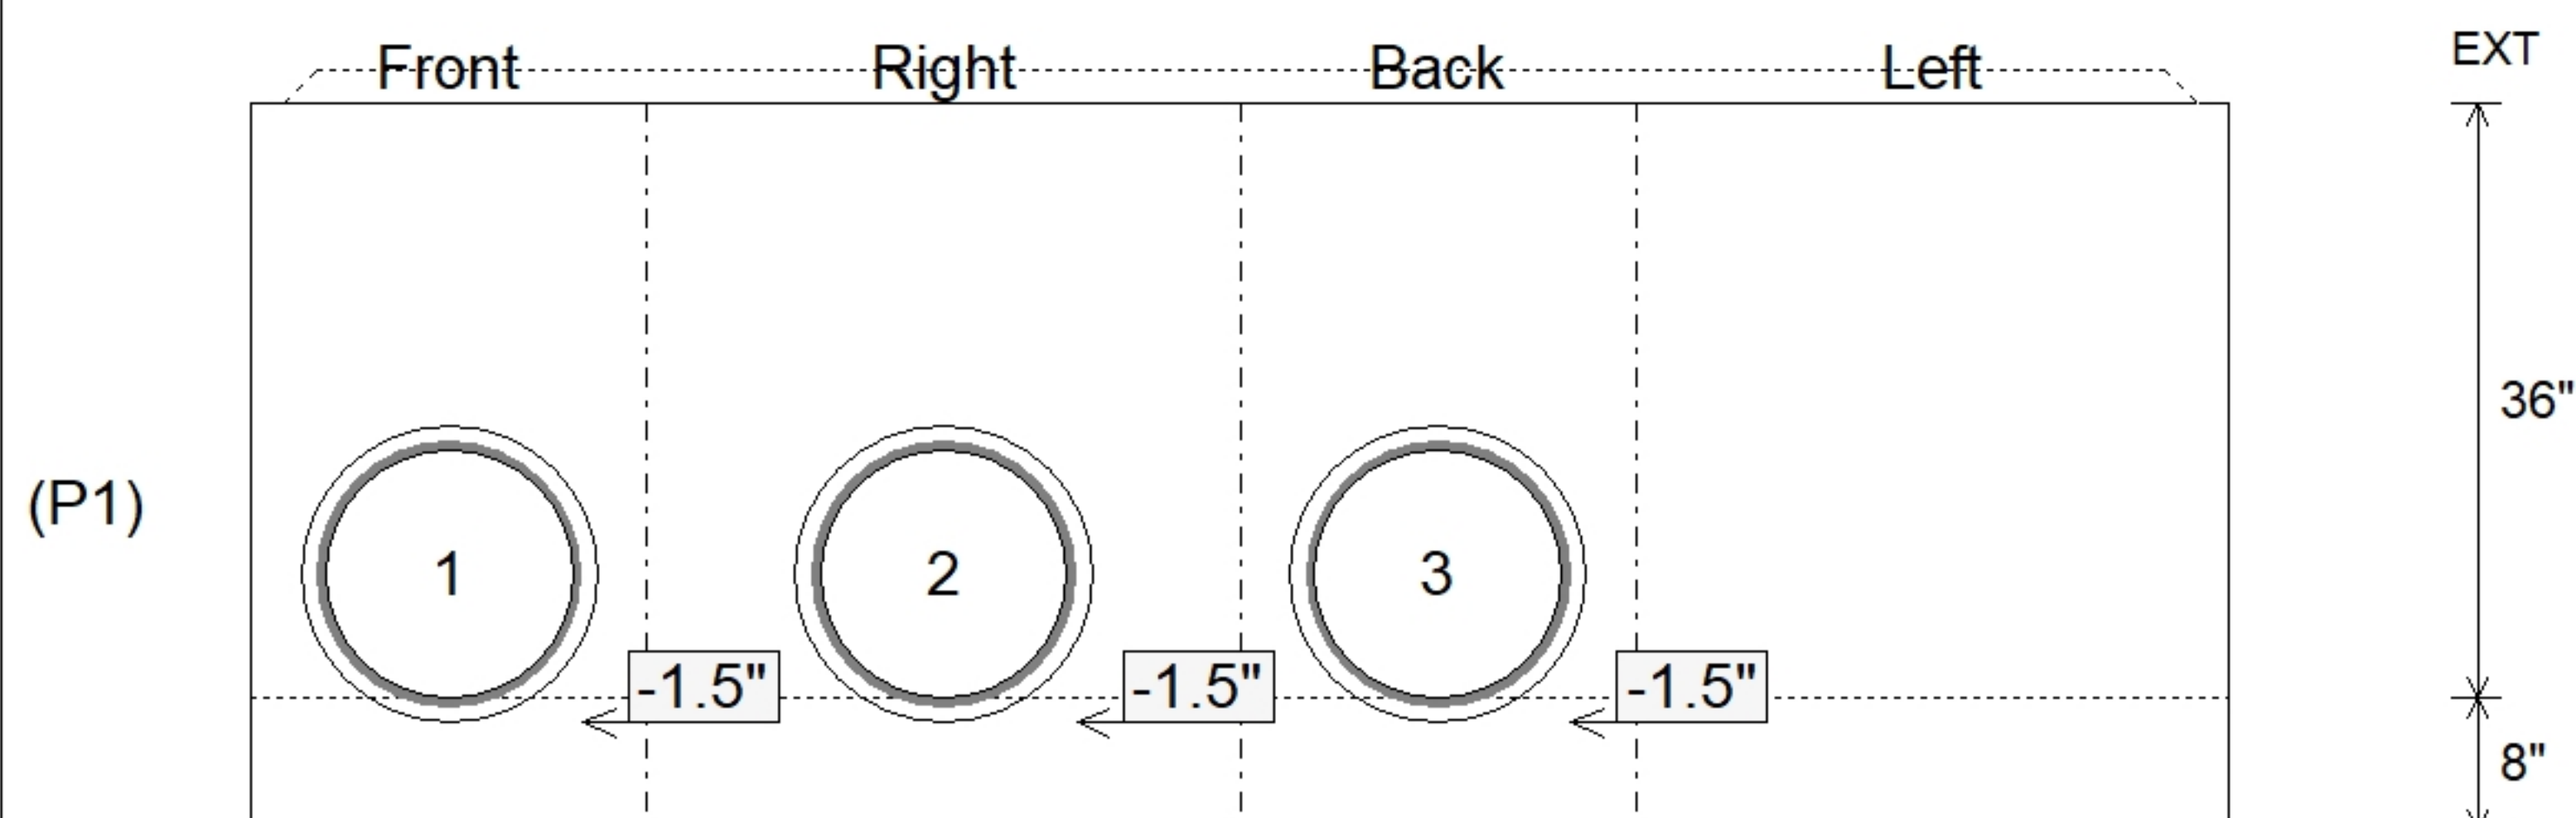

SUBMITTAL  
APPROVED BY:
