



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 8/12/2026 11:09:21 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 15610-145 MHB											
P1 MH048BA72		MH BASE T/n									
P4) 24" - CASTING HEIGHT - 8" P3) 24" - GRADE RING F/F - 3" P2) 48" - ECC CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE T/n - 72" 1) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 1) Hole - 34 1) Hole - 28 10) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 3200 lb 5672 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 0 lb Structure Total: 9075 lb		Structure Notes: . **KYTC STATE PROJECT** 1. PER KYTC MH B / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE KY-510 F/C (KY TY.2)). . REINFORCING PER ASTM A615 (GRADE 60.) - CONE (As.12). - RISER/WALLS (As.12). - FLOOR (As.31) #5 BARS AT 12" C.C.E.W.				
Rim: 821.1' Rim to Invert: 10.08' Slack: 0.96" Sump: 5" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	811.02'	0°	0"	24" RCP B WALL	30"	Hole 34	34"	37.782"	0"	0"	
Invert 2	811.02'	180°	91.125"	24" CMP	25"	Hole 28	28"	29.896"	3"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

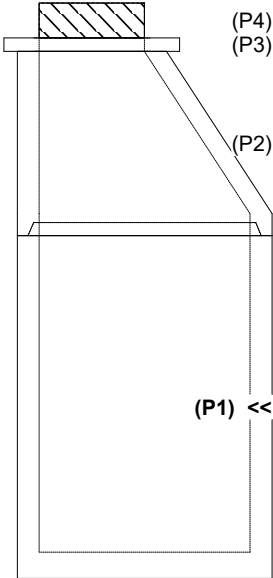

(P4)
(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

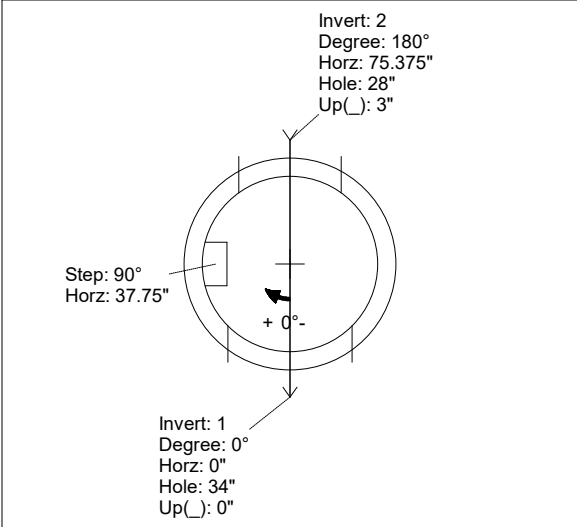


Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 28"
Up(_): 3"

Step: 90°
Horz: 37.75"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 34"
Up(_): 0"

UPSIDE-DOWN VIEW (int. dimensions)

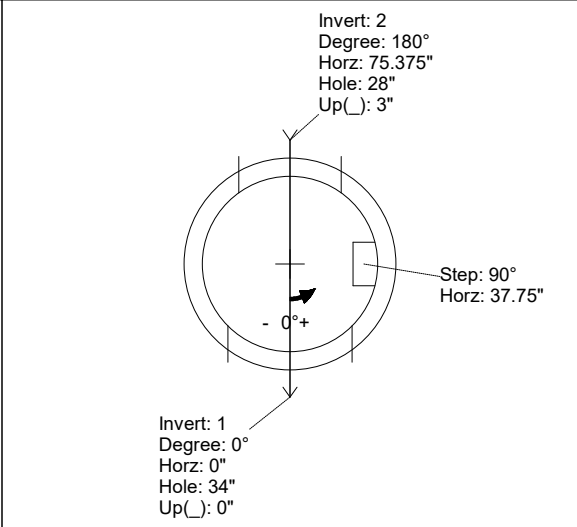


Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 28"
Up(_): 3"

Step: 90°
Horz: 37.75"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 34"
Up(_): 0"

INSIDE WALL DIMENSIONS

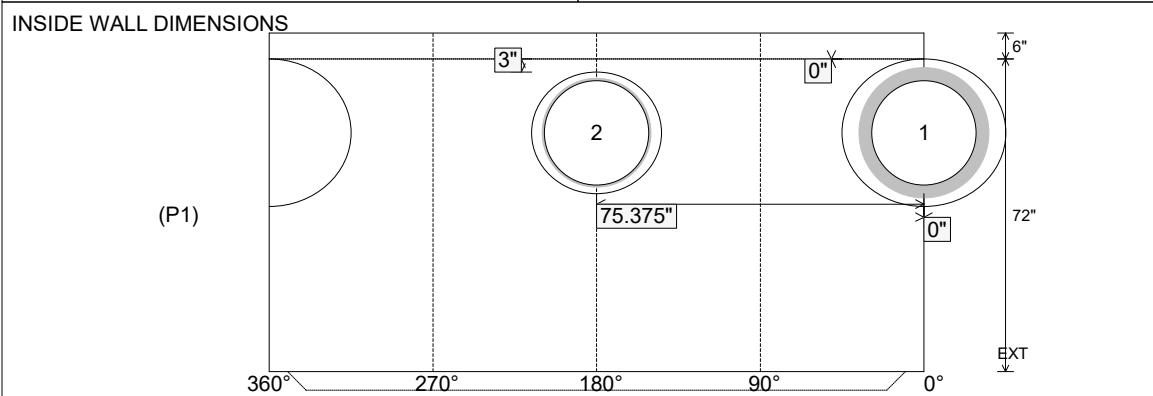

(P1)

360° 270° 180° 90° 0°

3" 0" 75.375" 0" 72" 6" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 72" Height (Ext): 78"	Weight (Net): 5672 lb Volume (Net): 1.45cu.yd
----------------------------------	---------------------------------	--	--	--
