

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100



Rim to Invert: 10.08'

Floor Height: 6"


Slack: 0.96"

- FLOOR (As.31) #5 BARS AT 12" C.C.E.W.


10) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 9075 lb

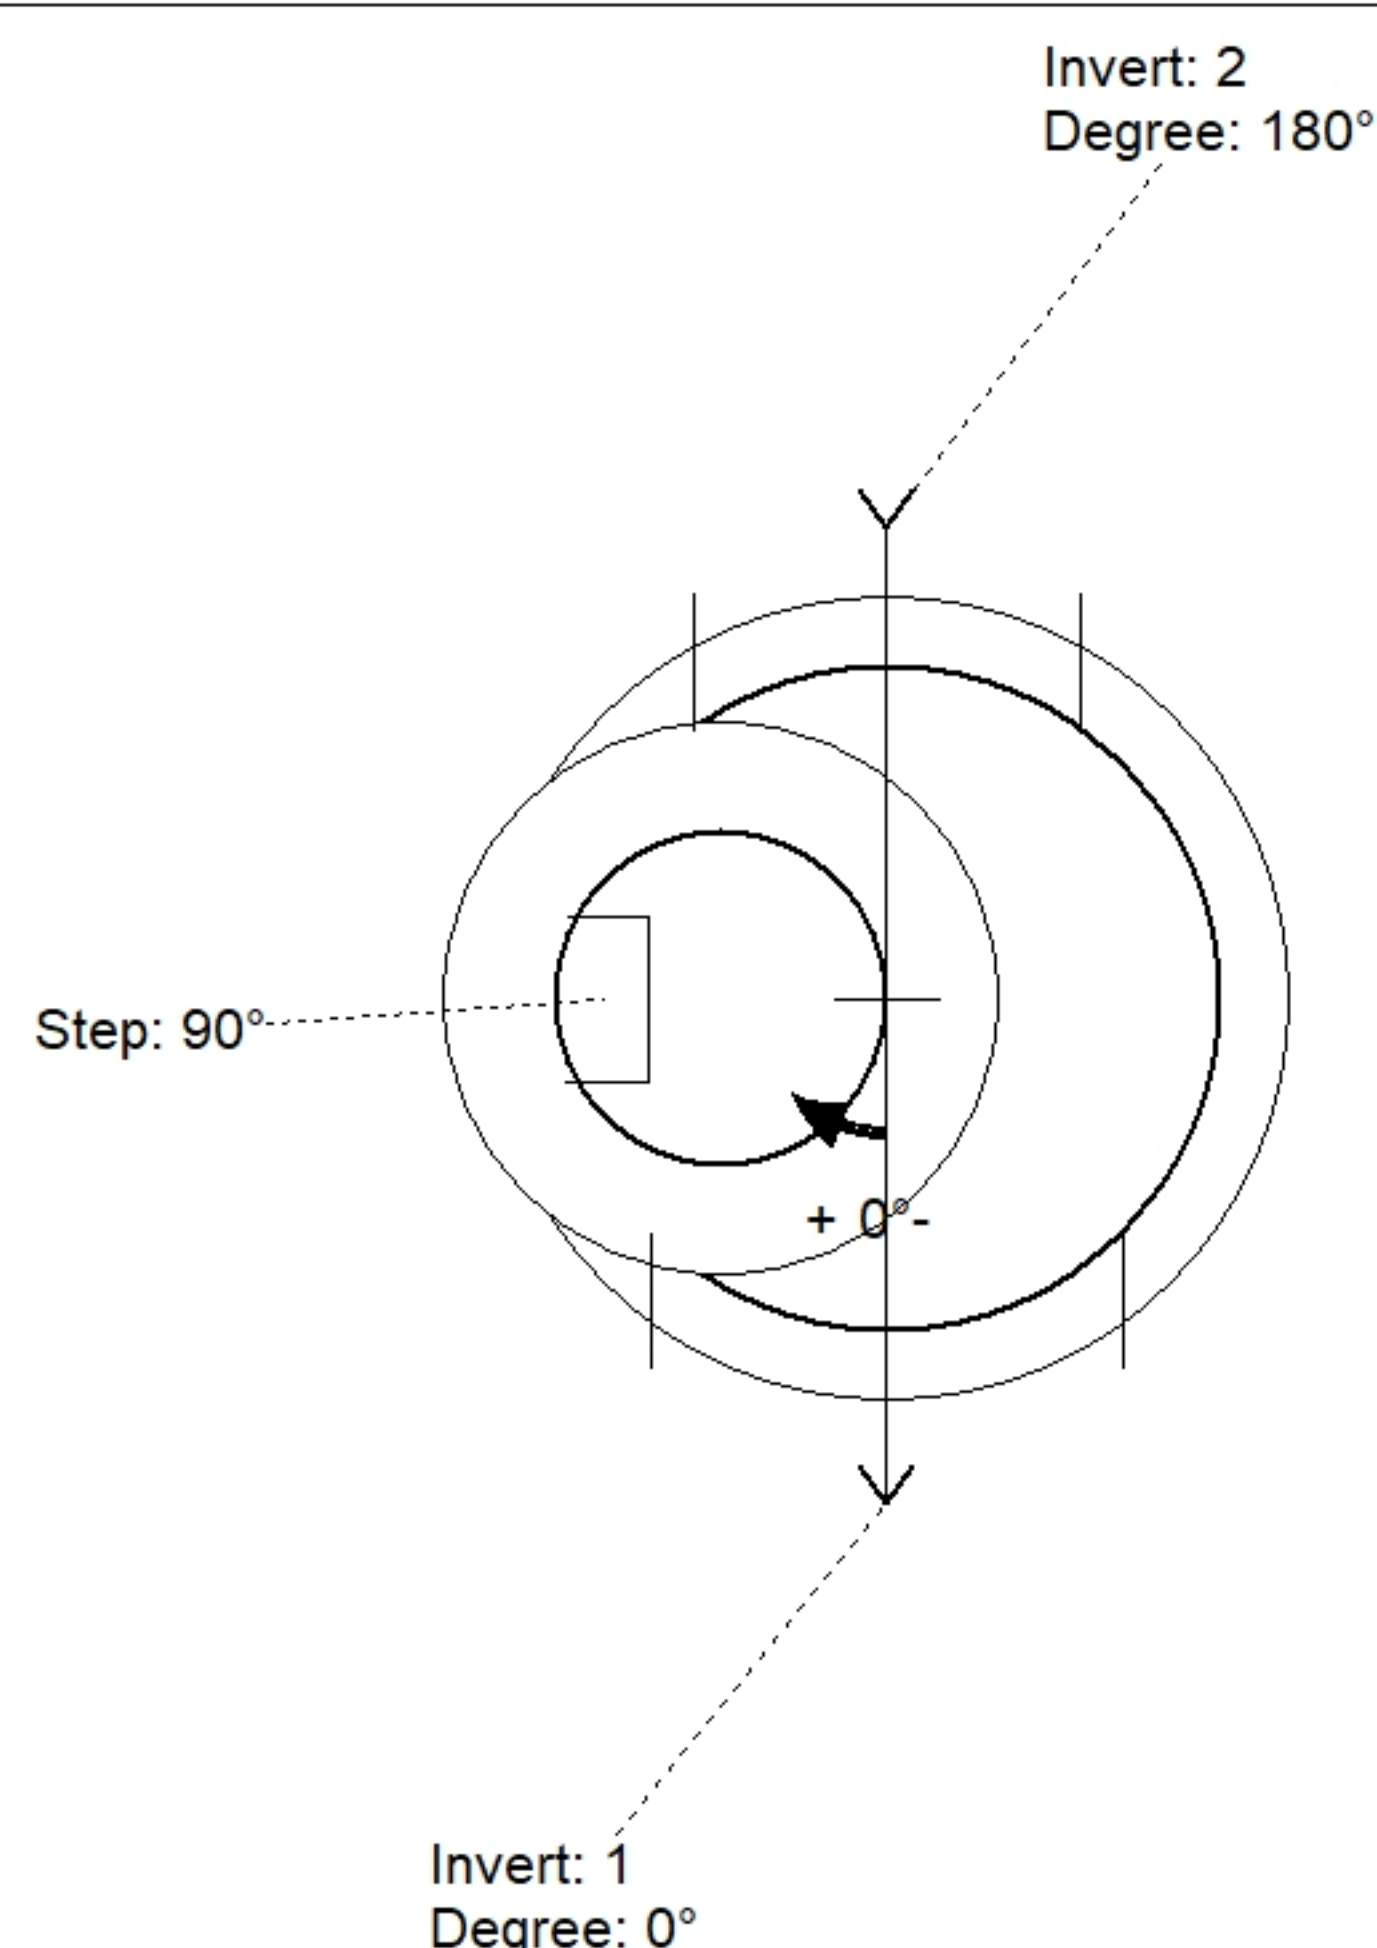

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	821.1'							
Reducer								
Invert 1	811.02'	0°	24" RCP B WALL	30"	34"	Hole 34	0"	P1
Invert 2	811.02'	180°	24" CMP	25"	28"	Hole 28	3"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

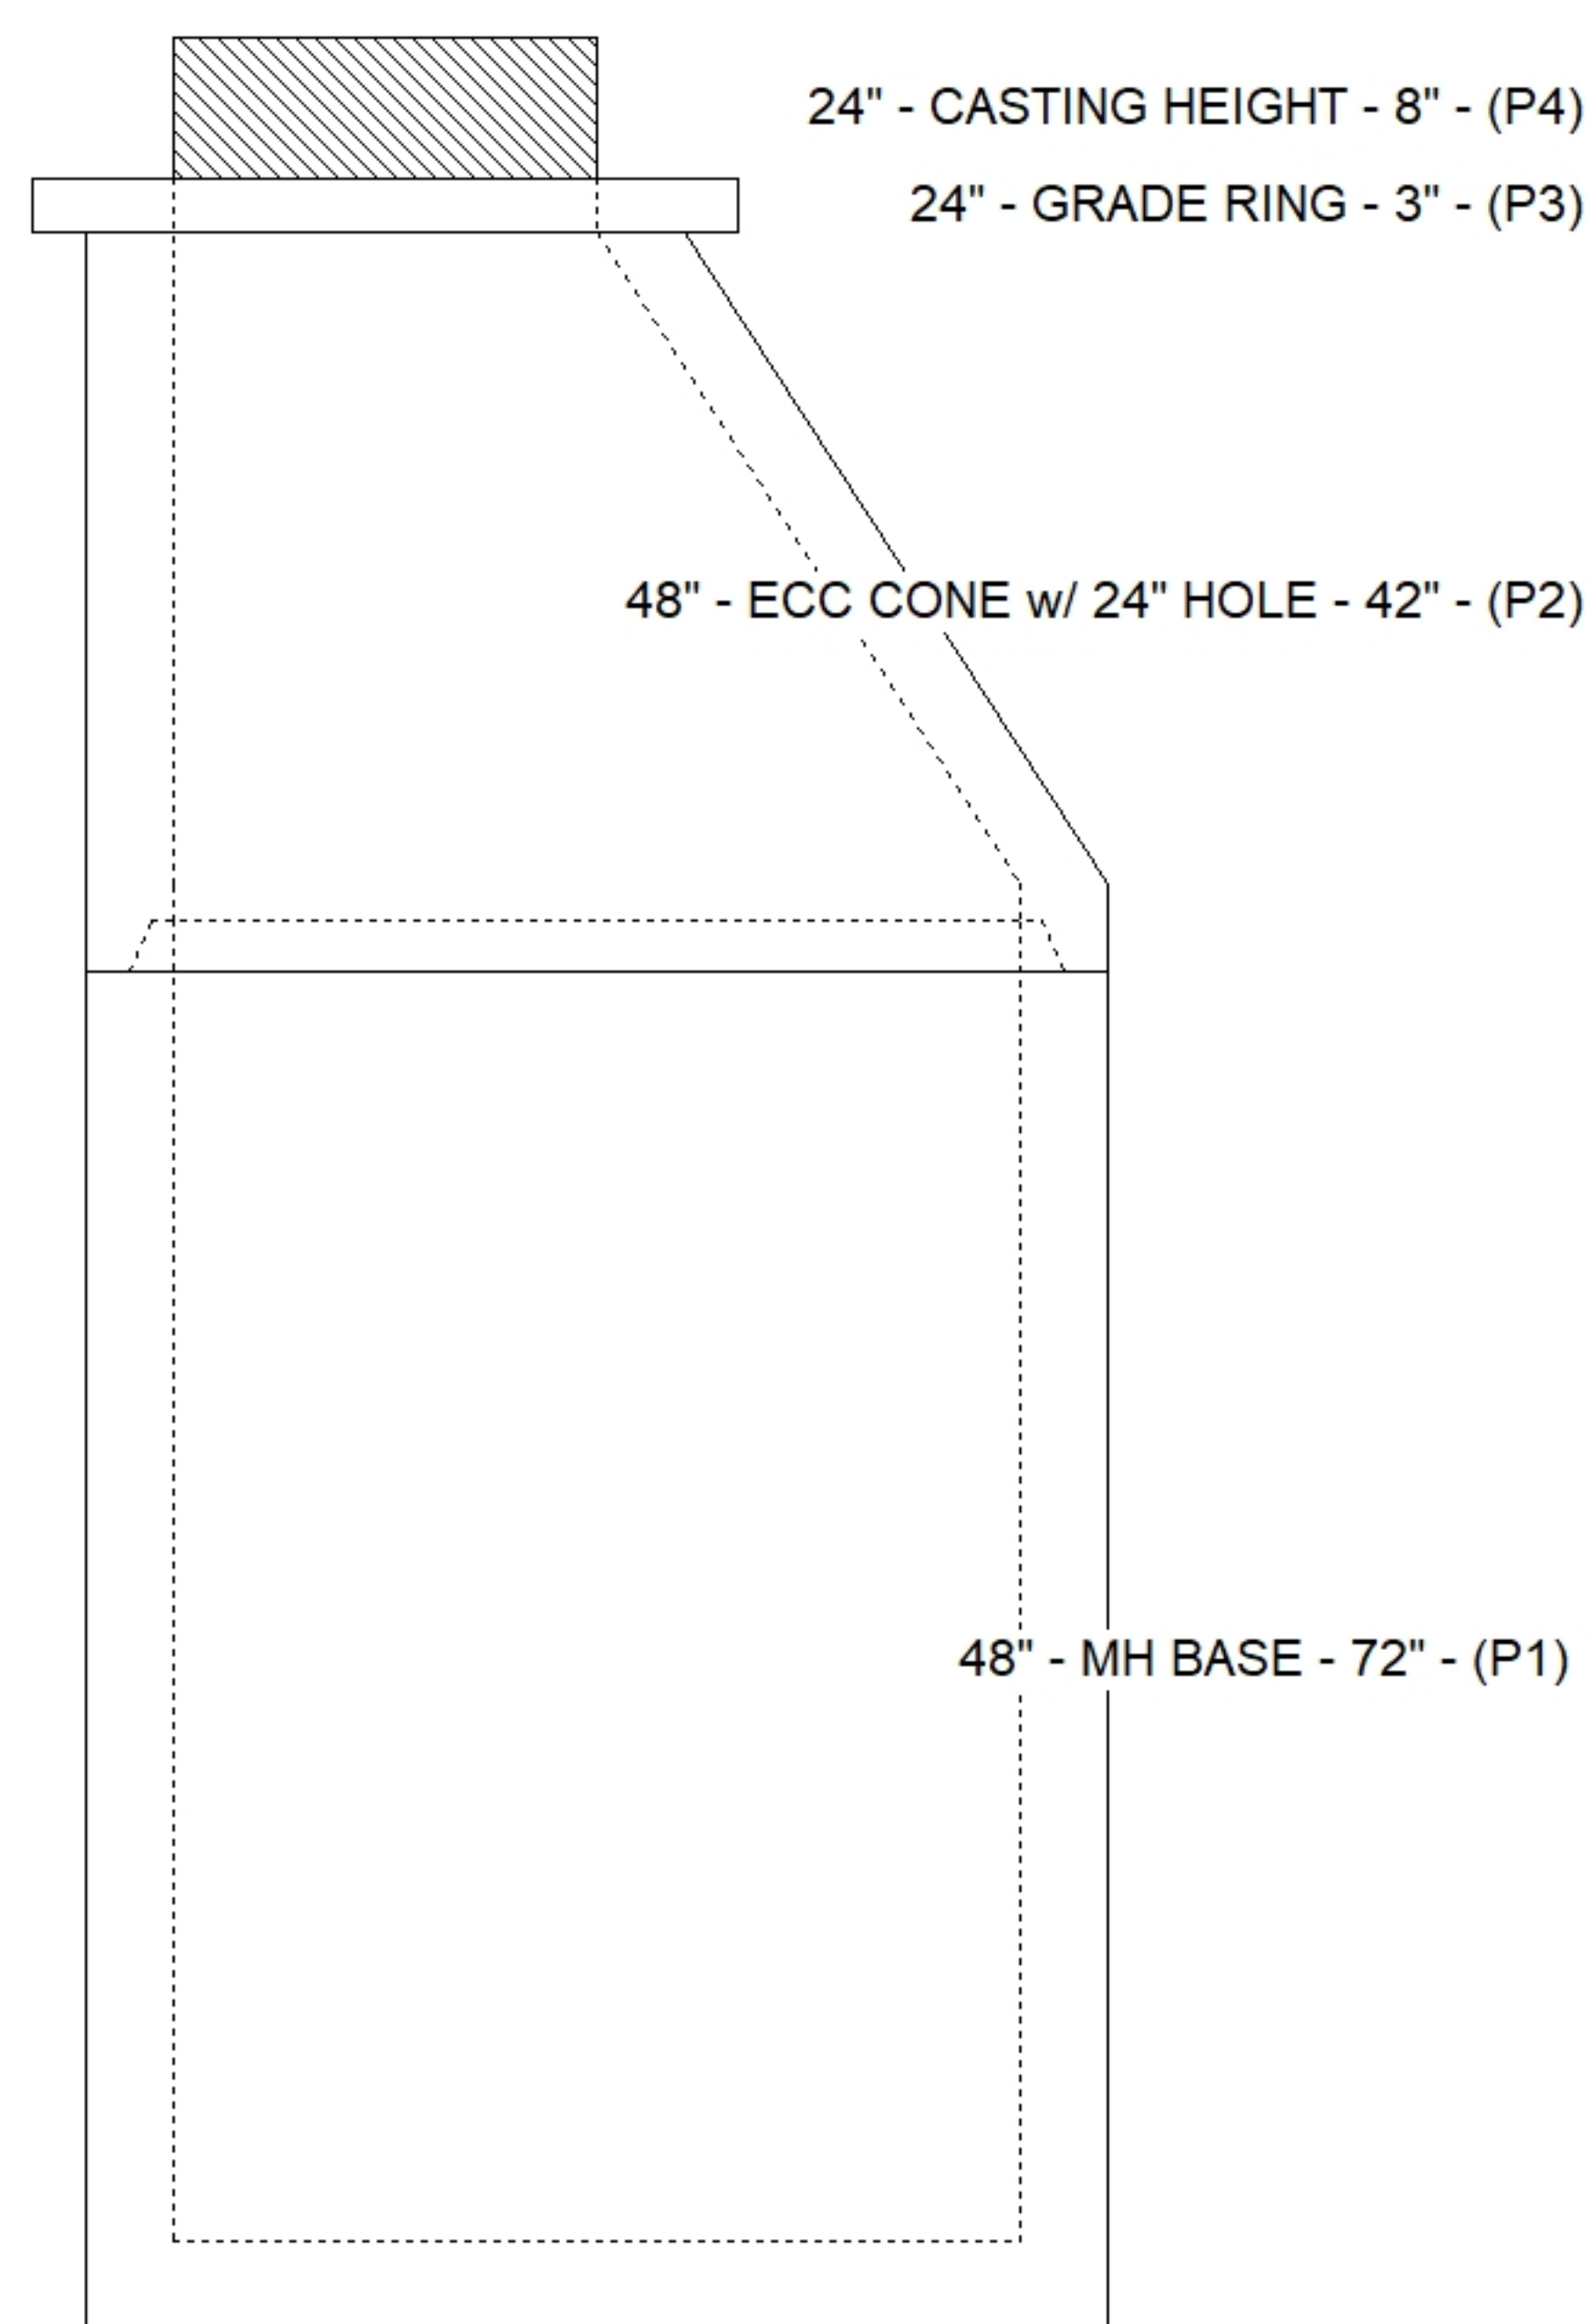

Default - Interior Dimensions

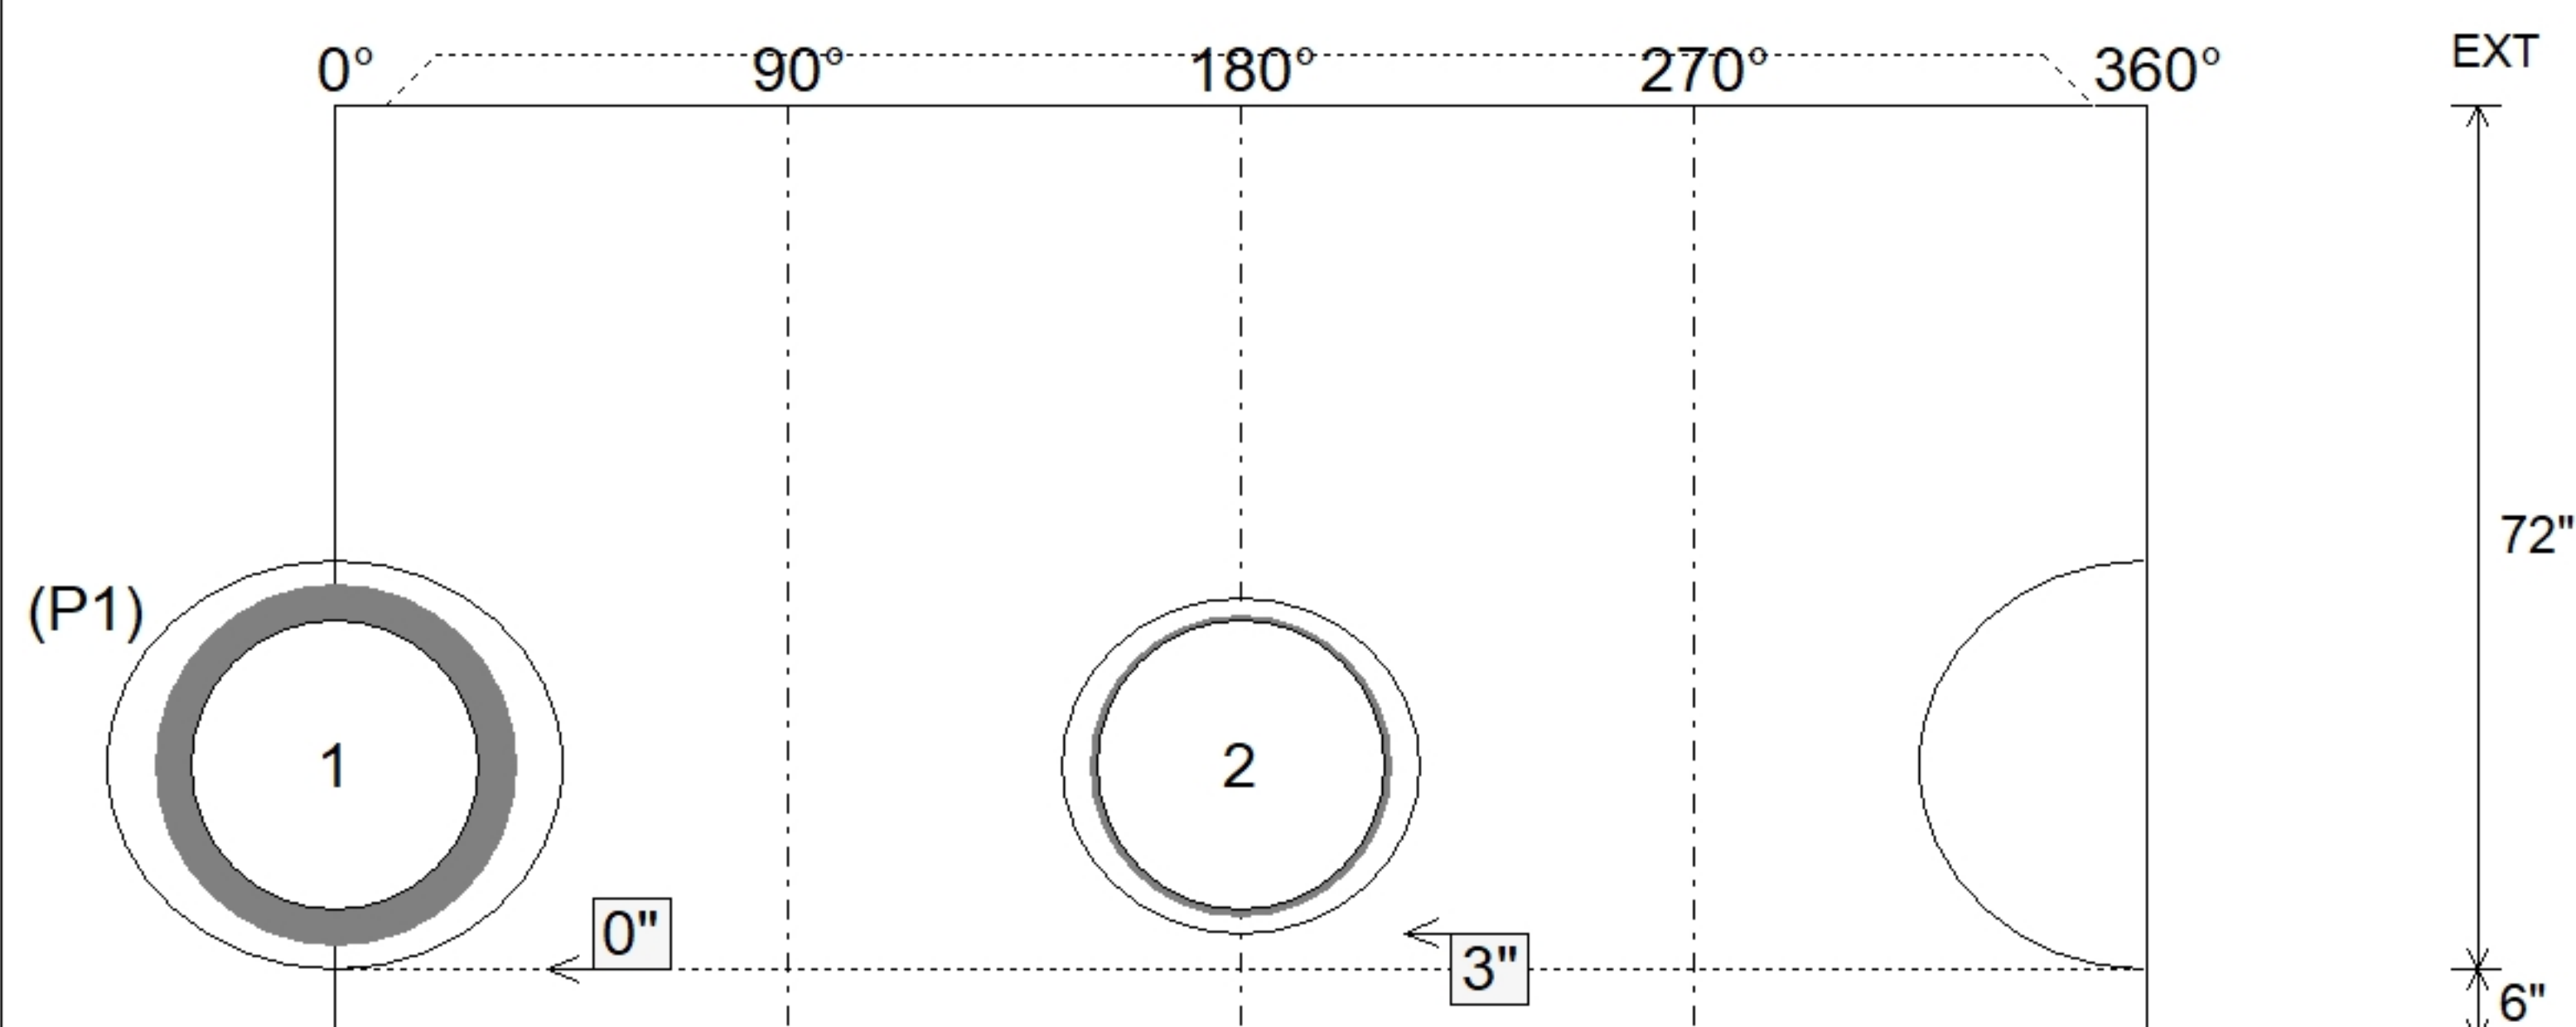

Submittal Drawing
8/17/2026 2:01:39 PM

SUBMITTAL
APPROVED BY:
