

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Peewee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

8/14/2026 1:21:12 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 35770-148 MHC

P2 BX4848_08TS8

CB FT REDUCER 48" HOLE T/F

- P4) 24" - CASTING HEIGHT - 8"
P3) 48" - ECC CONE w/ 24" HOLE F/G - 24"
P2) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 8"
P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF F/n - 38"
1) 48" x 48" - Conseal CS-102 1.00"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 34
1) Hole - 22
6) MH Step ML-10-TDS-NCR - 10"

Structure Total:


0 lb
1550 lb
1535 lb
10684 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
13769 lb

Structure Notes:


**** KYTC STATE PROJECT****

1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING SUPPLIED BY OTHERS (HOE KY-510 F/C (KY TY.2)).
4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK).

REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As.12)
- TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT).
- WALLS #5's AT 6" C.C.E.W.
- FLOOR #5's AT 12" C.C.E.W.

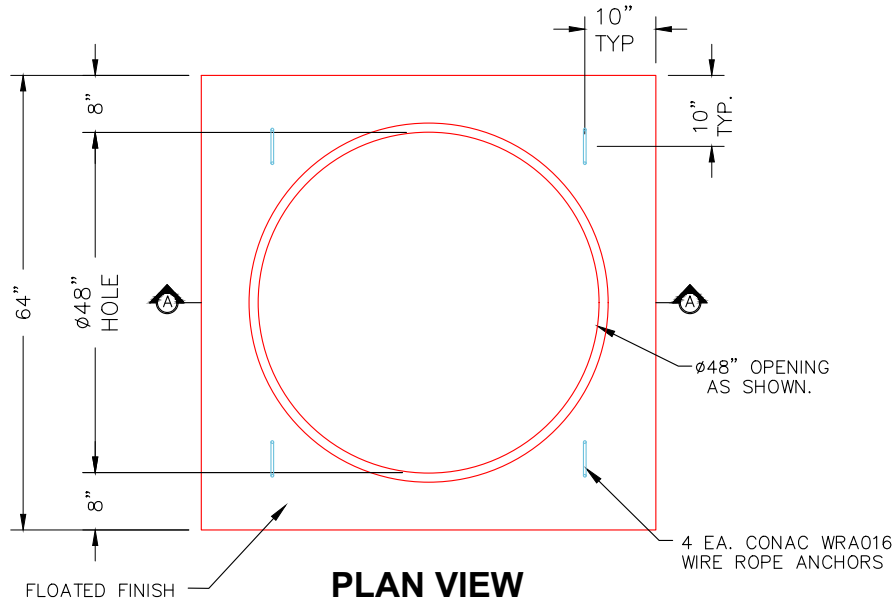

PLAN VIEW

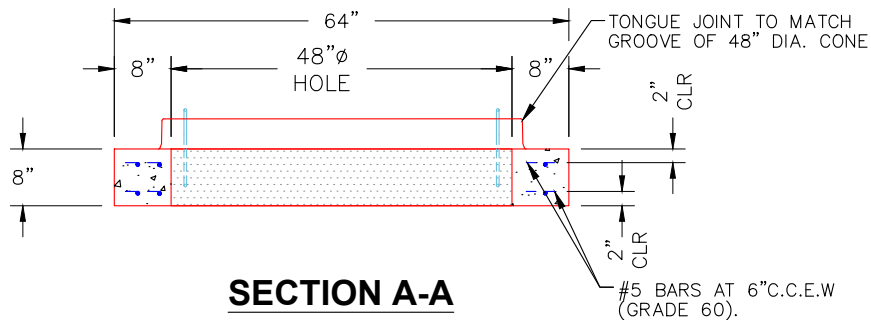

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (DOUBLE MAT) (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1535 lb
Volume (Net): 0.39cu.yd
