

Contractor: Cleary Construction, Inc.


TECH: Jared - F

Plant: 100




Slack: 0.08"


Structure Total: 7874 lb

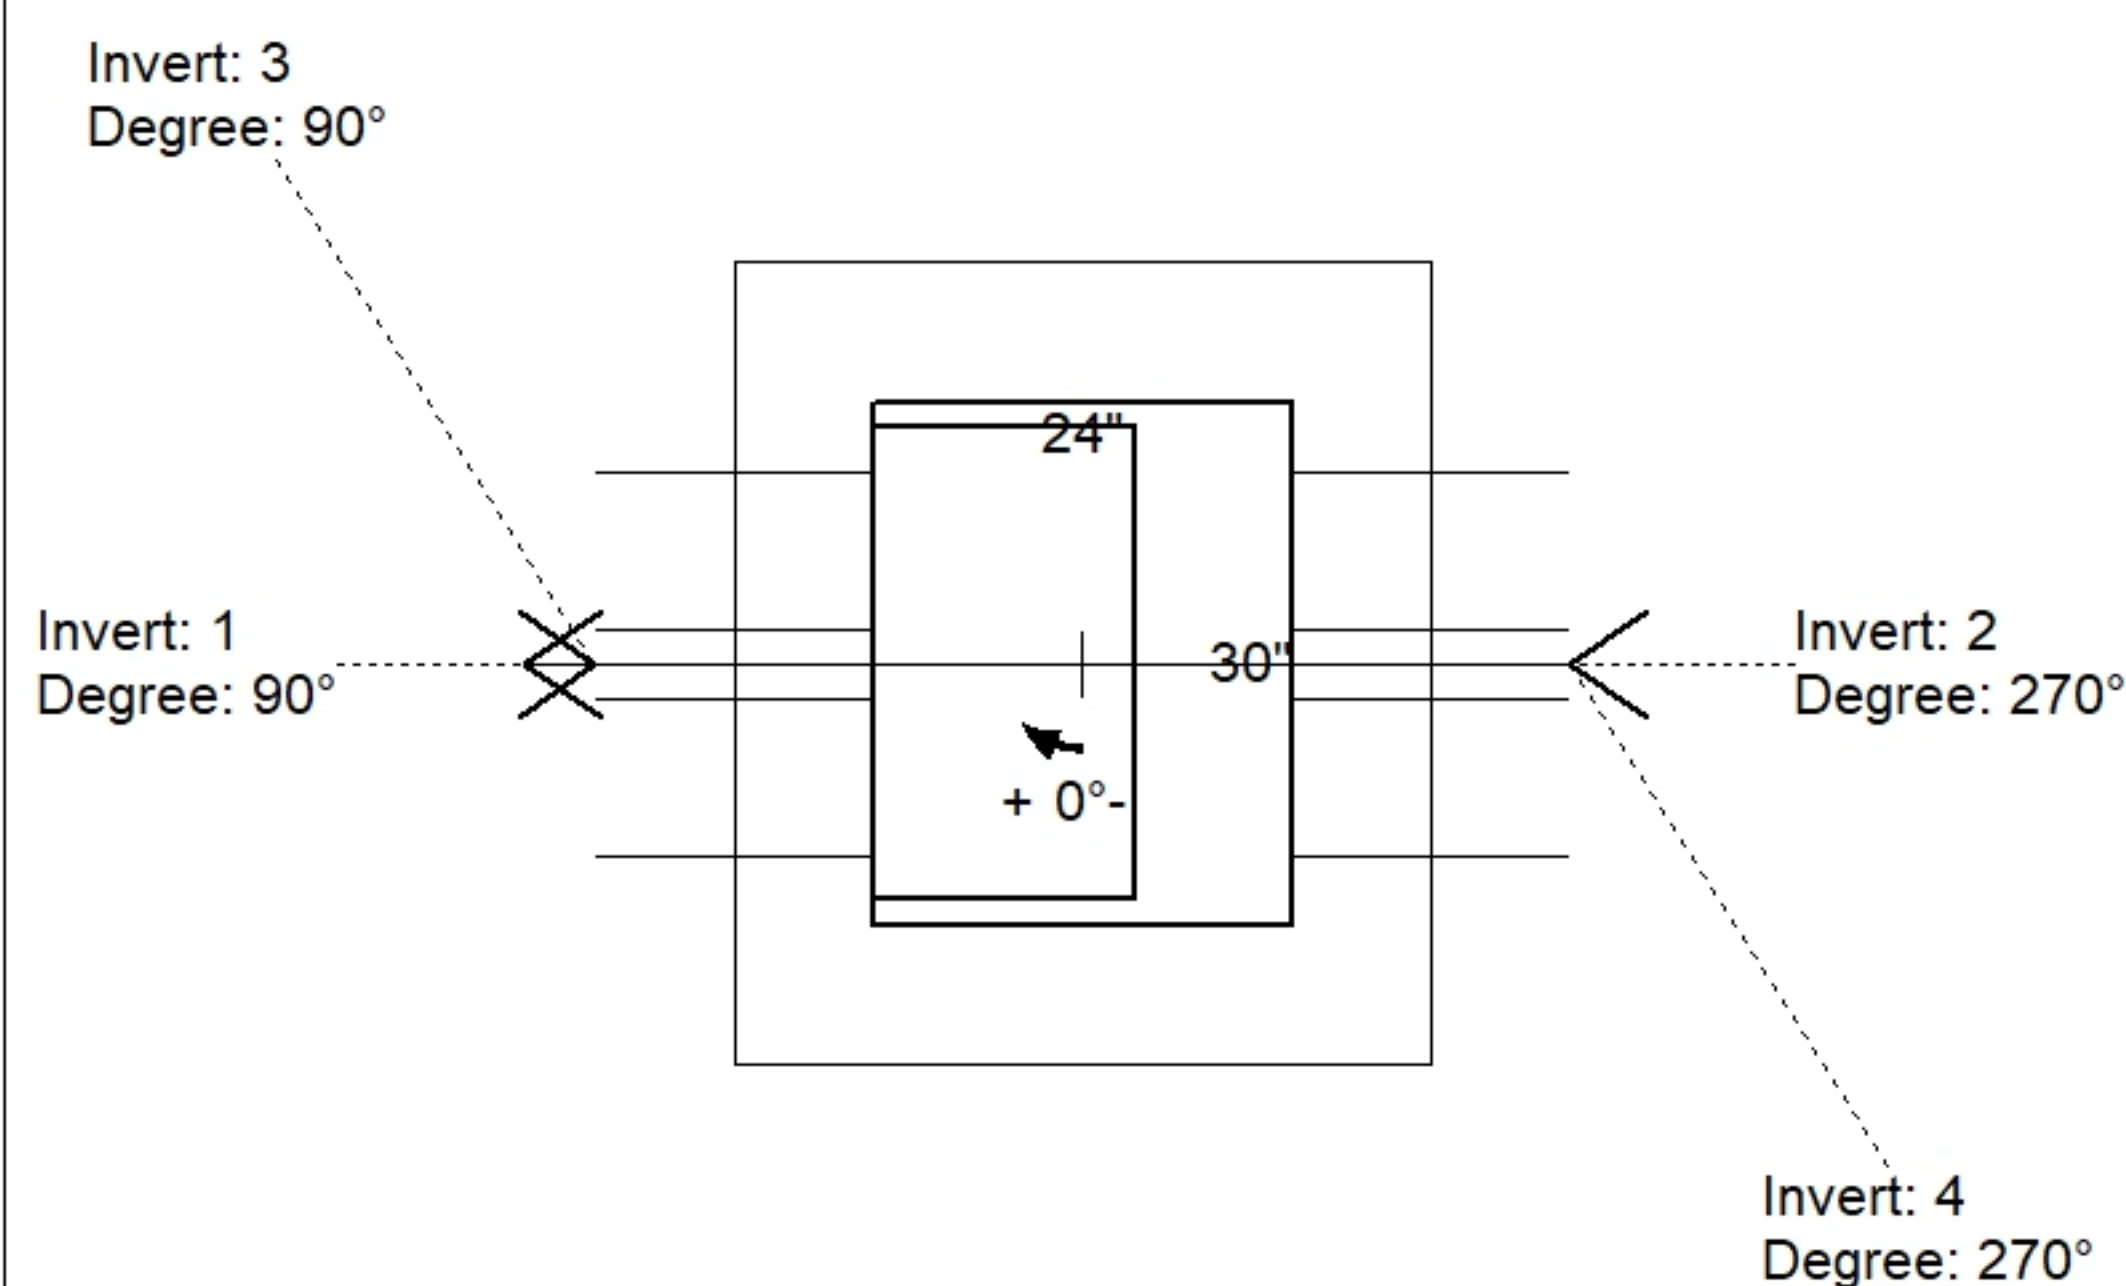

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	776.34'							
Reducer								
Invert 1	769.5'	90°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	769.5'	270°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3	774.333'	90°	4" WEEP HOLE	4"	4"	Hole 4	7.996"	P2
Invert 4	774.333'	270°	4" WEEP HOLE	4"	4"	Hole 4	7.996"	P2
Invert 5								
Invert 6								
Invert 7								
Invert 8								

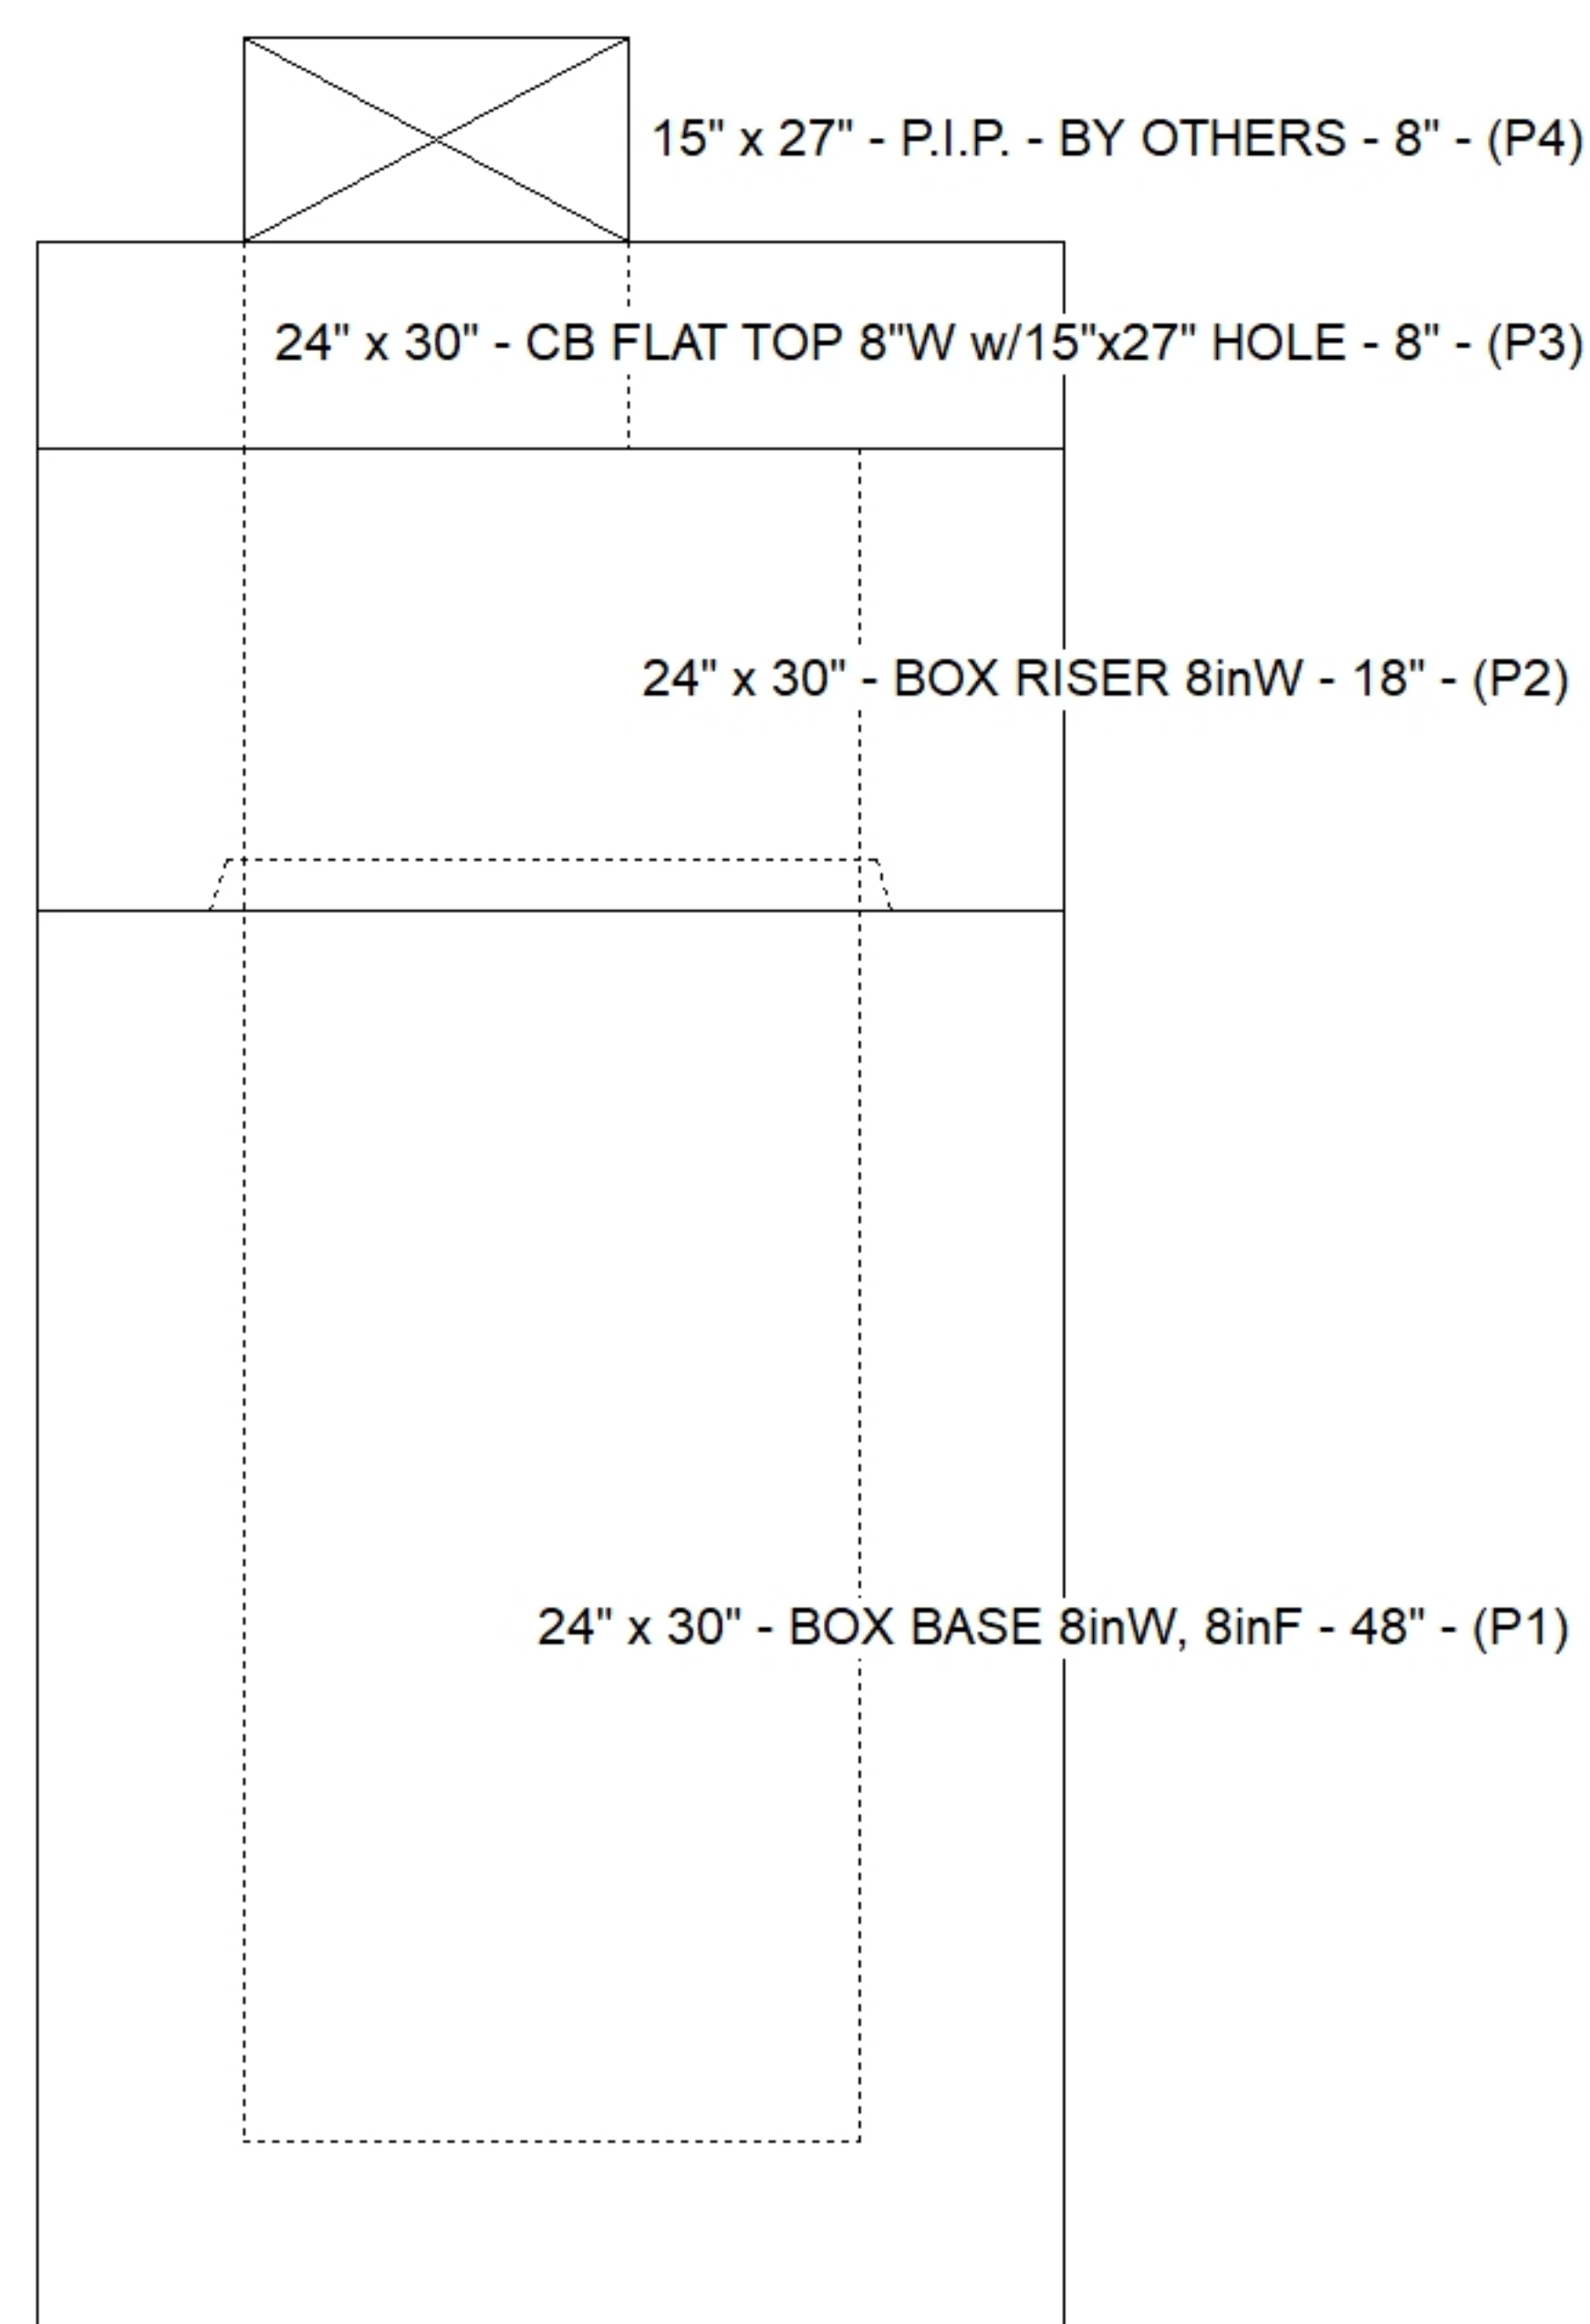

Default - Interior Dimensions

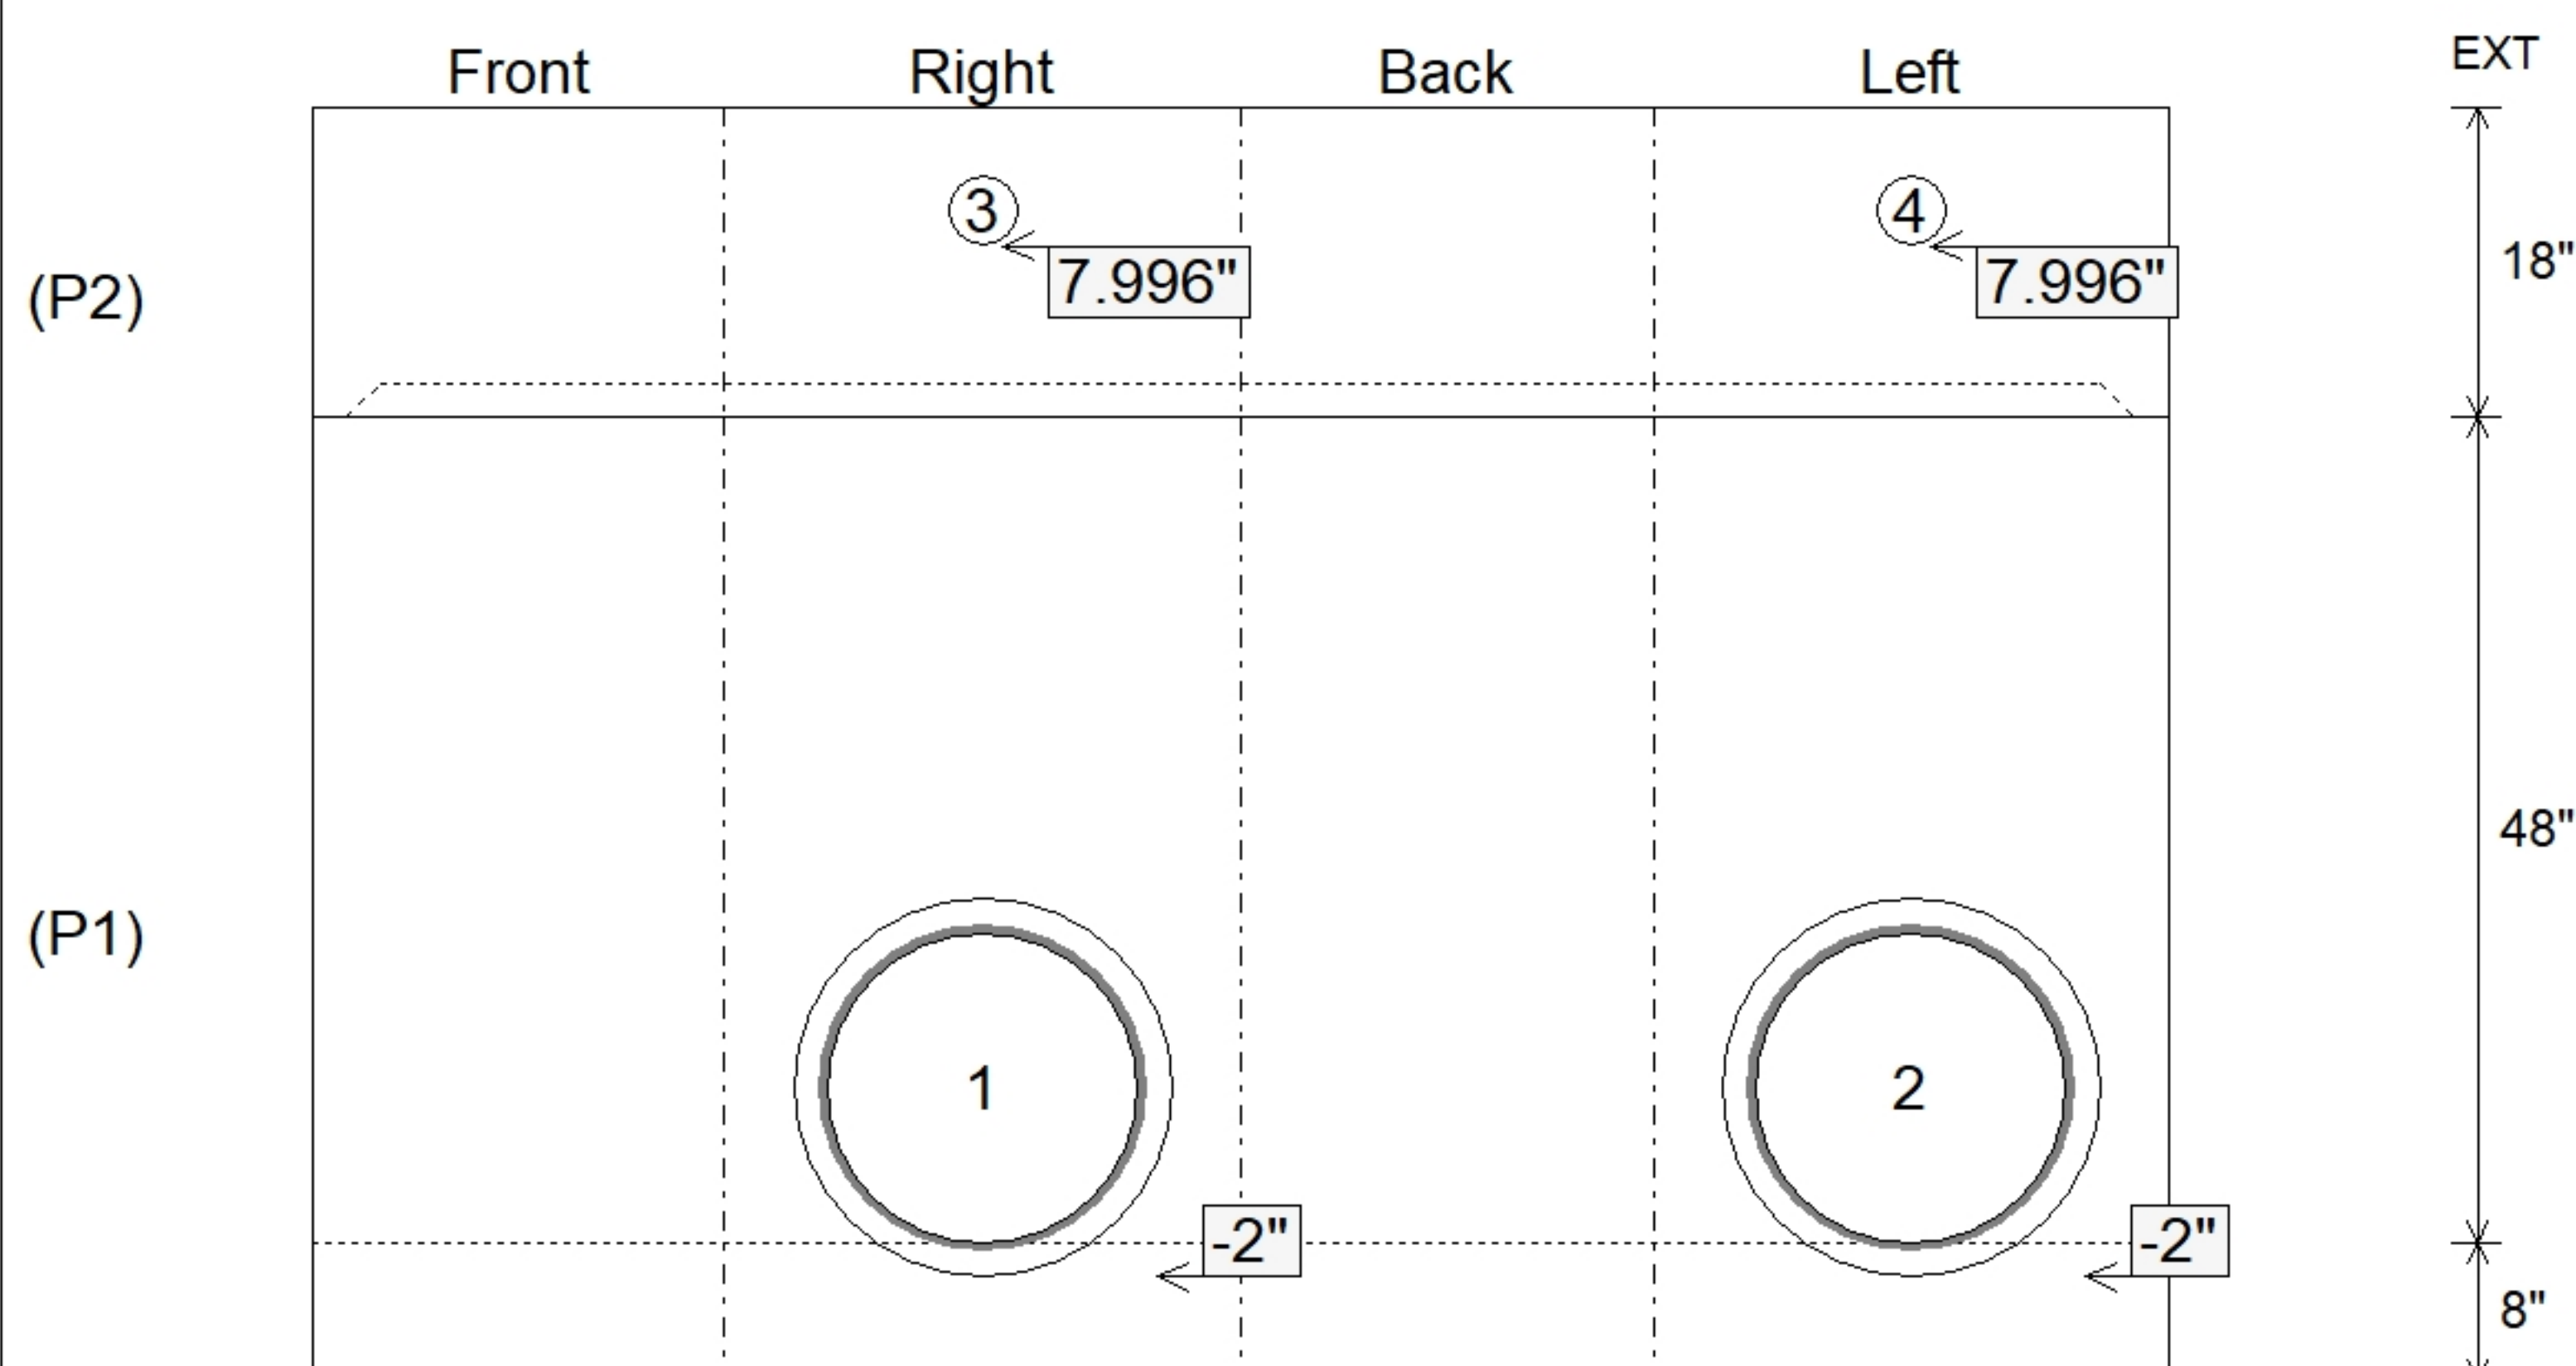

Submittal Drawing
8/17/2026 2:01:37 PM

SUBMITTAL
APPROVED BY:
