

Contractor: Cleary Construction, Inc.

TECH: Jared - F

Plant: 100




Slack: 0"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 40"
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 18

0 lb
6370 lb
0 lb
0 lb


Structure Total: 6370 lb

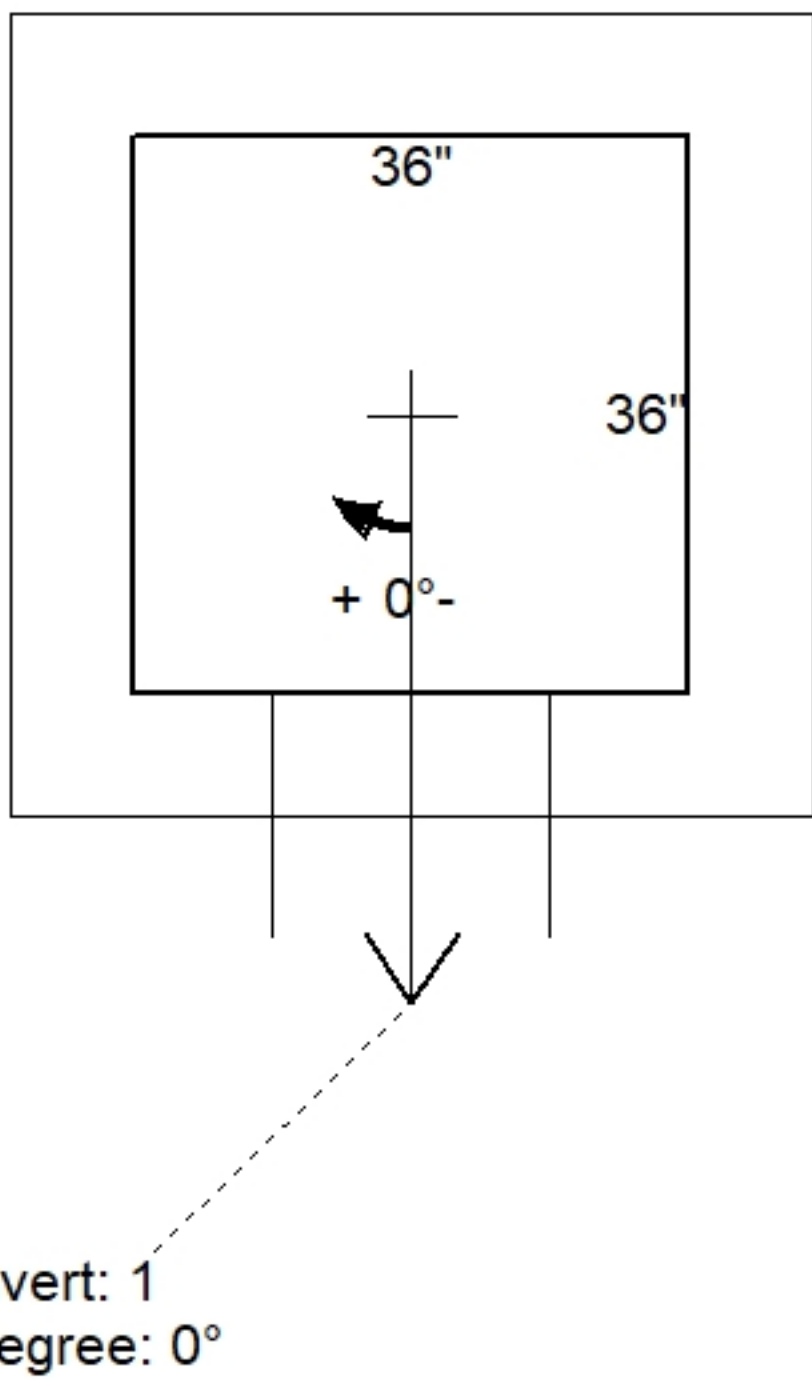

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	797.73'							
Reducer								
Invert 1	793.73'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

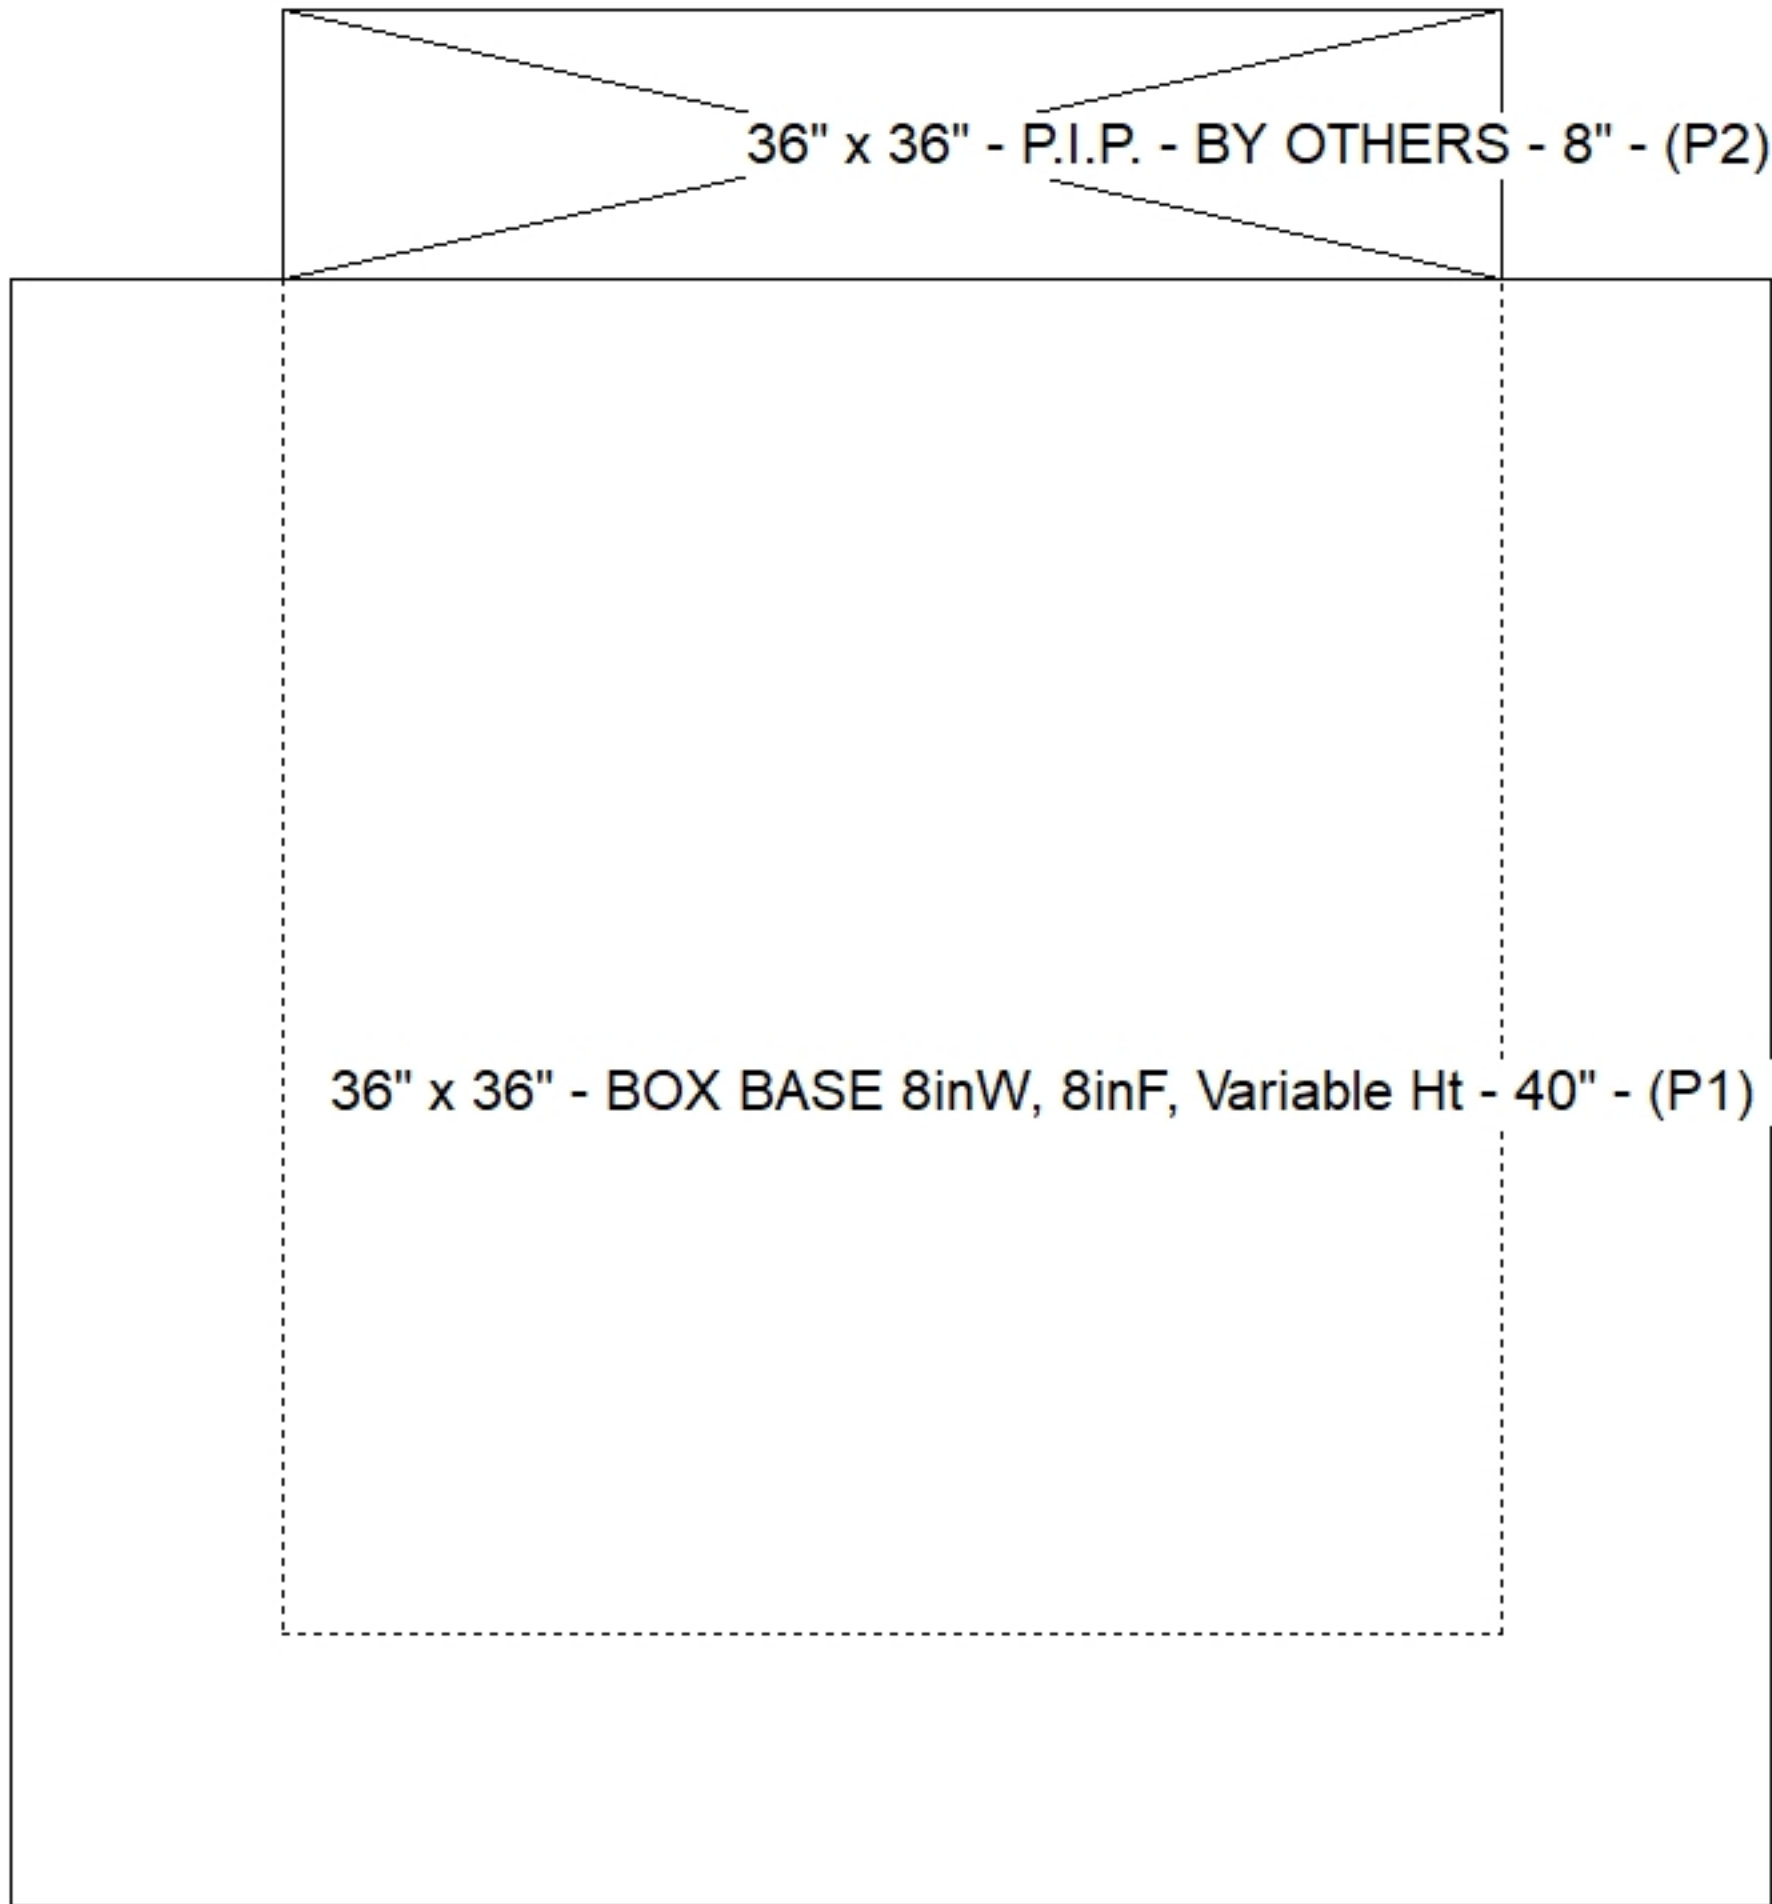

Default - Interior Dimensions

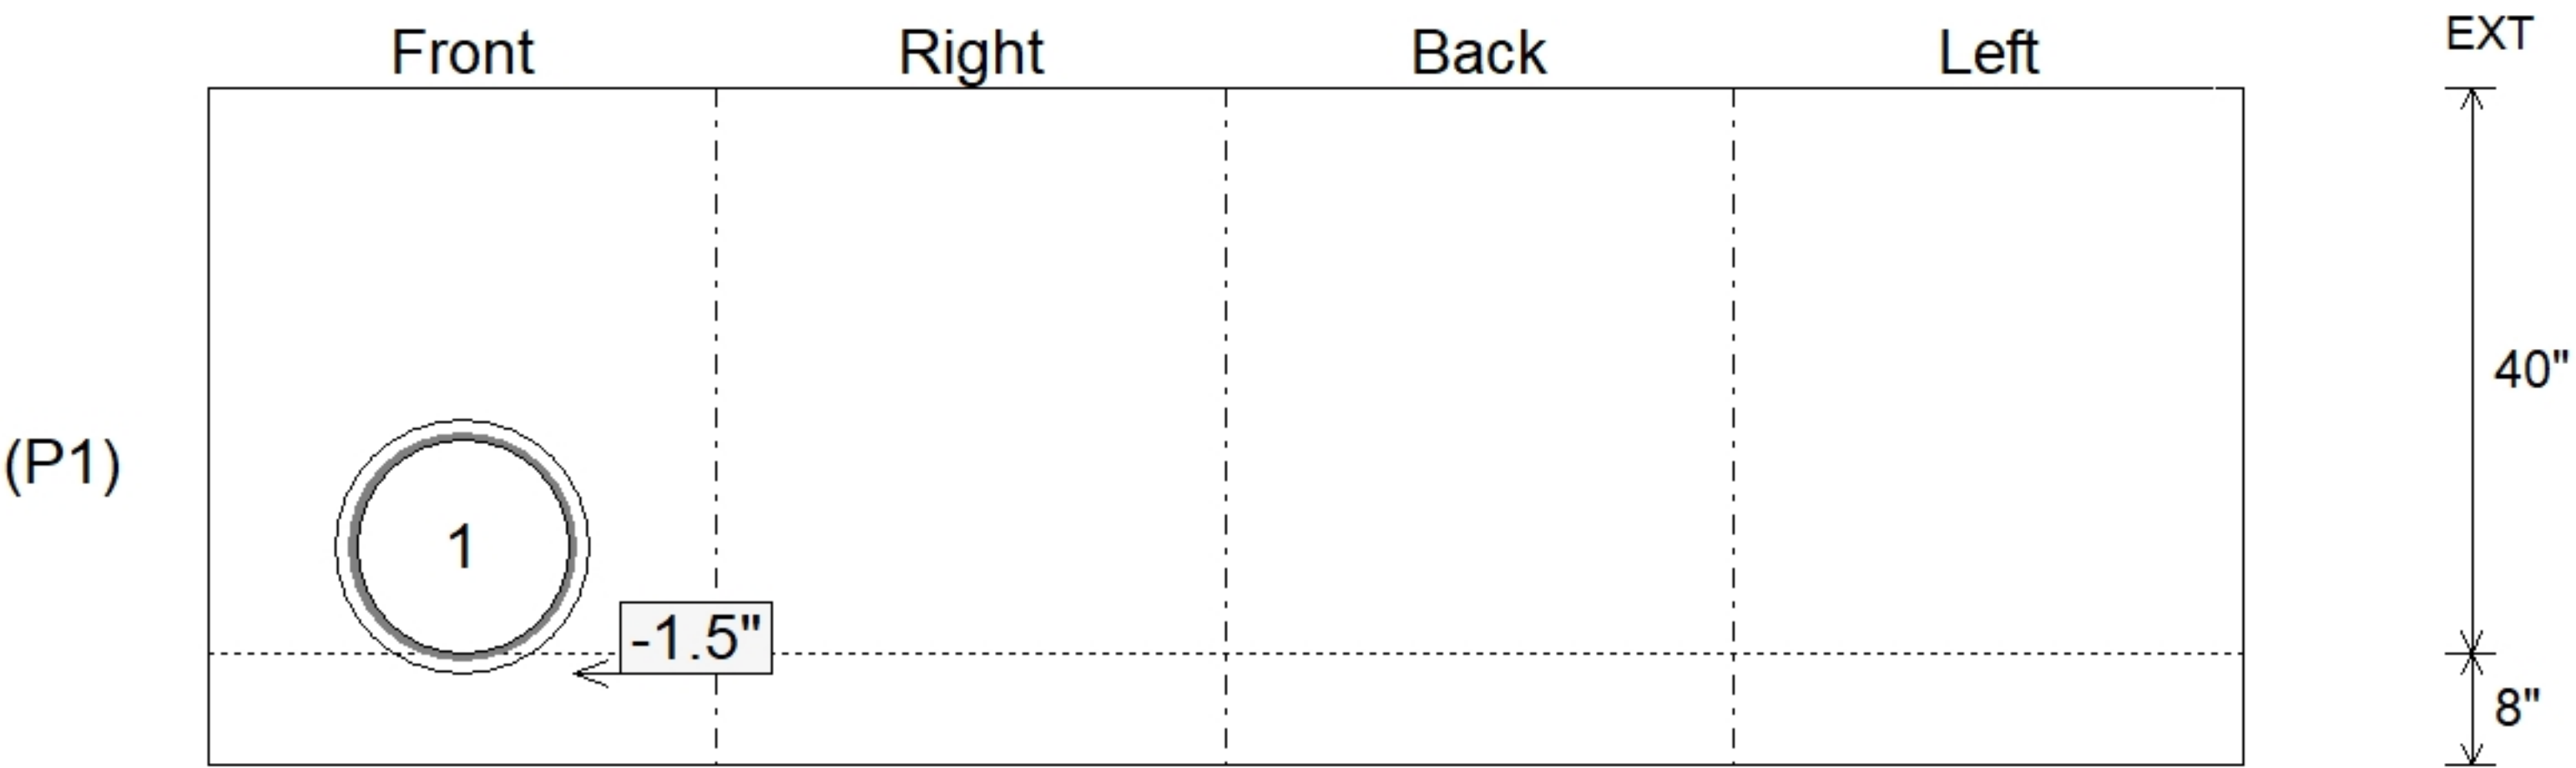

Submittal Drawing
8/17/2026 2:01:24 PM

SUBMITTAL
APPROVED BY:
