

Contractor: Cleary Construction, Inc.



TECH: Jared - F

Plant: 100




Slack: 2.84"

Structure Total: 5702 lb

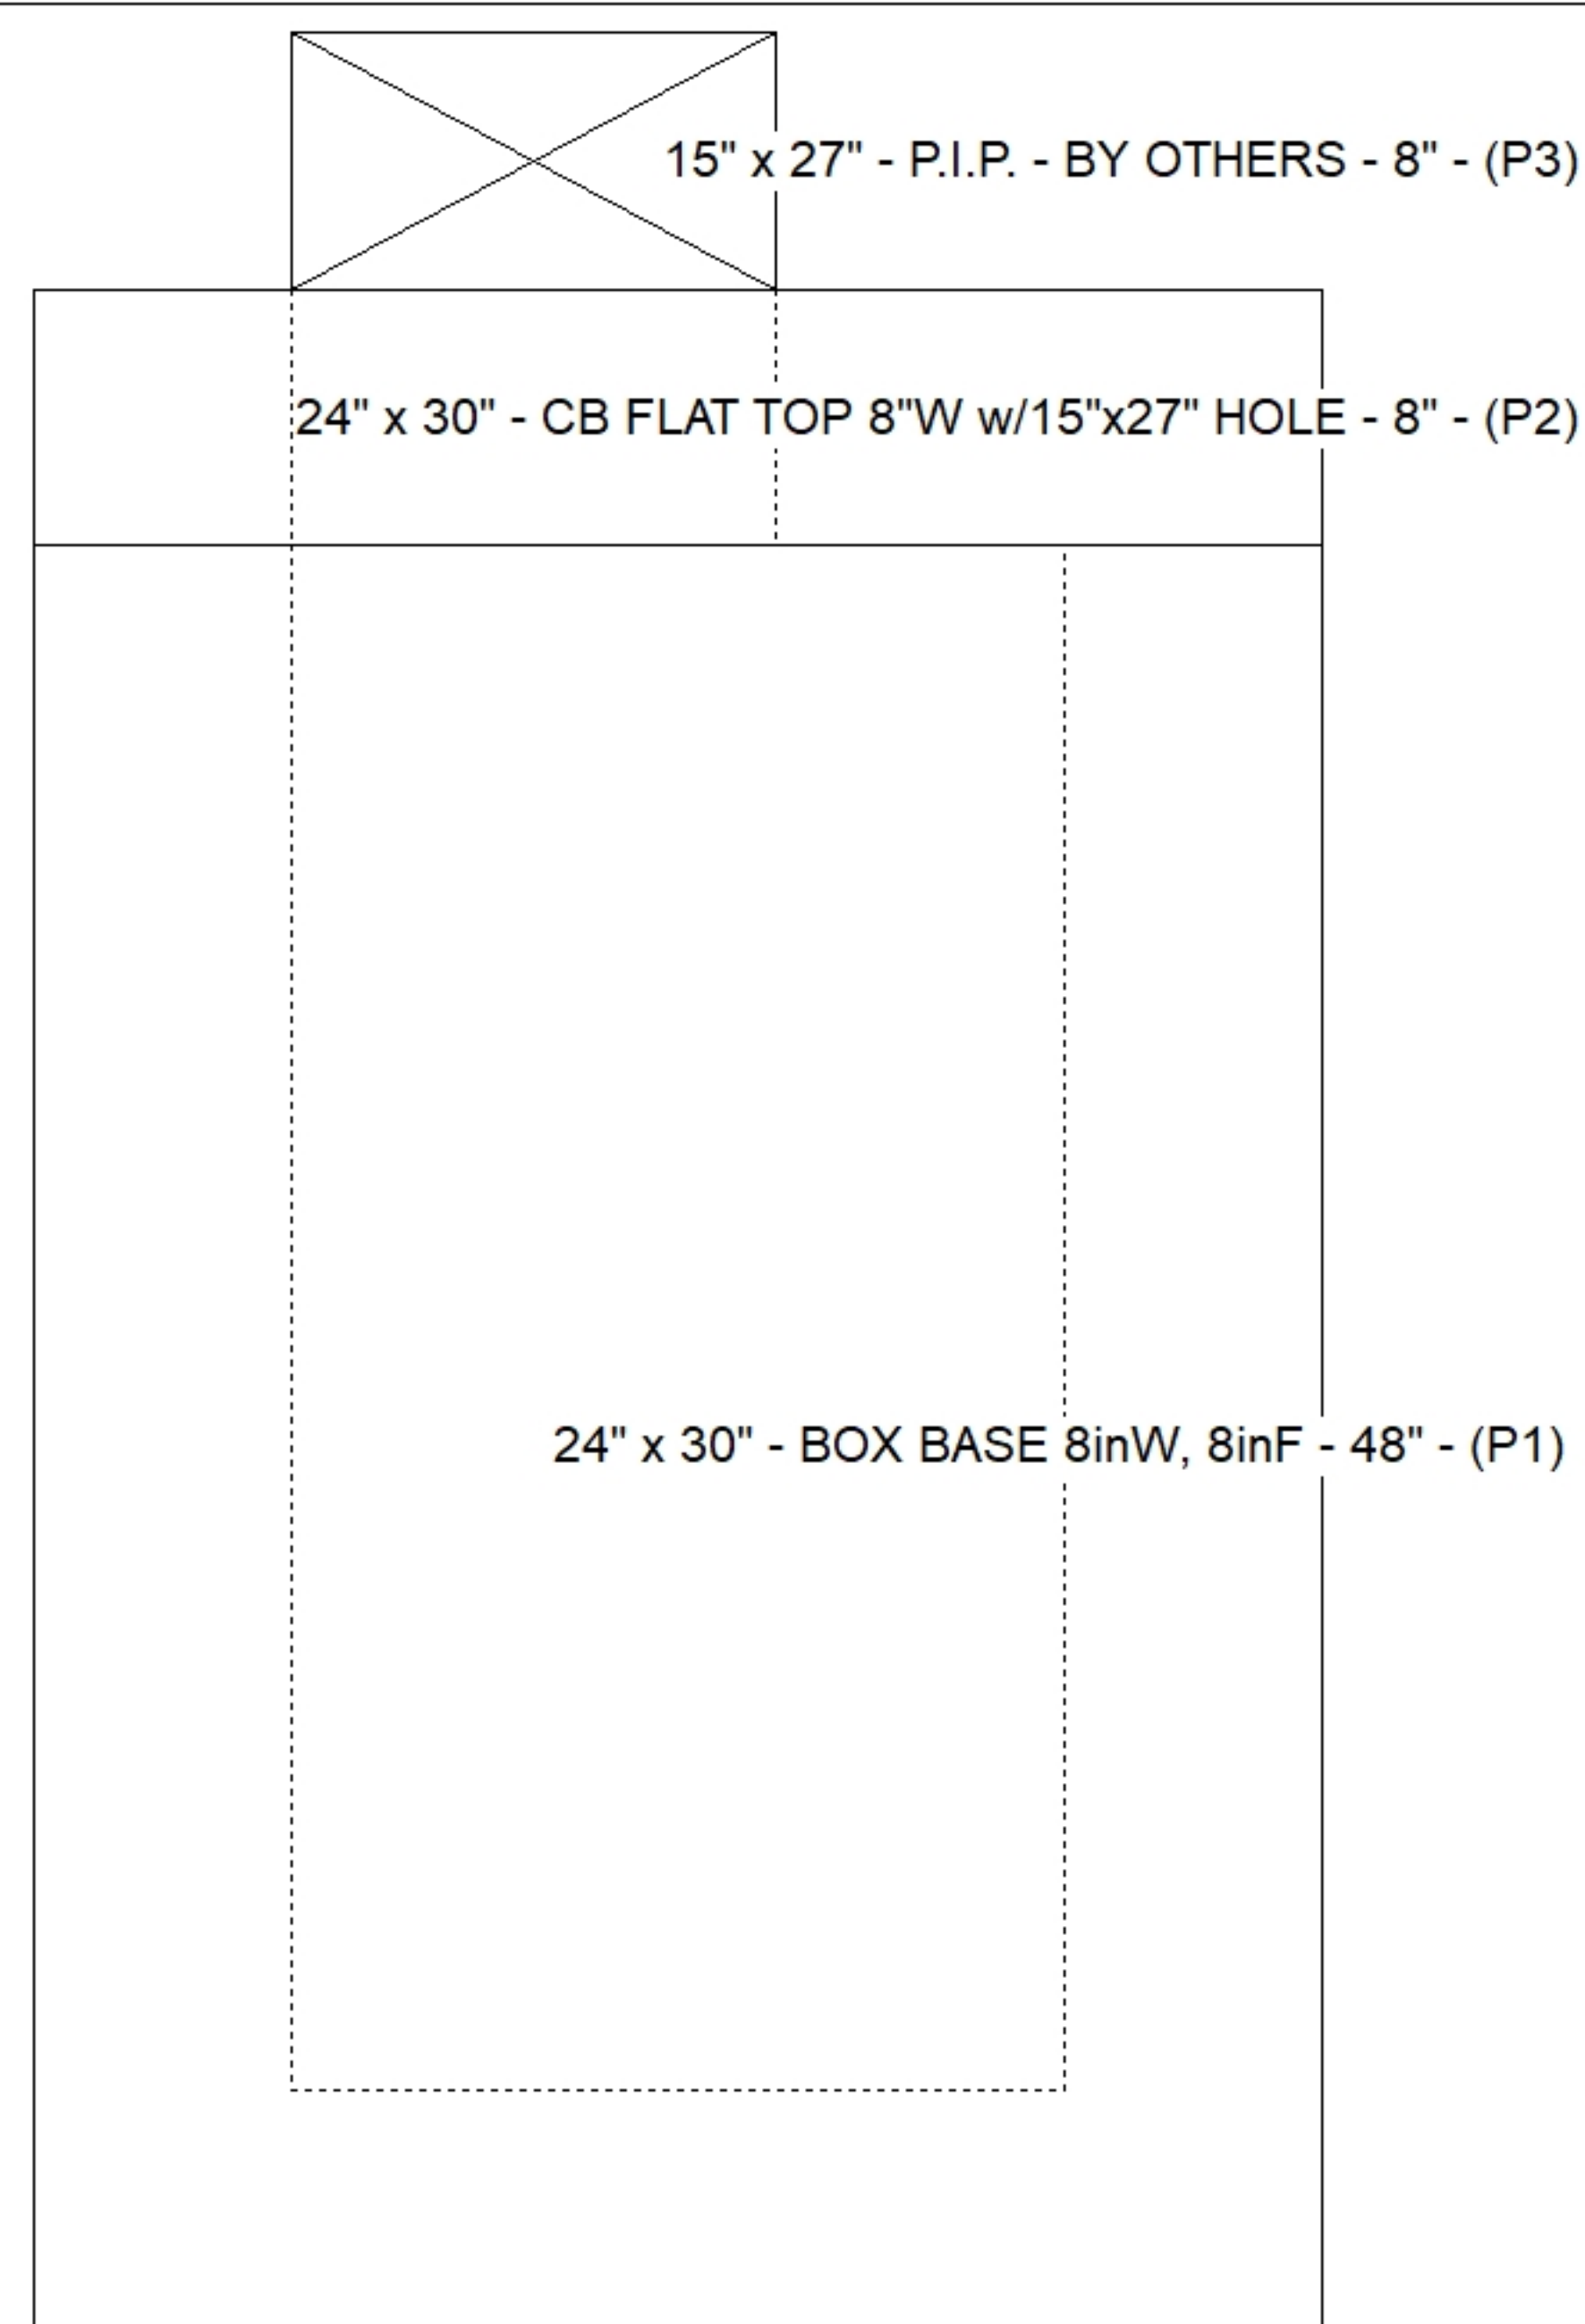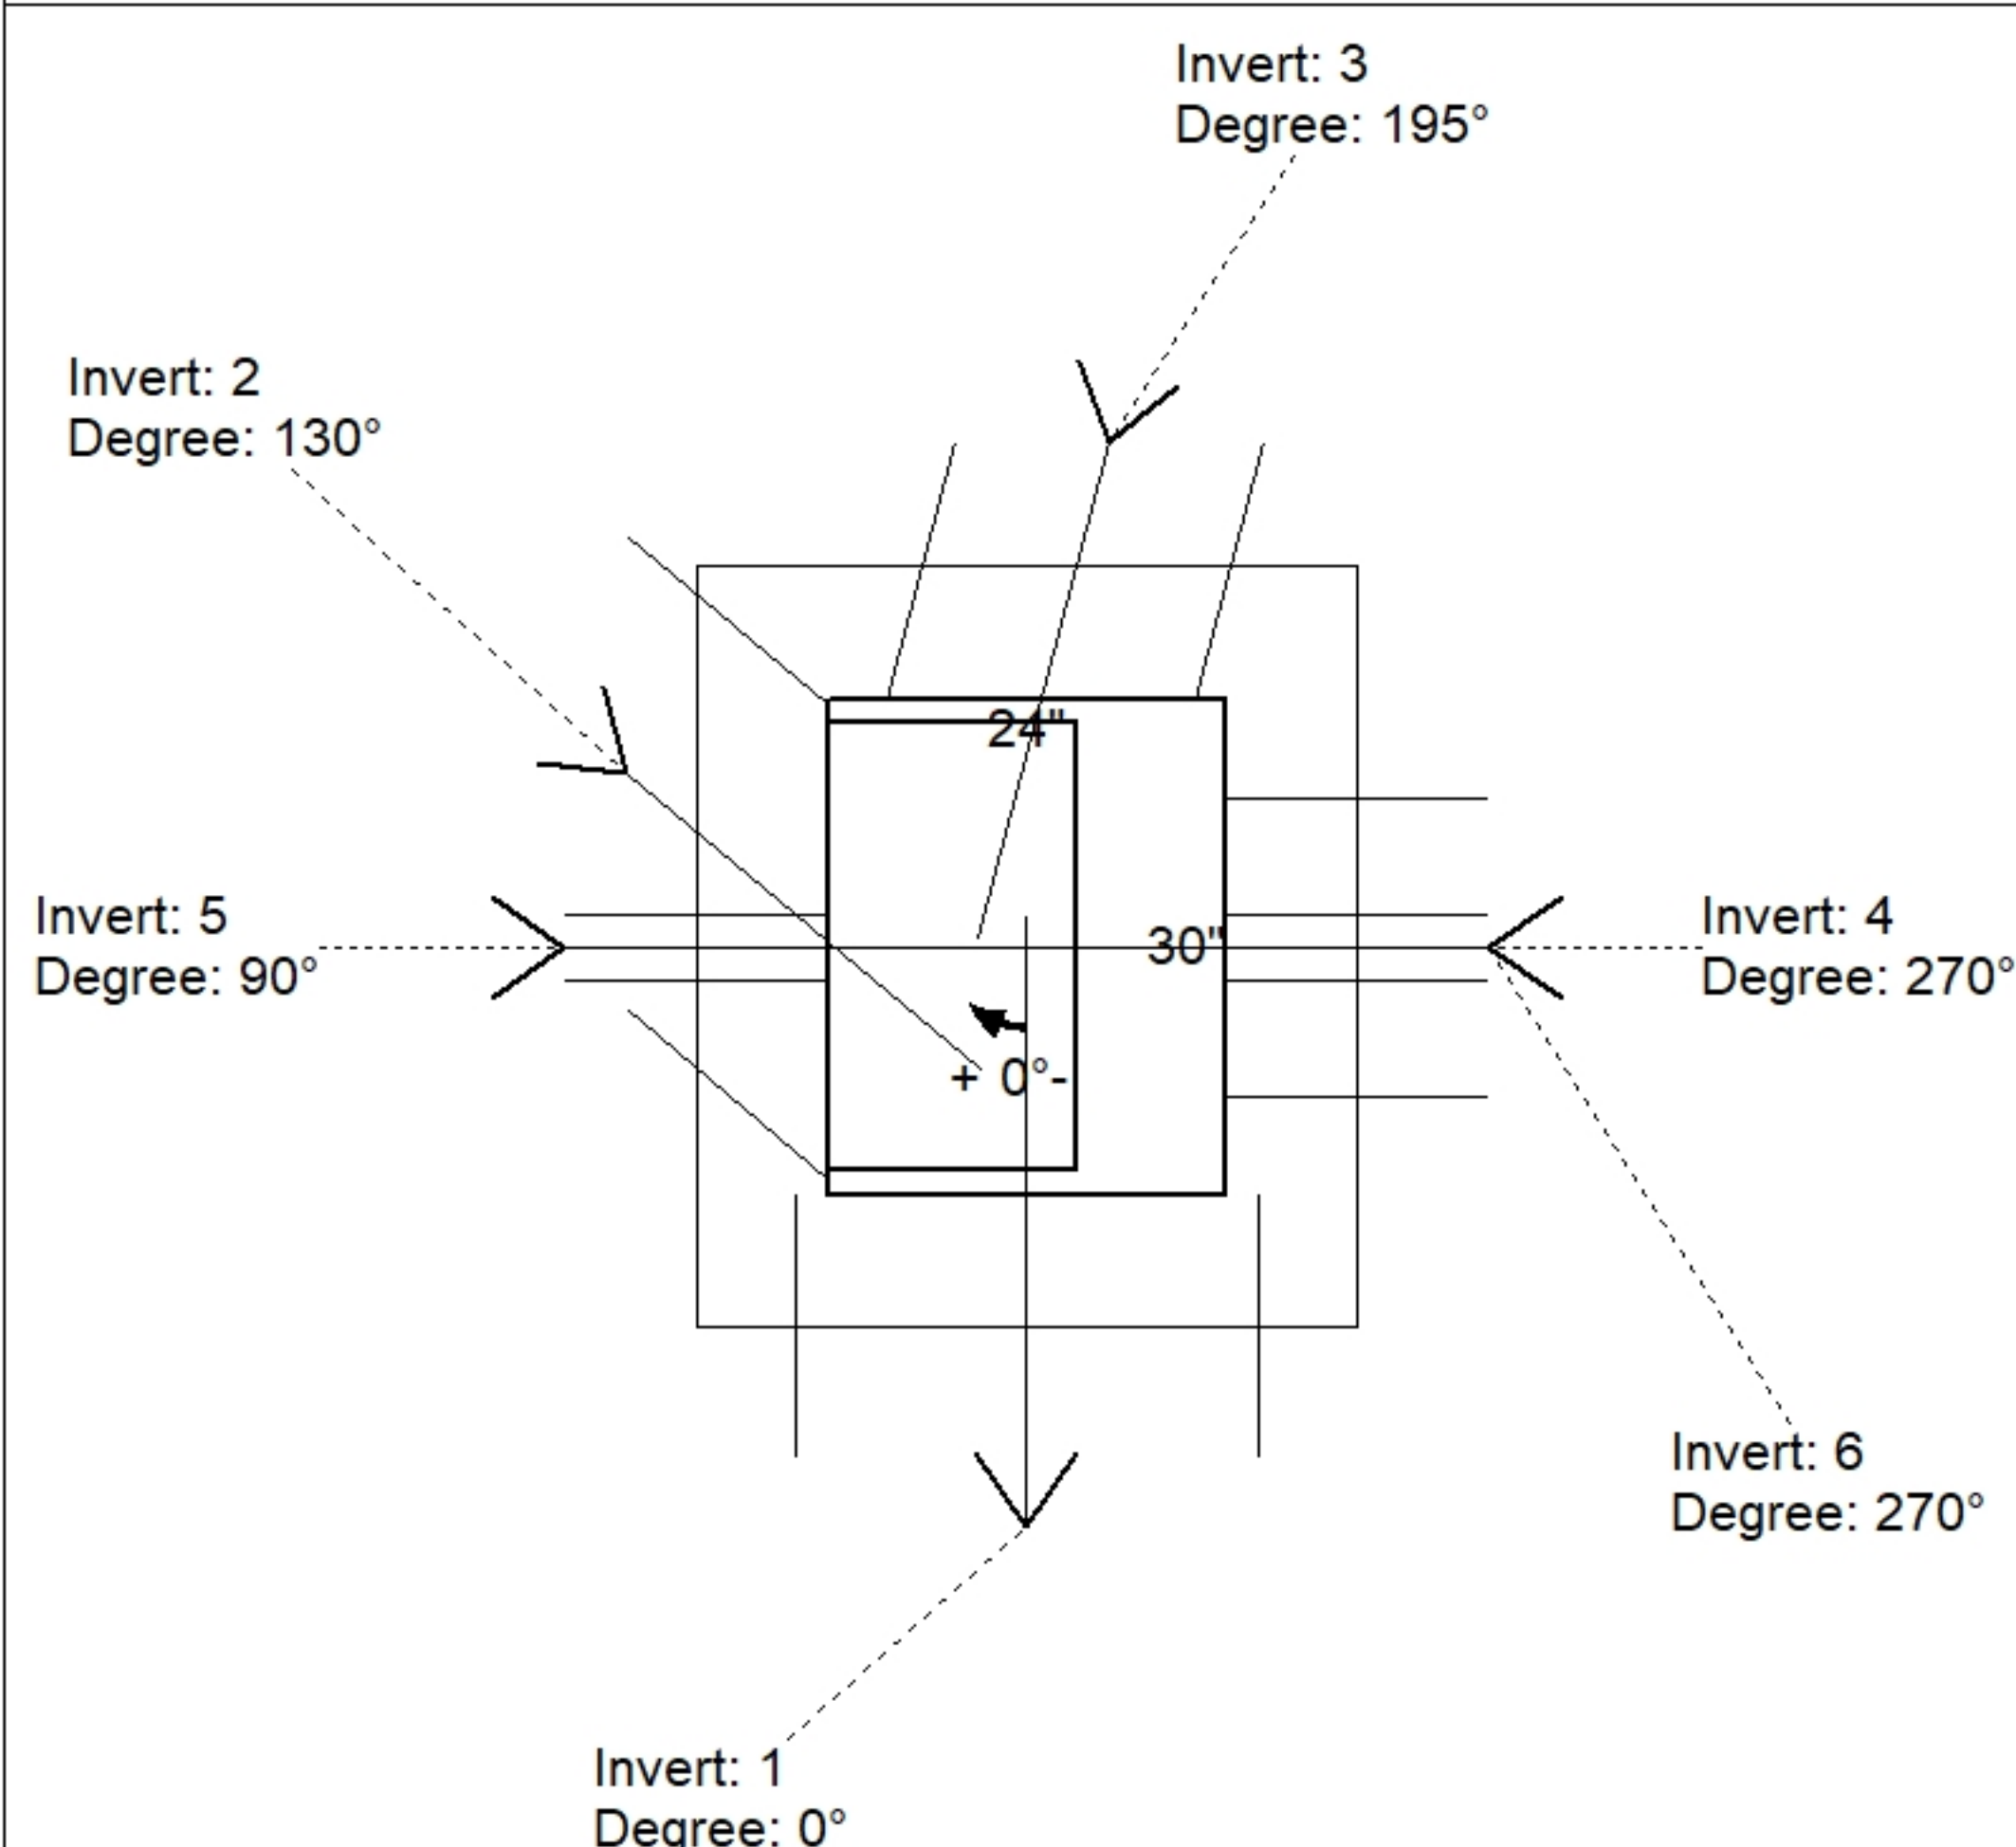

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	798.29'							
Reducer								
Invert 1	792.72'	0°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	792.72'	130°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3	792.72'	195°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 4	792.72'	270°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 5	795.89'	90°	4" WEEP HOLE	4"	4"	Hole 4	38.04"	P1
Invert 6	795.89'	270°	4" WEEP HOLE	4"	4"	Hole 4	38.04"	P1
Invert 7								
Invert 8								

Default - Interior Dimensions

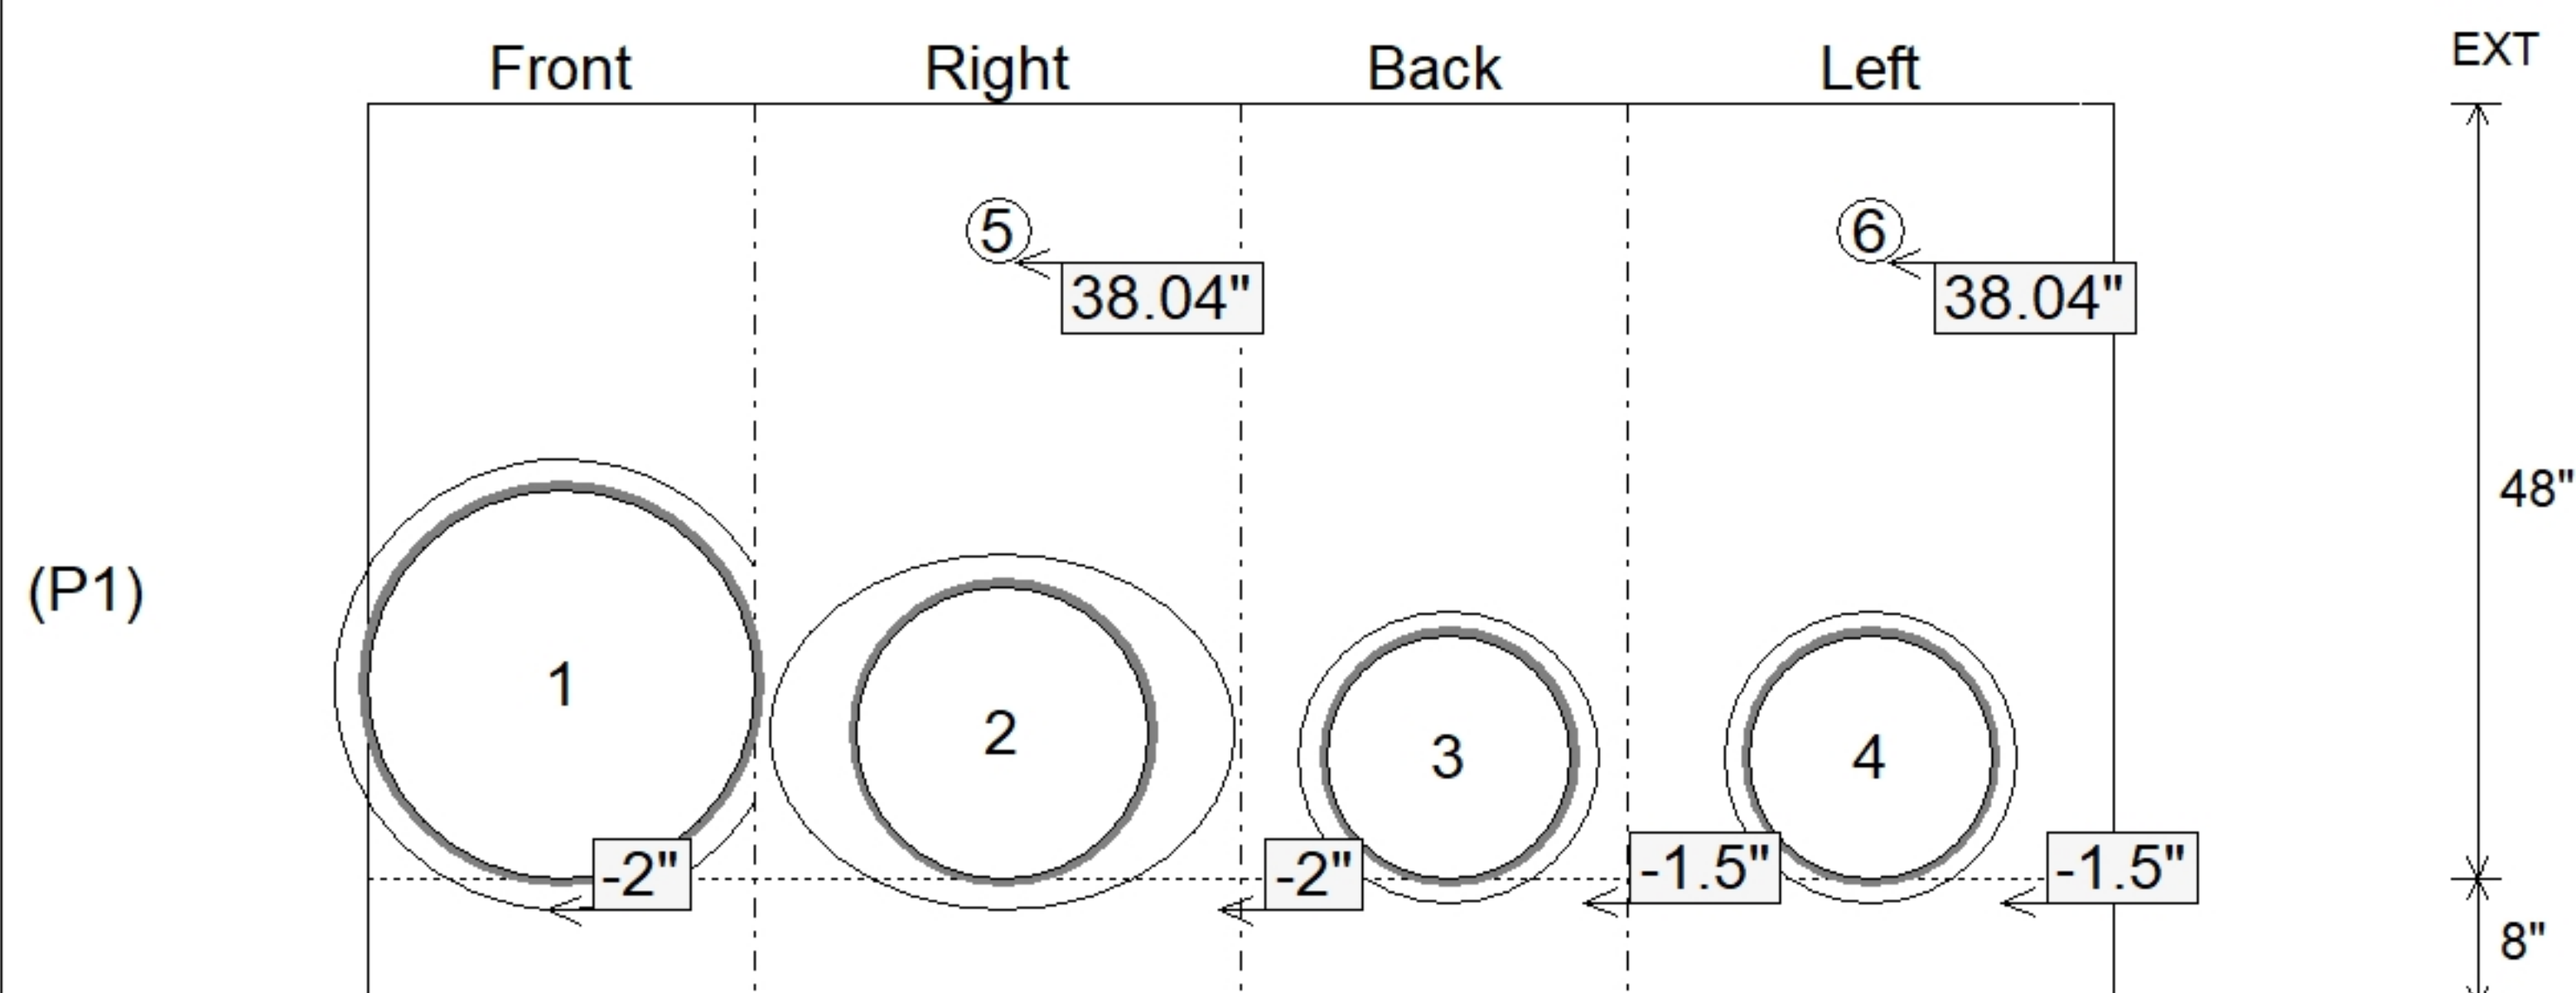

SUBMITTAL
APPROVED BY:
