

Job Name: 26-1644 - BGMU Miox Feed Lines	Plant: 100	Tech: Jared - F	
Job Location: Bowling Green, KY Contractor: Scott & Ritter, Inc.	3/31/2026 10:56:22 AM	PC: C. Goff	

Structure ID: JB-8-4 ST-JB

P1 P.I.P. BY OTHERS - BTM SLAB

P3) 60" - MH FLAT TOP w/ 36" CASTING CAST IN - 12"	3331 lb
P2) 60" - MH RISER Custom Ht - 65"	6146 lb
P1) 60" - P.I.P. BY OTHERS - BTM SLAB - 0"	0 lb
1) CASTING - PAMREX 36" F/C	393 lb
2) 60" - Conseal CS-102 1.00"	0 lb
1) 36" - Conseal CS-102 1.00"	0 lb
2) SQ. Hole - 14"x45"	0 lb
Structure Total:	9870 lb



Structure Notes:
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO INVERT CHANNEL.
 4. CASTING BY ICAST (PAMREX 36" F/C)

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER (As .18)


Rim: 479.53' Rim to Invert: 6.5' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)

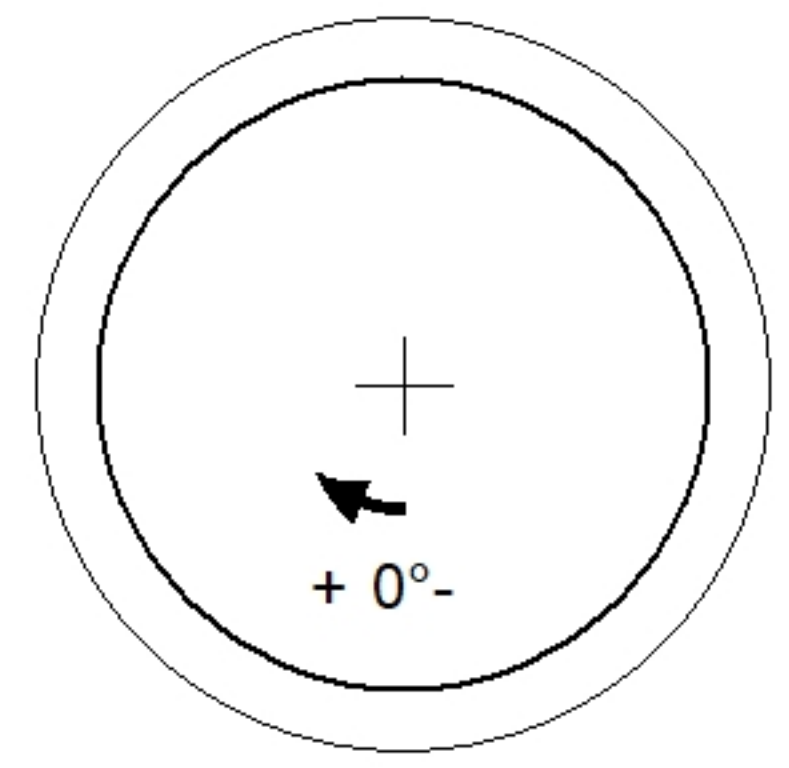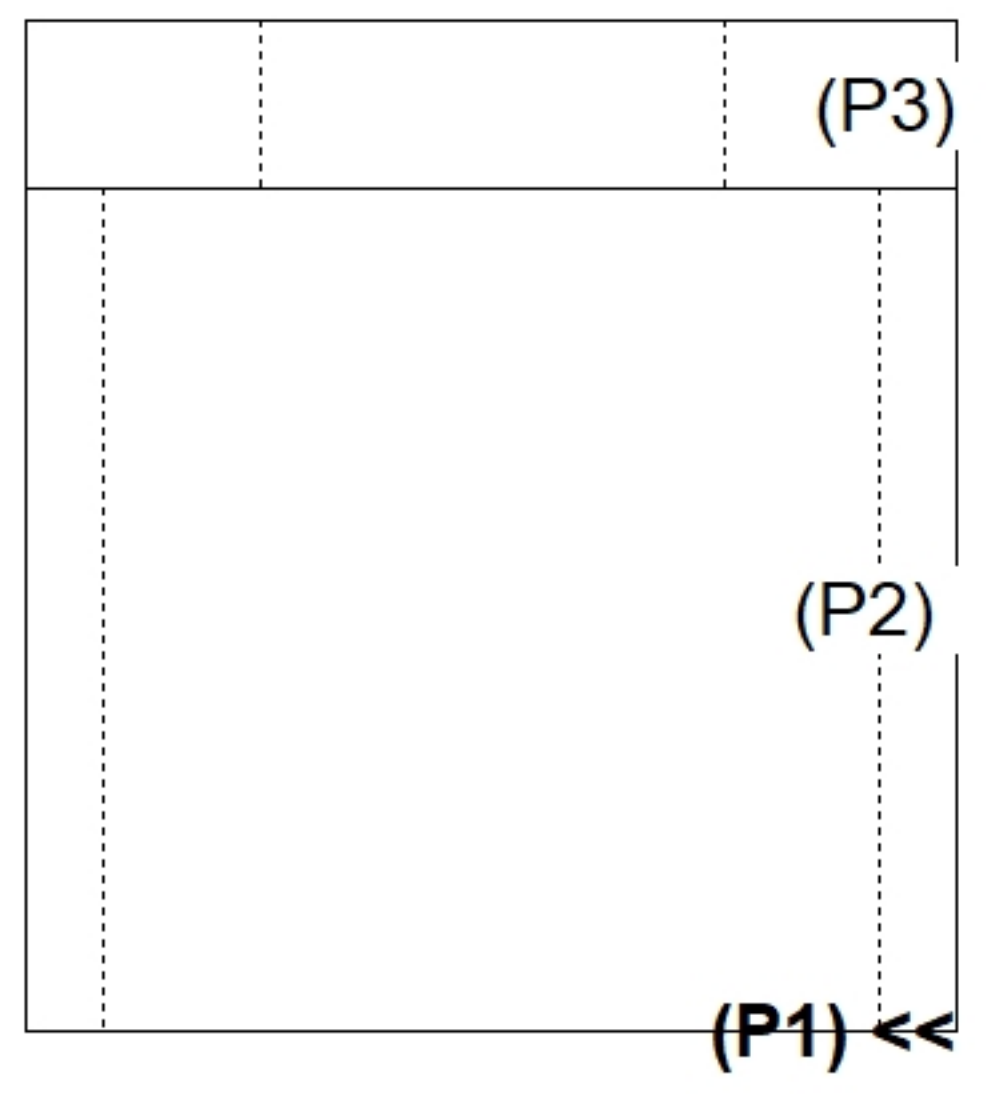

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 0"	Height (Int): 0" Height (Ext): 0"	Weight (Net): 0 lb Volume (Net): 0cu.yd
----------------------------------	-------------------------------	--	--------------------------------------	--
