

Contractor: Weddle Enterprises, Inc


TECH: Jared - F

Plant: 100





Slack: 0.72"

Structure Total: 4853 lb

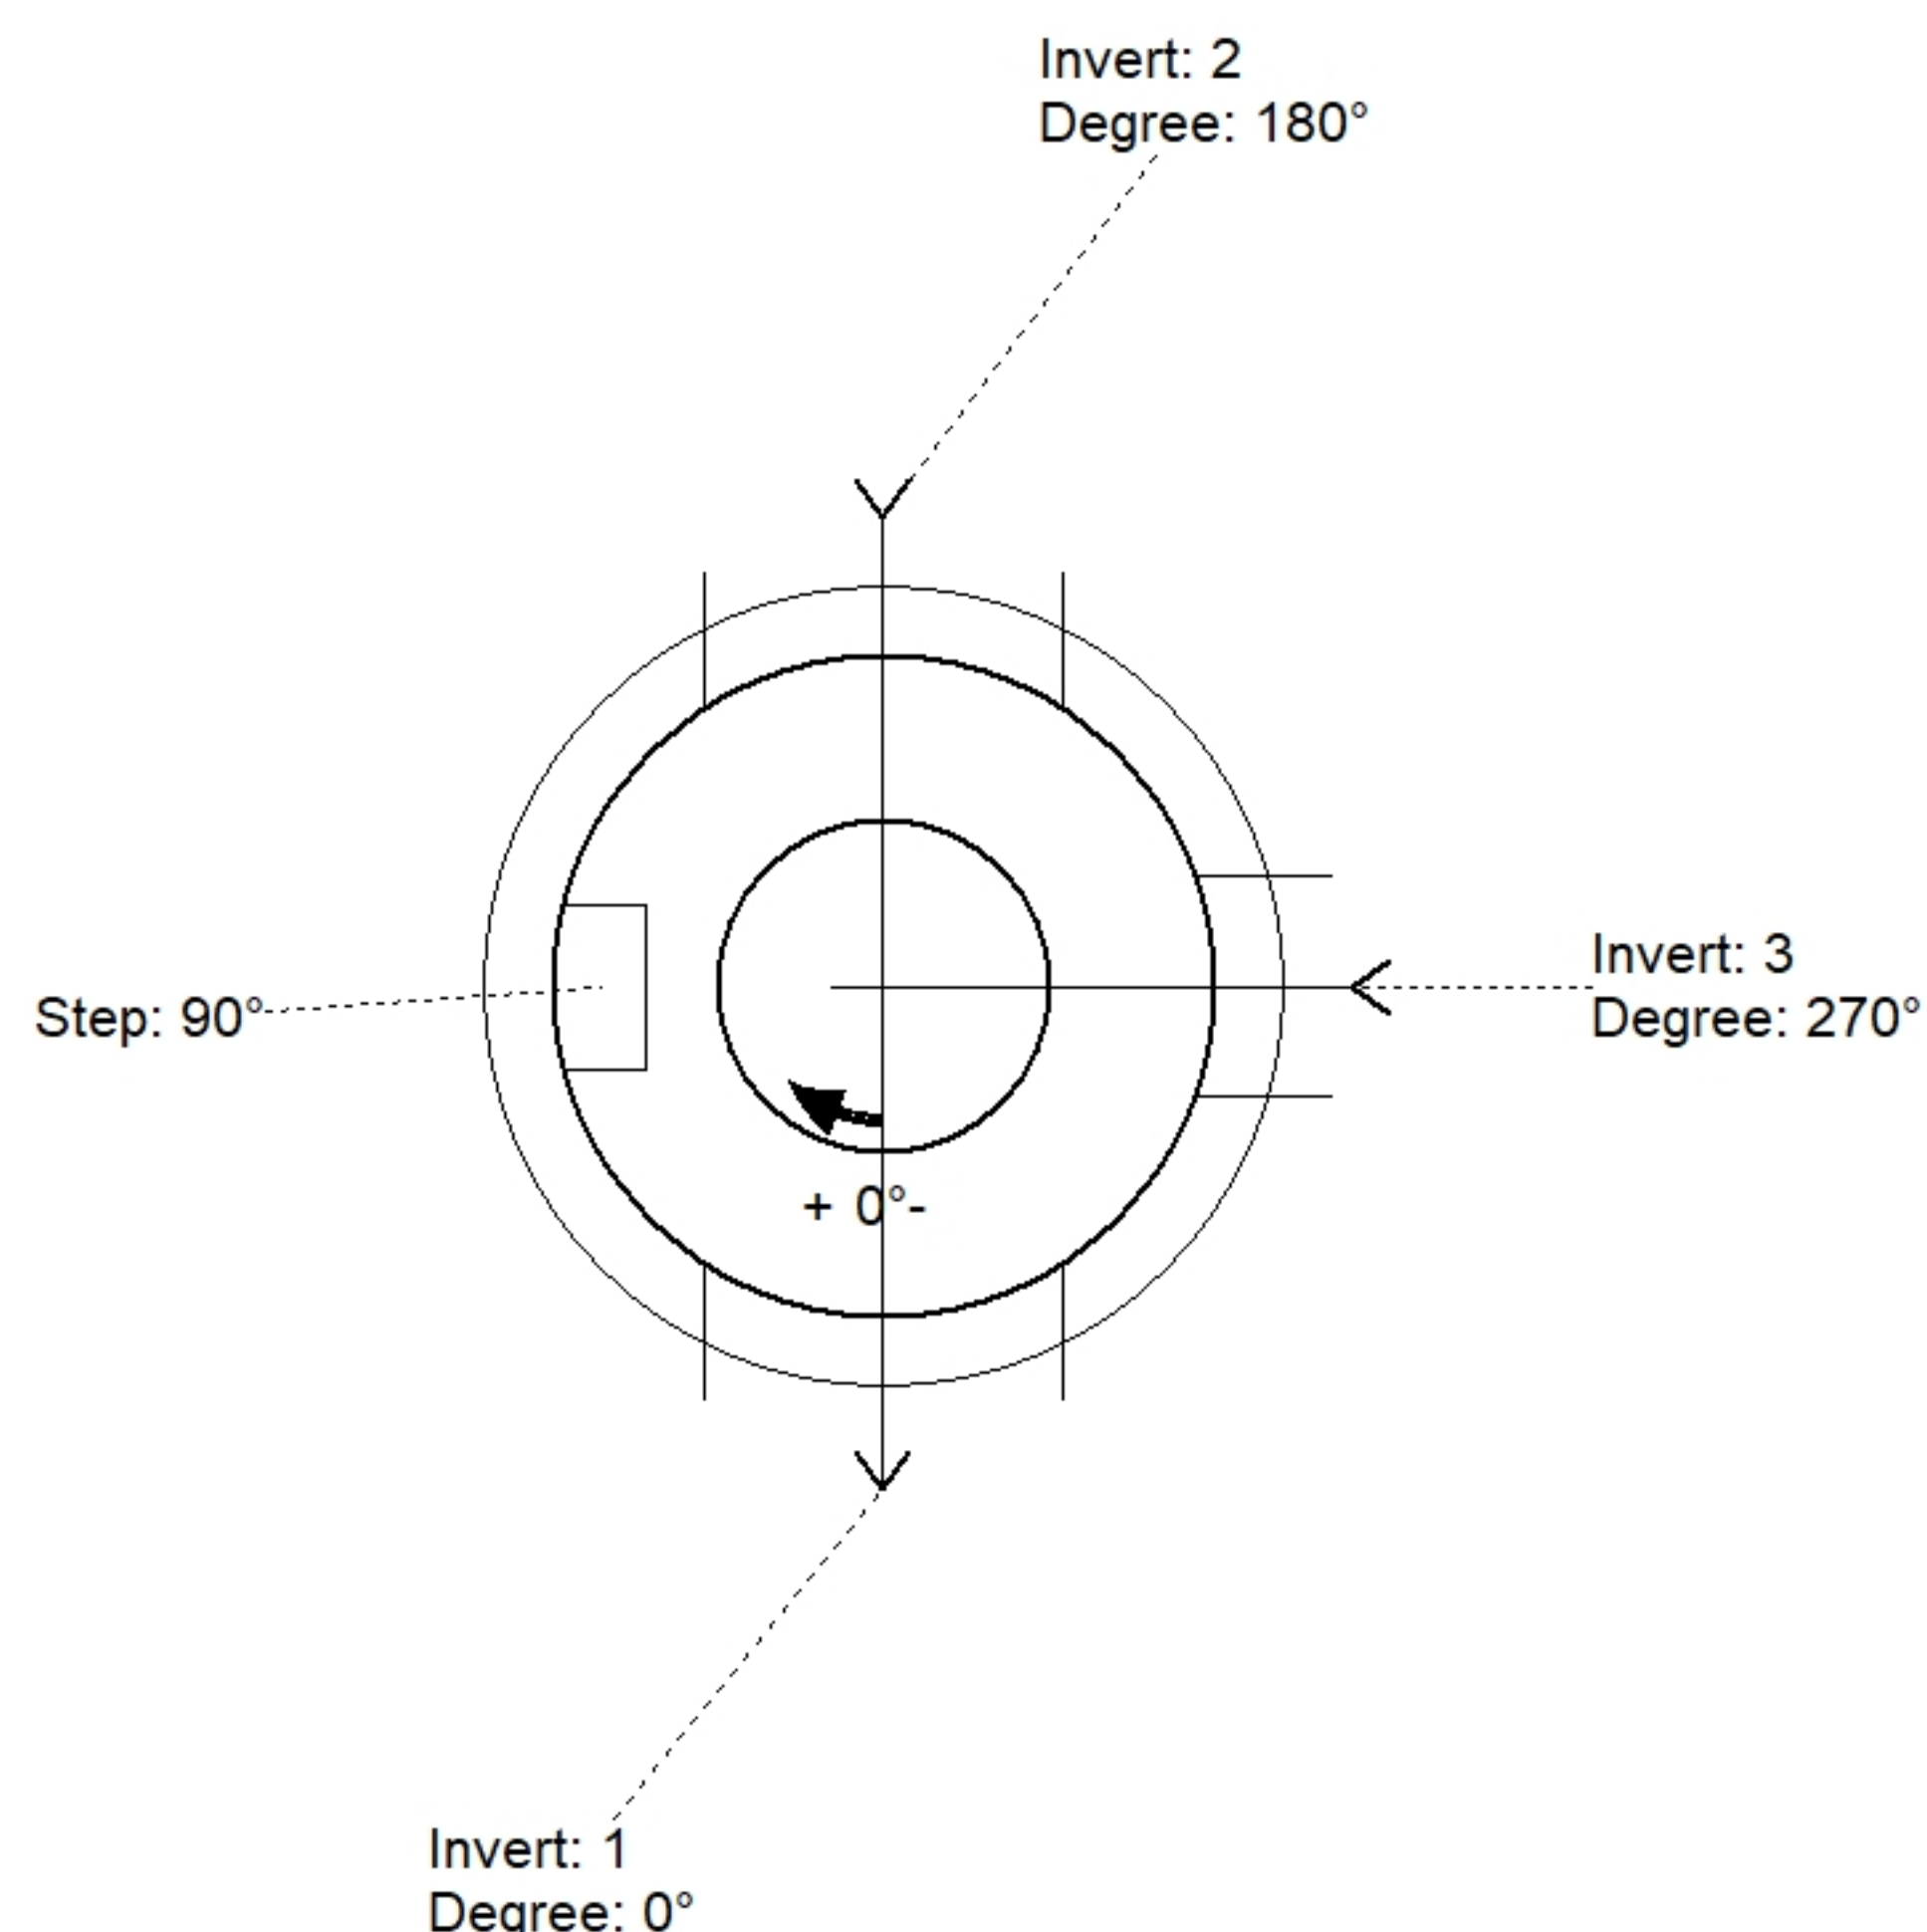

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	1076'							
Reducer								
Invert 1	1072.19'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	1072.19'	180°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 3	1073.43'	270°	12" HDPE	14.5"	16"	Hole 16	13.63"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

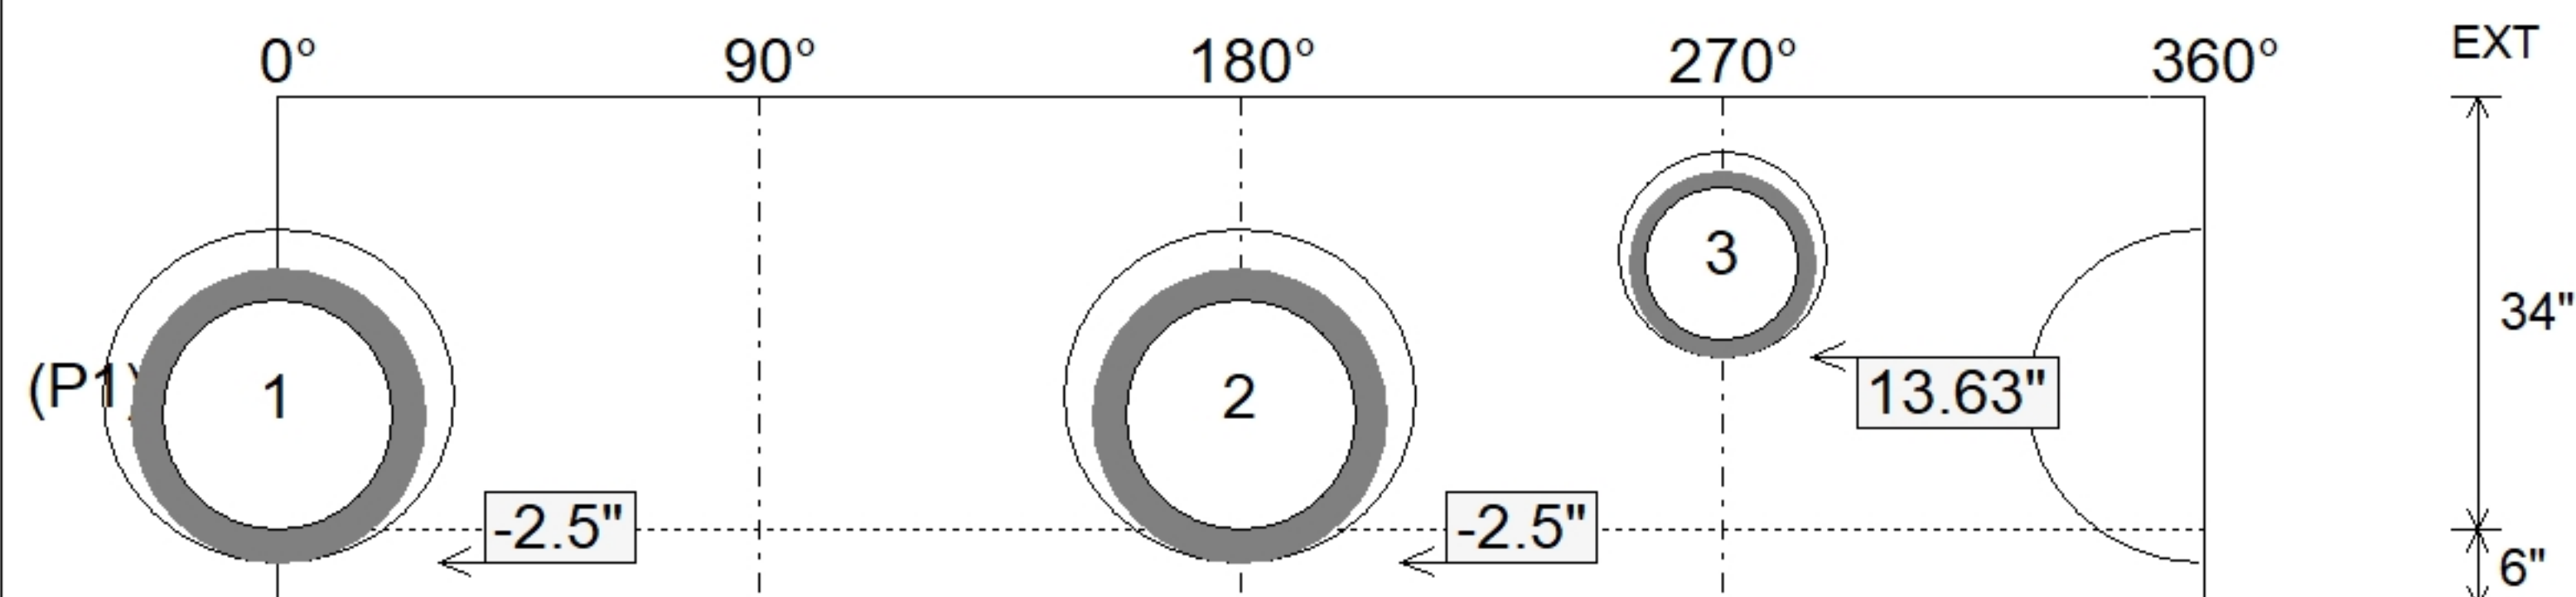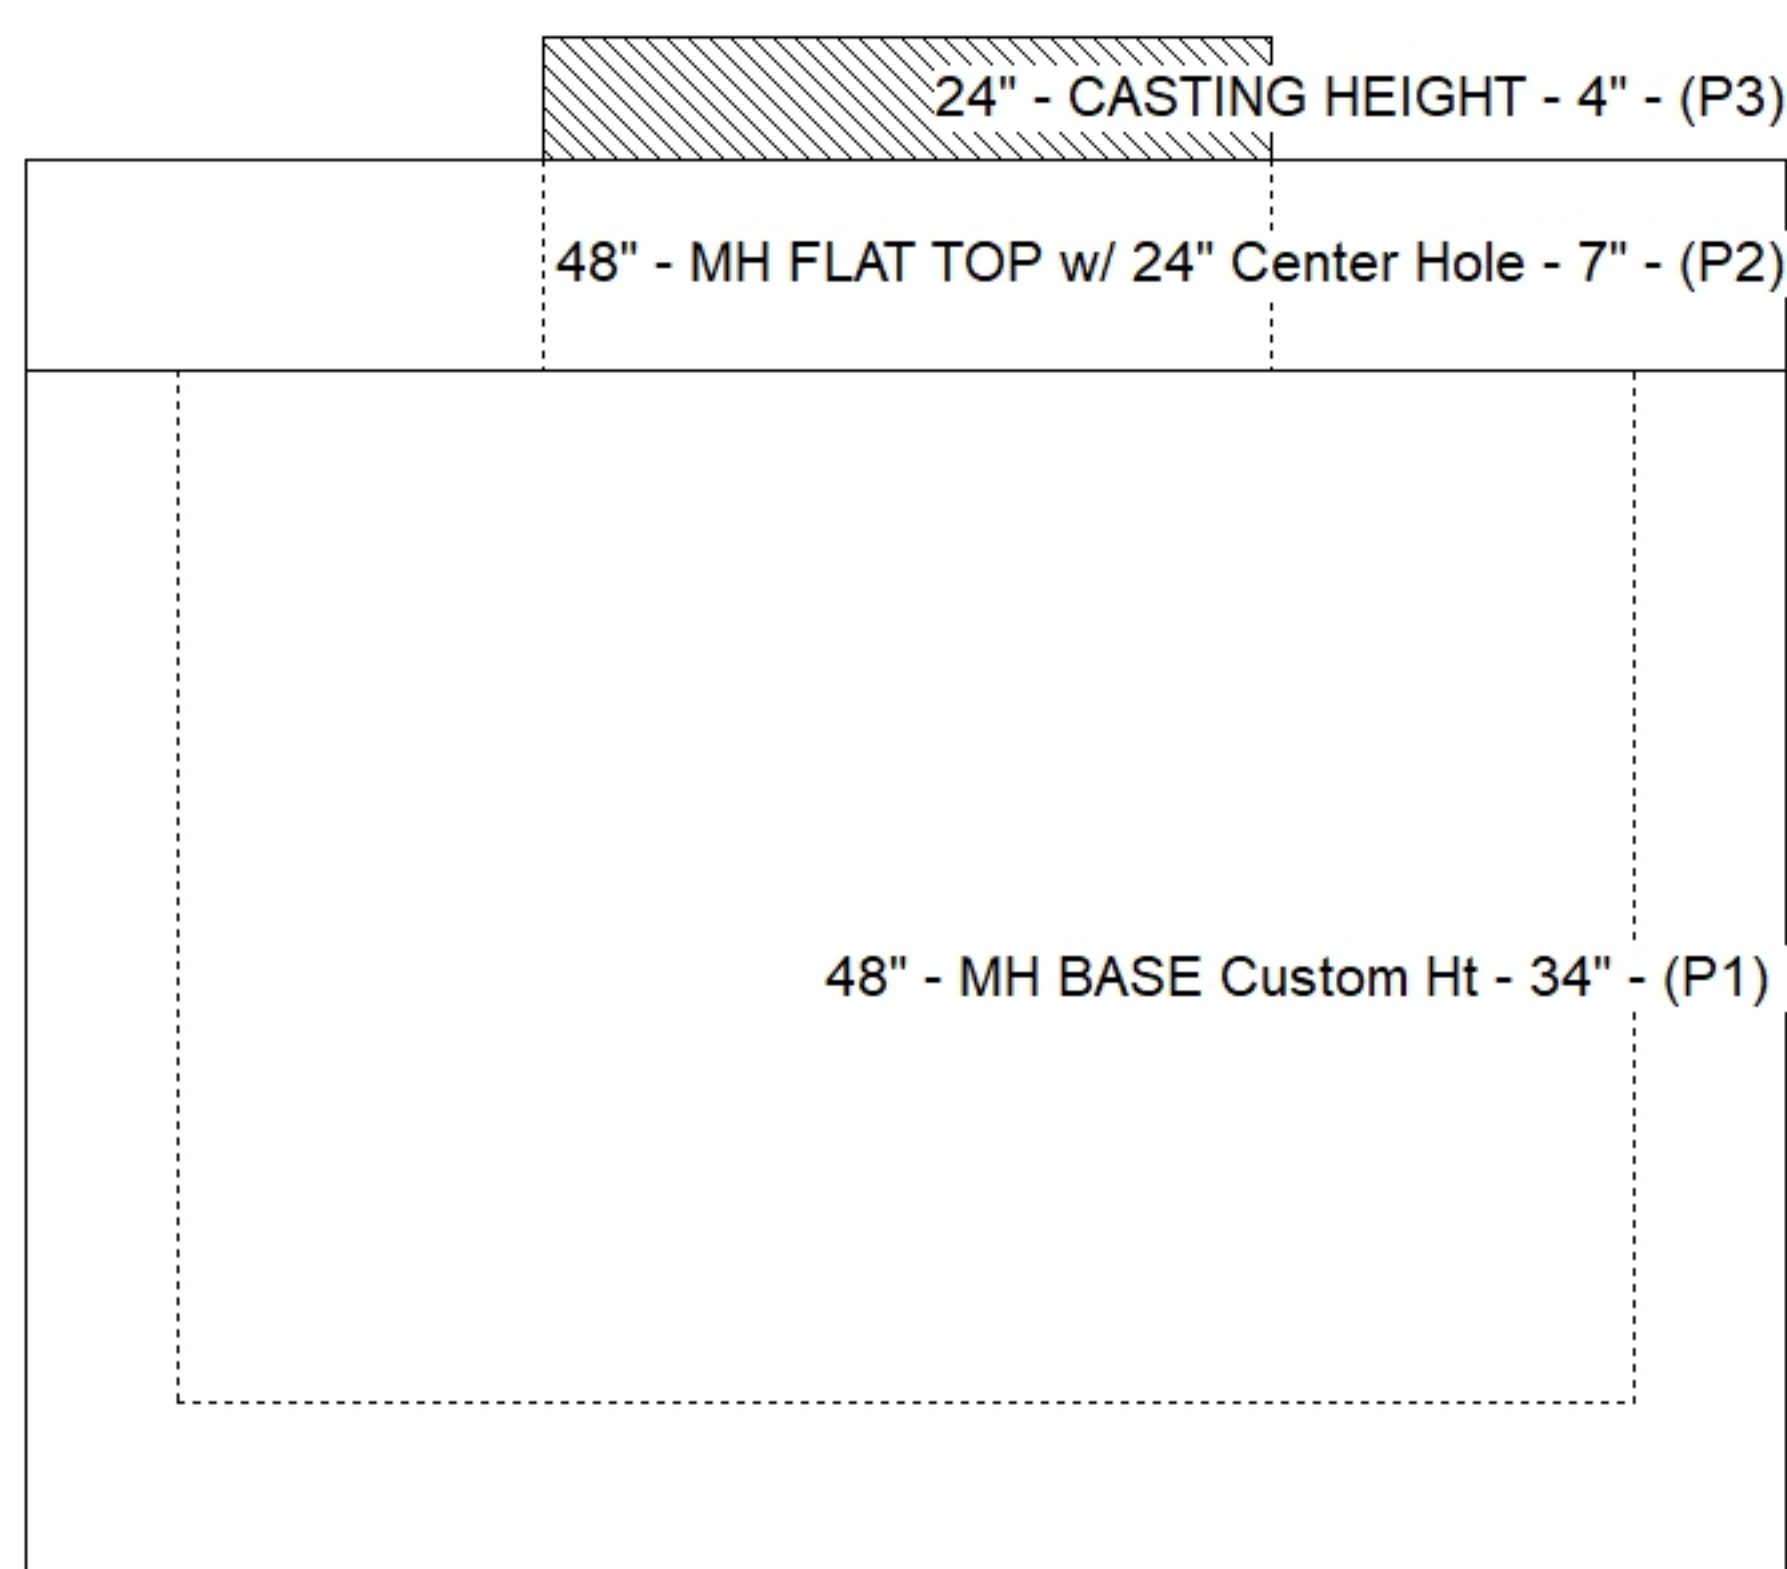

SUBMITTAL
APPROVED BY:
