

Contractor: Weddle Enterprises, Inc

TECH: Jared - F

Plant: 100



Size: 60"

Rim to Invert: 7.19'

Floor Height: 8"

Slack: 1.28"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

P3) 24" - CASTING HEIGHT - 4"
P2) 60" - MH FLAT TOP w/24" Ctr. Hole - 13"
P1) 60" - MH BASE Custom Ht - 72"
1) 60" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 46
6) MH Step ML-10-TDS-NCR - 10"

0 lb
2674 lb
8388 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 11062 lb

The diagram shows three concentric circles. The innermost circle has a crosshair at its center. A curved arrow below the crosshair points clockwise and is labeled $+0^\circ$. The middle circle has a small rectangular feature on its right side. The outermost circle has several tick marks along its circumference. Dashed lines connect various points on the circles to labels in the surrounding text.

-Step: 270°

Invert: 1
Degree: 0°


24" - CASTING HEIGHT - 4" - (P3)

60" - MH FLAT TOP w/24" Ctr. Hole - 13" - (P2)

60" - MH BASE Custom Ht - 72" - (P1)

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	1076'							
Reducer								
Invert 1	1068.81'	0°	36" RCP B WALL	44"	46"	Hole 46	0"	P1
Invert 2	1068.81'	142°	36" RCP B WALL	44"	46"	Hole 46	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

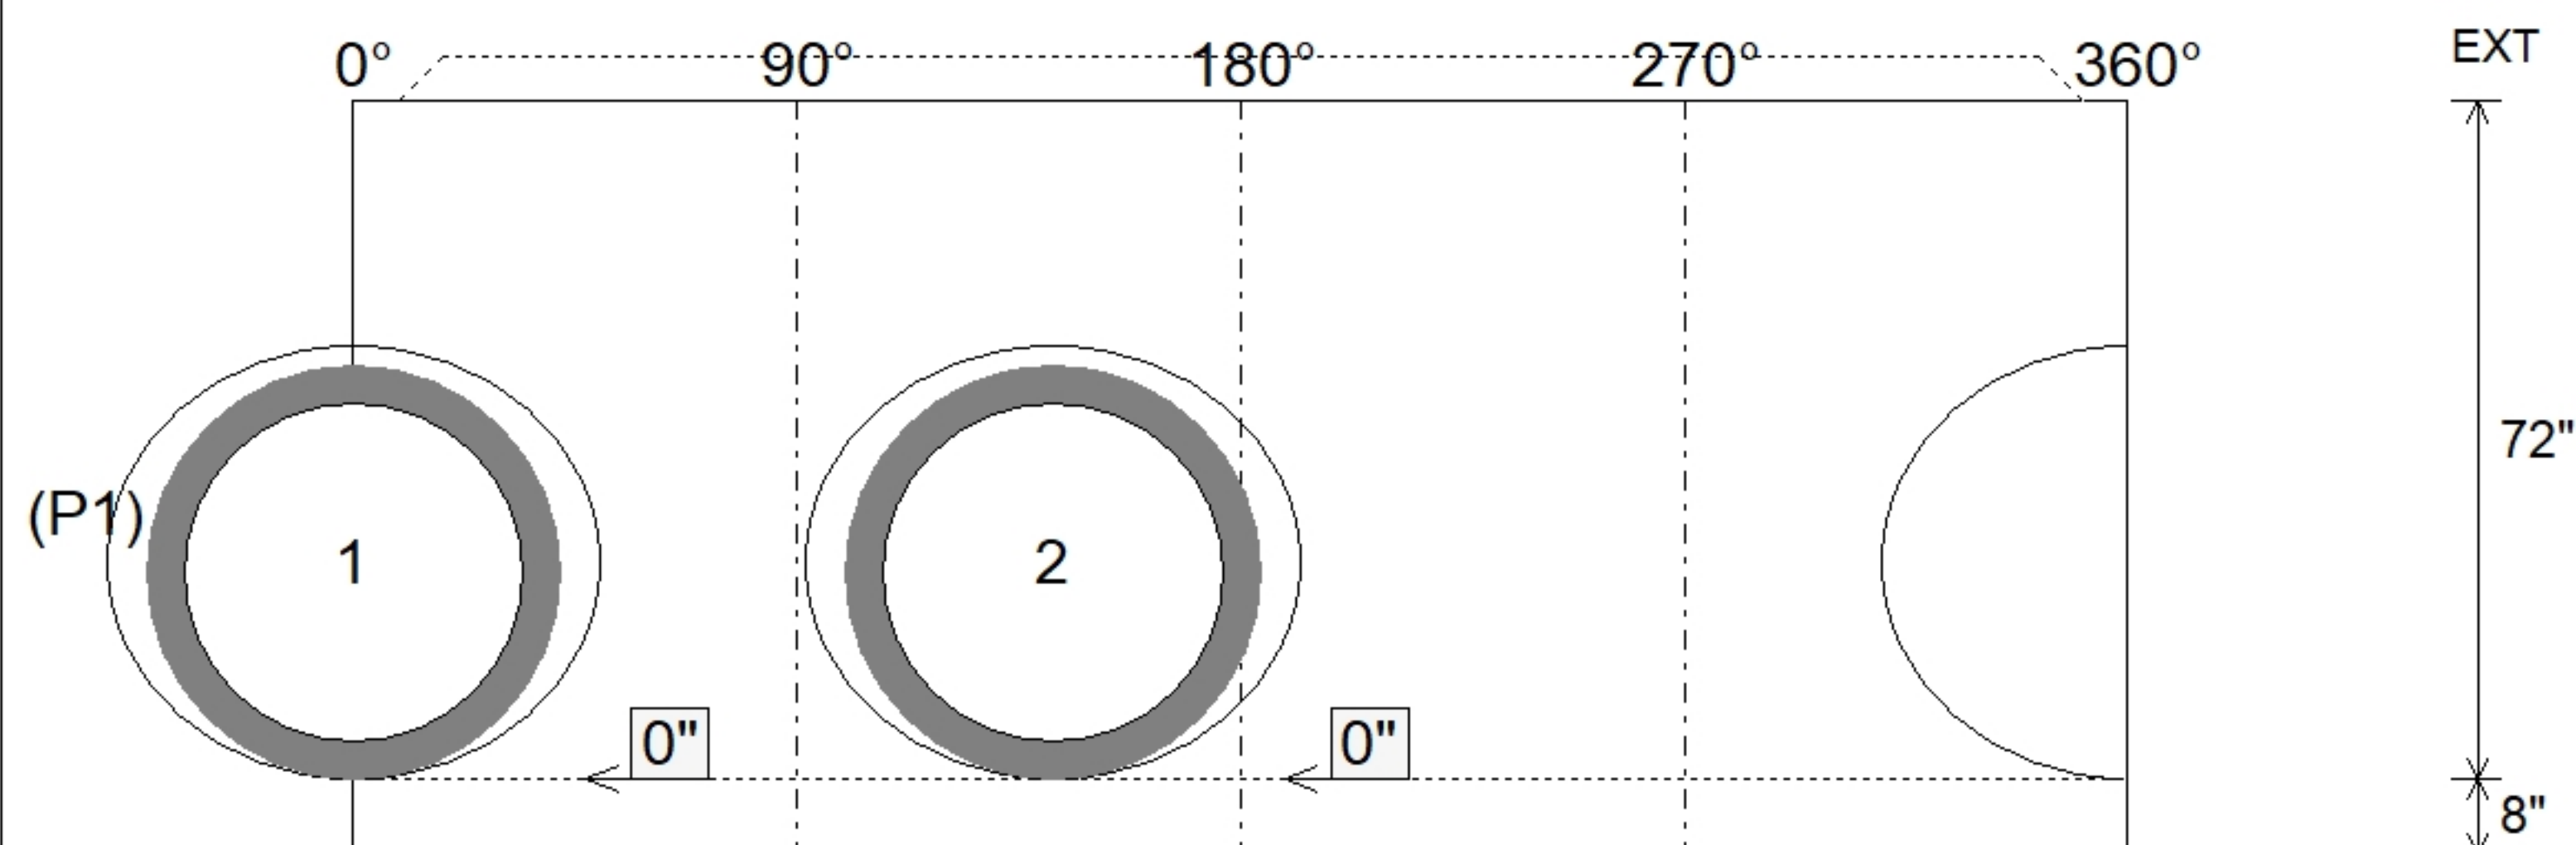

Submittal Drawing
7/21/2026 7:34:22 AM

SUBMITTAL
APPROVED BY:
