

Contractor: Clarksville Gas and Water

TECH: Jared - F

Plant: 100



Size: 120" x 120"

Rim to Invert: 8'

Floor Height: 8"

Slack: 0"


- FLOOR (As .12) #5 BARS AT 8" C.C.E.W.

P4) 42" x 72" - HATCH (CAST FLUSH) - 3.5"
P3) 120" x 120" - BX FLAT LID 8inW w/2x 42"x72" HATCHES - 8"
P2) 120" x 120" - BOX RISER 8inW, Variable Ht - 64"
P1) 120" x 120" - BOX BASE 8inW, 8inF, Variable Ht - 24"

- 1) Conseal CS-102 1.00" (Double)
- 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) SECONDARY POUR - WALLS
- 1) Hole - 0

100 lb
8355 lb
21997 lb
20665 lb
0 lb
0 lb
0 lb
0 lb
0 lb



Structure Total: 51117 lb

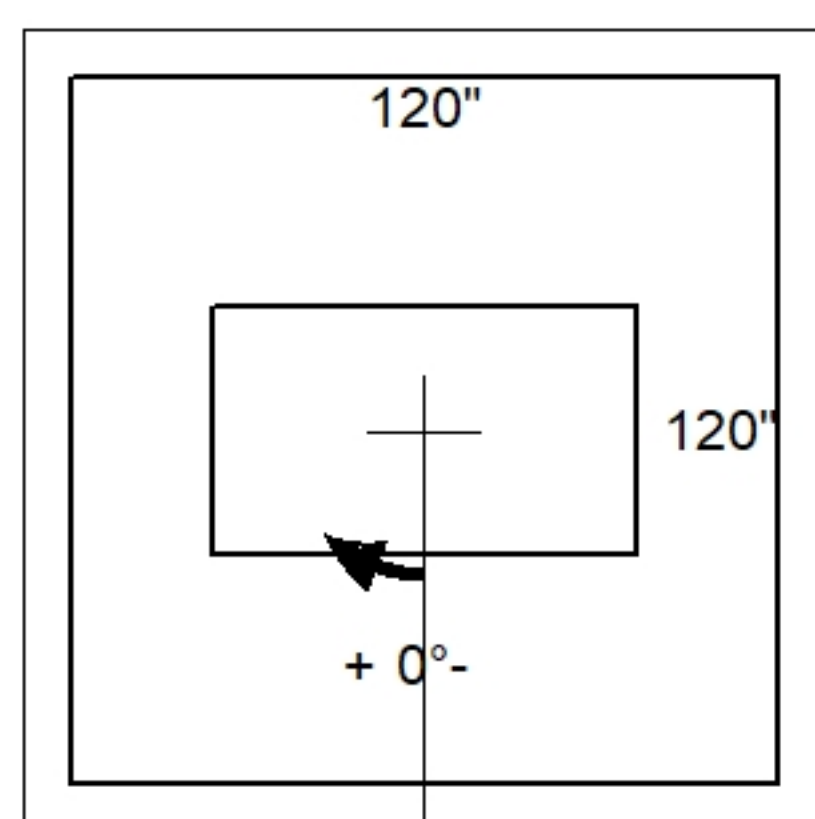

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (␣)	Ref
Rim	8'							
Reducer								
Invert 1	0'	0°	0" No Hole	0.01"	0"	Hole 0	0.005"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

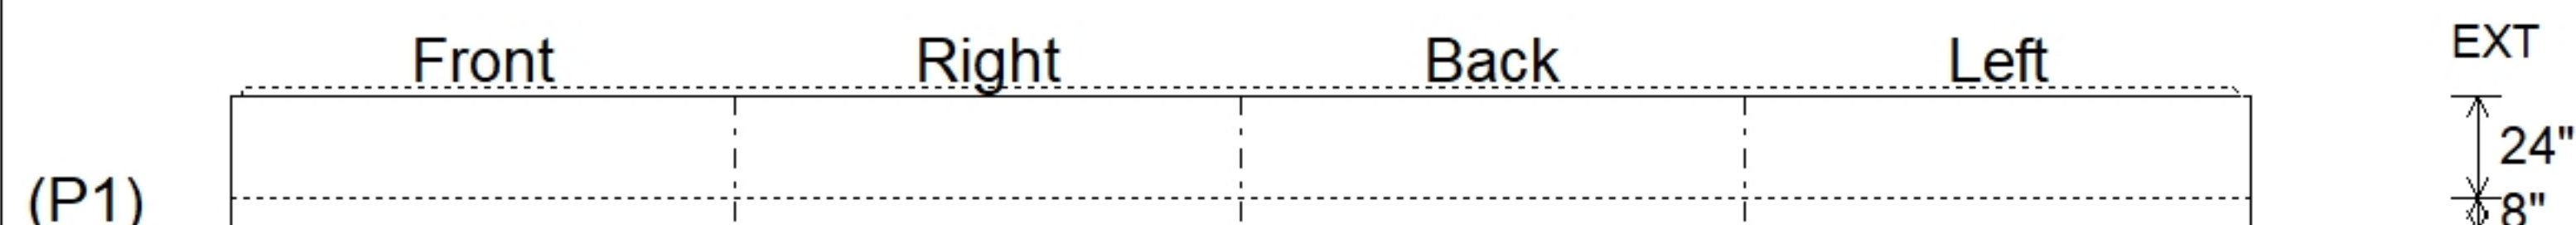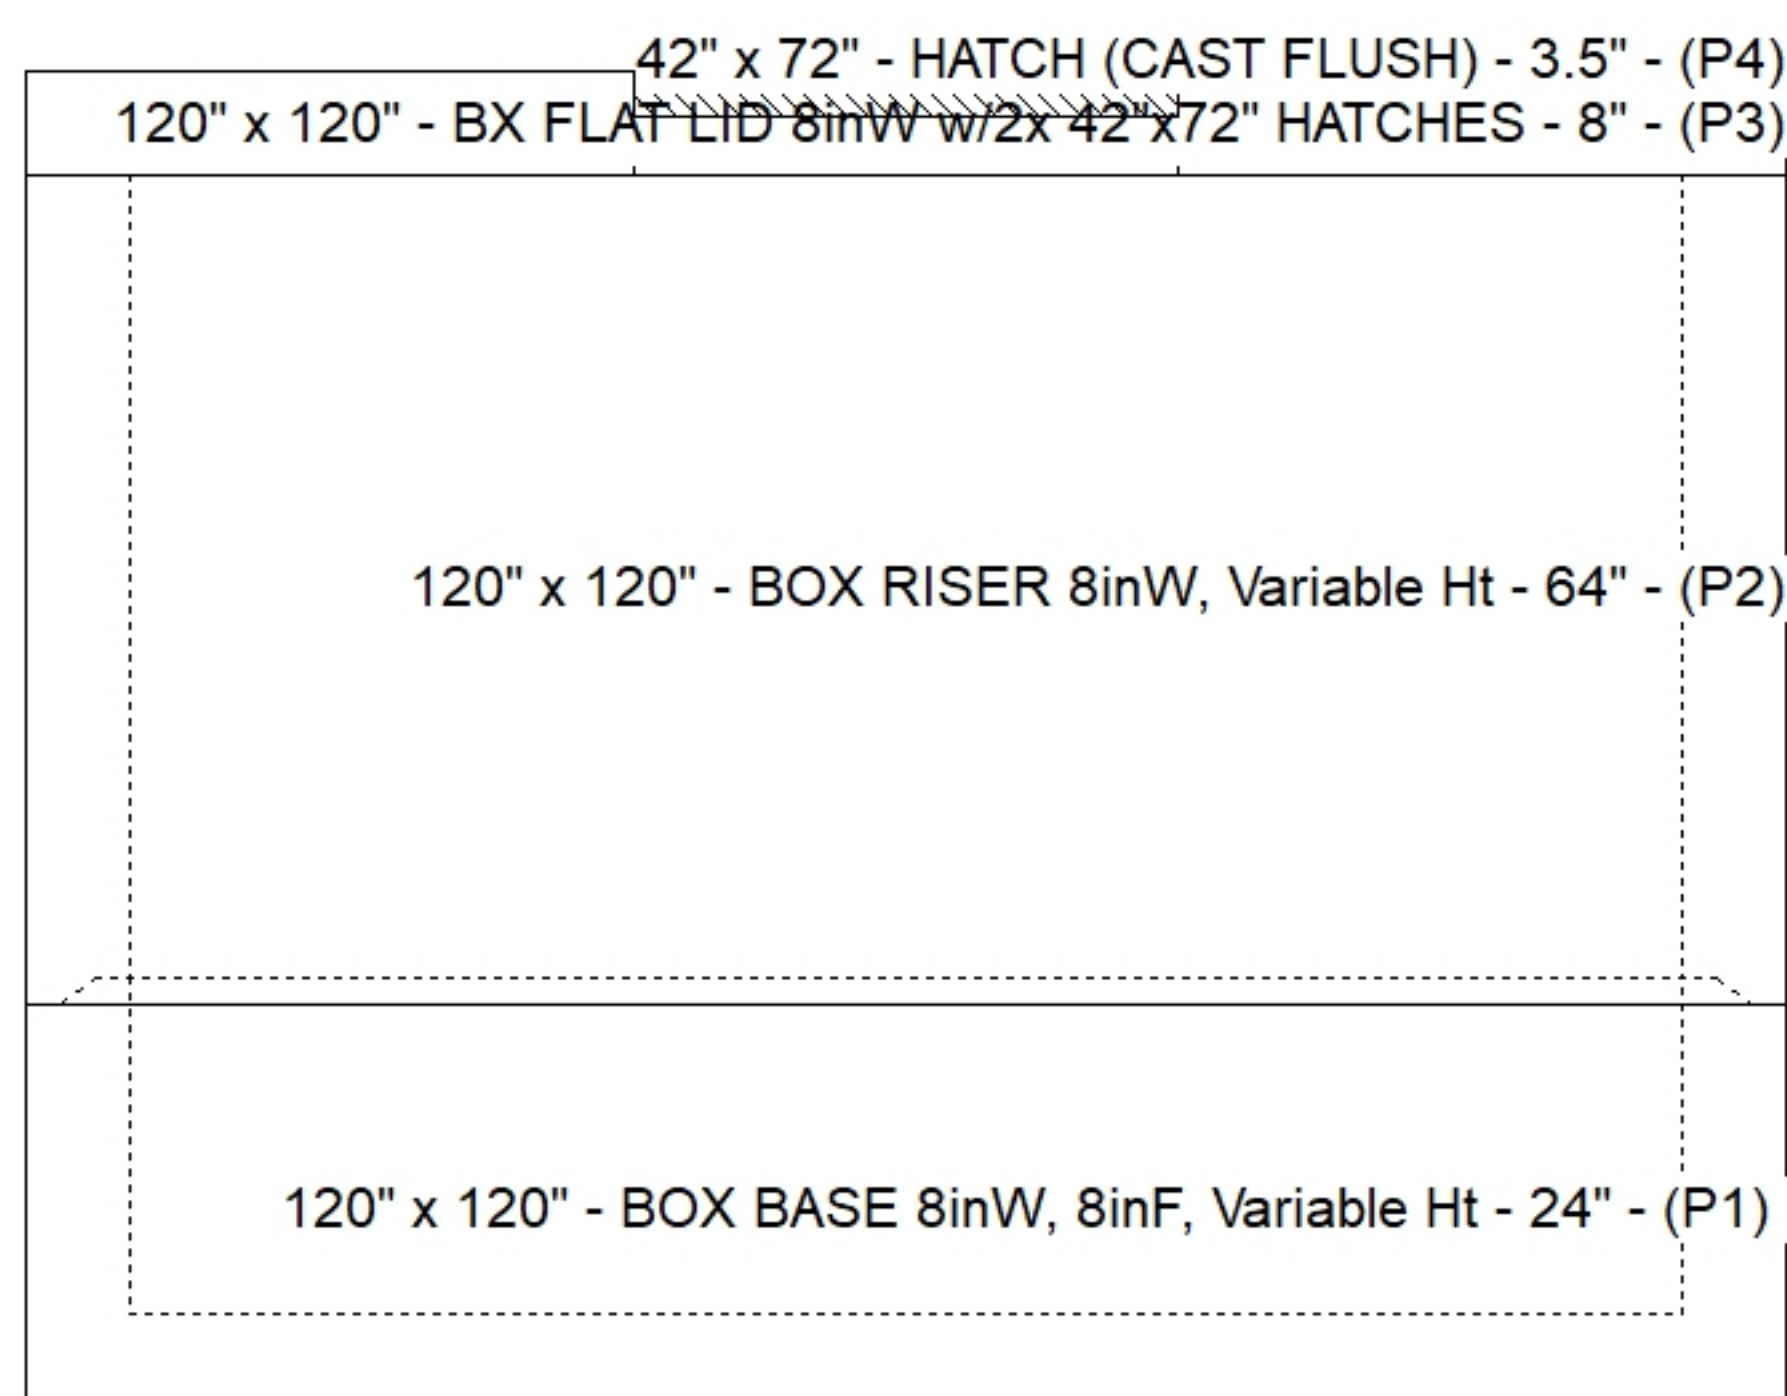

Submittal Drawing
8/13/2026 10:26:01 AM

SUBMITTAL
APPROVED BY:
