

Contractor: Luttrell & Sons, LLC

TECH: Jared - F

Plant: 100



Slack: 2.2"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

5) MH Step ML-10-TDS-NCR - 10"


0 lb

Structure Total: 9824 lb

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	545.5'							
Reducer								
Invert 1	537.4'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	537.5'	130°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

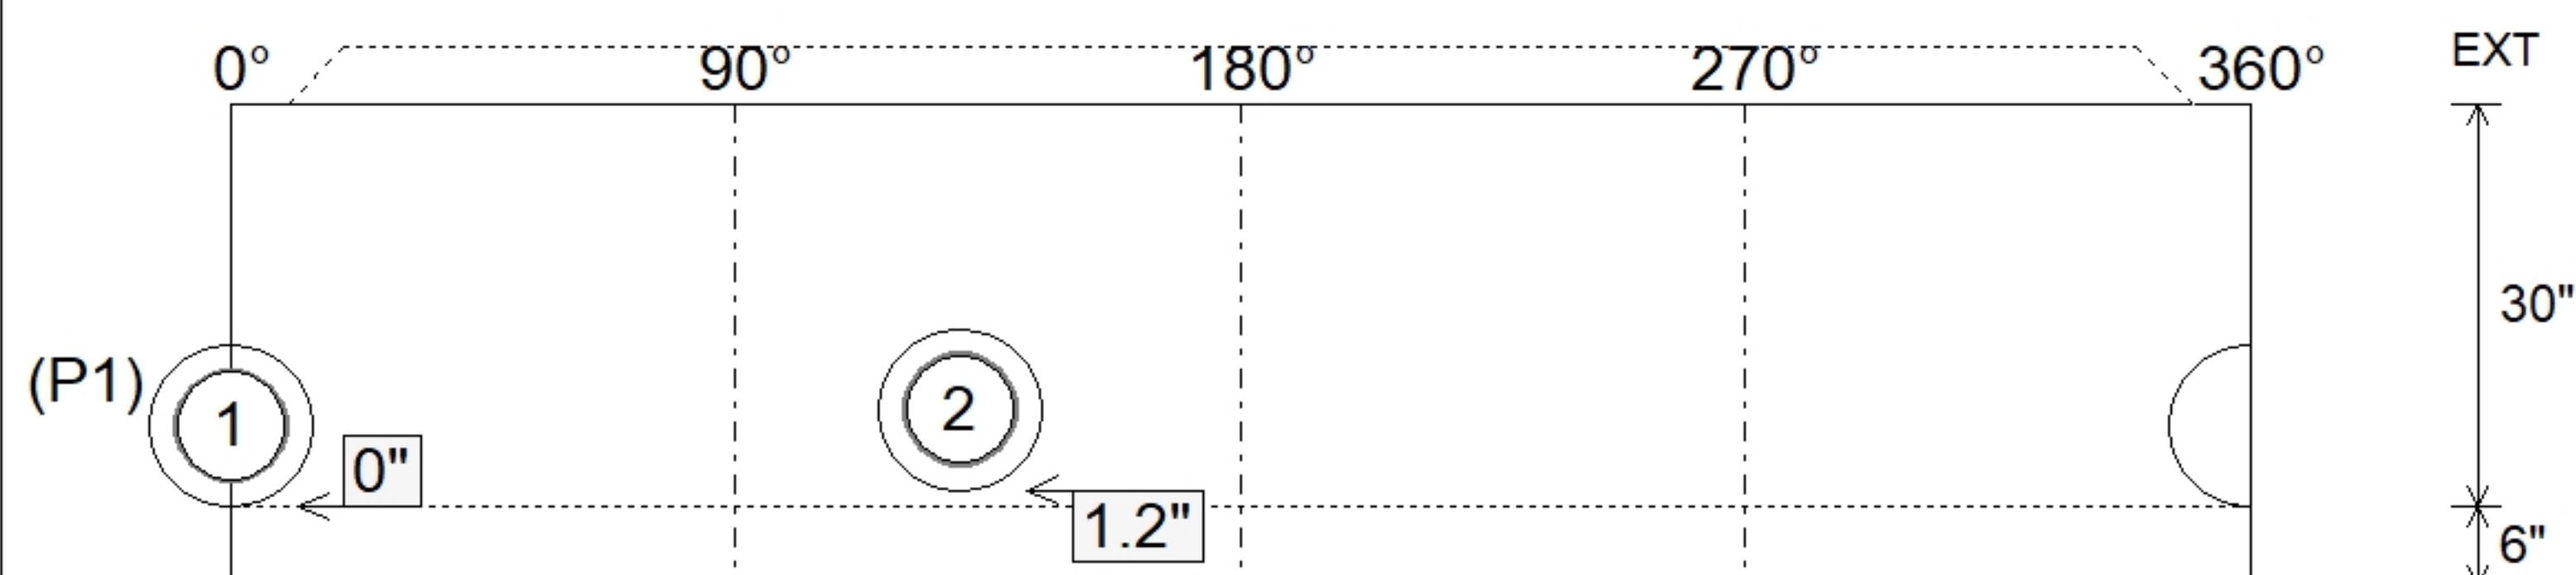

48" - MH BASE - 30" - (P1)

SUBMITTAL
APPROVED BY:
