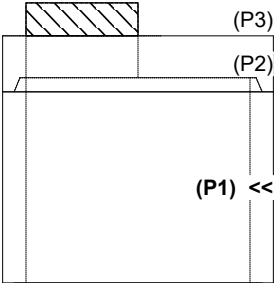
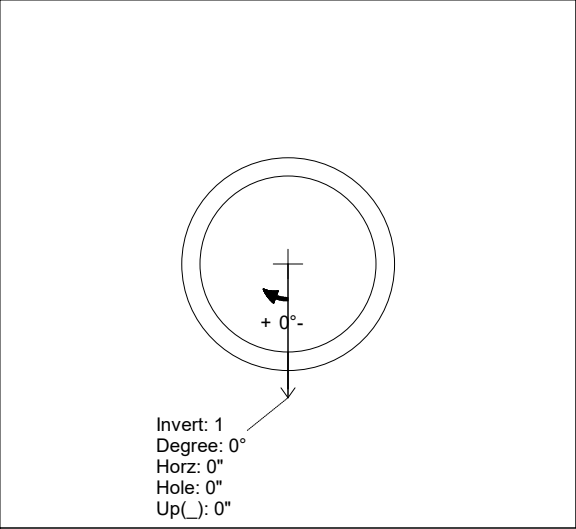
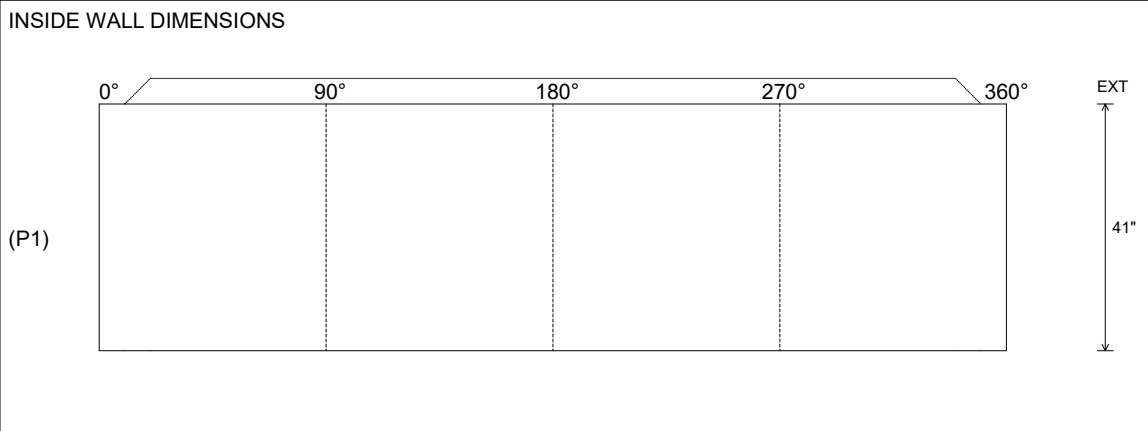


Job Name: 26-1814 - Brownsville Sewer System Additions Job Location: Cave City, KY Contractor: Luttrell & Sons, LLC					Plant: 100 7/31/2026 1:28:09 PM		Tech: Jared - F PC: A. Chambers					
Structure ID: 33+50 ARV												
P1		MH048DHVF									MH DH RISER Custom Ht T/F	
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH DH RISER Custom Ht T/F - 41" 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) Hole - 0					0 lb 1561 lb 2864 lb 271 lb 0 lb 0 lb 0 lb ----- 4696 lb Structure Total:		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12)					
Rim: 5'		Rim to Invert: 5'		Slack: 0"		Sump: 0"		Step Position:				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	0'	0°	0"	0" No Hole	0.01"	Hole 0	0"	0"	0"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)							
												
INSIDE WALL DIMENSIONS												
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Flat		Wall Thickness: 5" Floor Height: 0"		Height (Int): 41" Height (Ext): 41"		Weight (Net): 2864 lb Volume (Net): 0.73cu.yd			
