

Job Name: 26-1814 - Brownsville Sewer System Additions
Job Location: Cave City, KY
Contractor: Luttrell & Sons, LLC

Plant: 100

7/31/2026 1:28:55 PM

Tech: Jared - F

PC: A. Chambers



Structure ID: 92+05 ARV

P2 MH048LD12ECC

MH FLAT TOP w/ 24" ECC Hole F/G

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12"
P1) 48" - MH DH RISER Custom Ht T/F - 41"
1) CASTING - HOE MC-375 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
1) Hole - 0


Structure Total:

0 lb
1561 lb
2864 lb
271 lb
0 lb
0 lb
0 lb
4696 lb


Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS.
4. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C "SANITARY")

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB = H20 LOADING.
- RISER/WALLS (As .12)

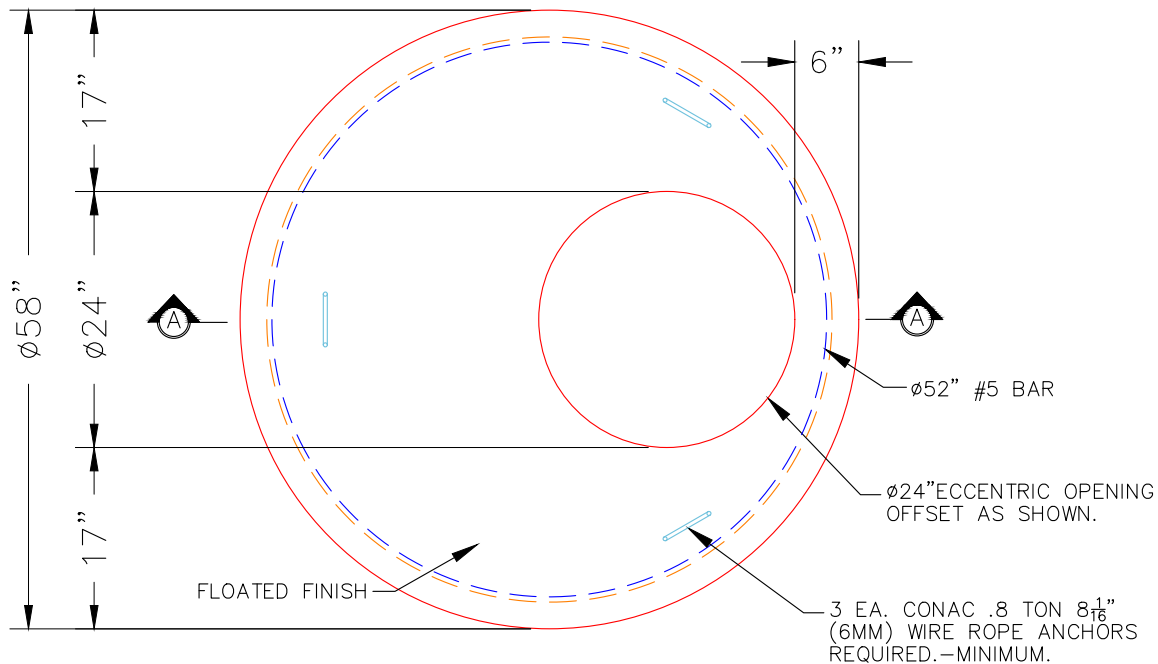

PLAN VIEW

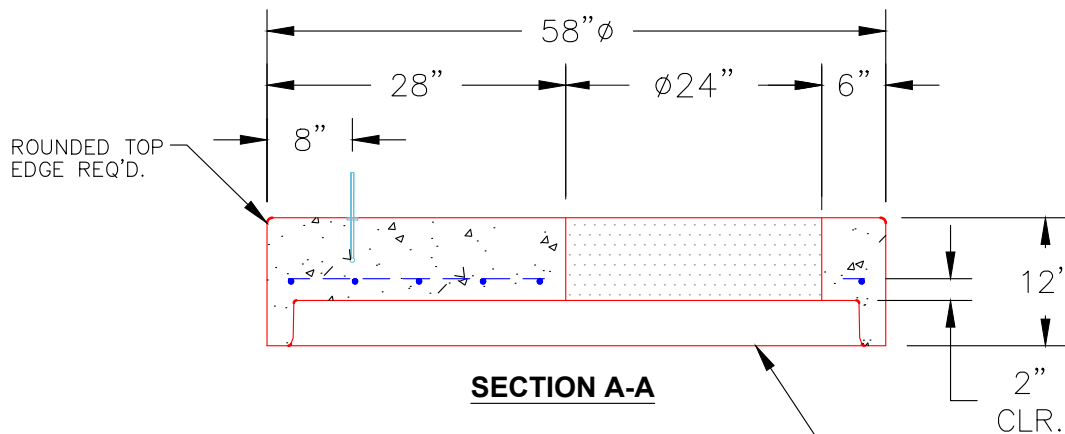

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.42cu.yd
