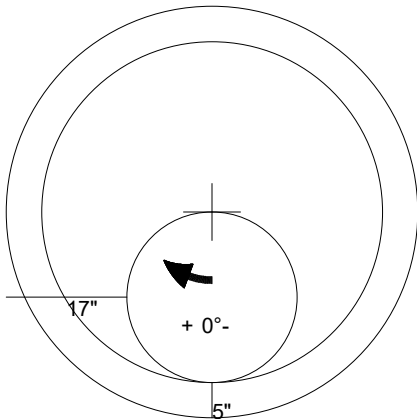



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks		Plant: 100 8/26/2026 3:50:03 PM	Tech: Jared - F PC: E. Bradley	
Structure ID: S2.1 SS-MH P3 MH048CN30-S		ECC CONE w/ 24" HOLE NO STEP F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 30" P2) 48" - MH RISER NO STEPS T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 26" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 0350		0 lb 2050 lb 2515 lb 3101 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 1 lb ----- Structure Total: 9378 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
