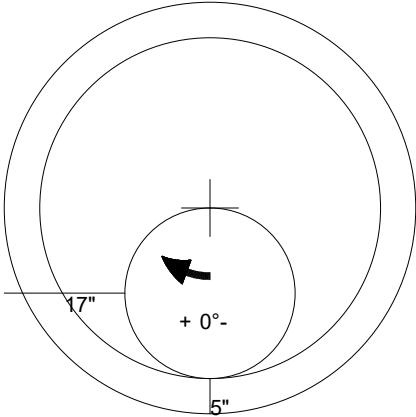



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks		Plant: 100 8/26/2026 3:50:02 PM	Tech: Jared - F PC: E. Bradley	
Structure ID: S6 SS-MHD				
P3 MH048CN24-S		ECC CONE w/ 24" HOLE NO STEP F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 24" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 40" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285 1) A-Lok - 0140		0 lb 1550 lb 2515 lb 4053 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb 1 lb ----- Structure Total: 9832 lb	<u>Structure Notes:</u> . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) 5. INTERNAL DROP ASSEMBLY PROVIDED BY OTHERS. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
