

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100




Slack: 2.52"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


1) A-Lok - 0140

1 lb


Structure Total: 9832 lb

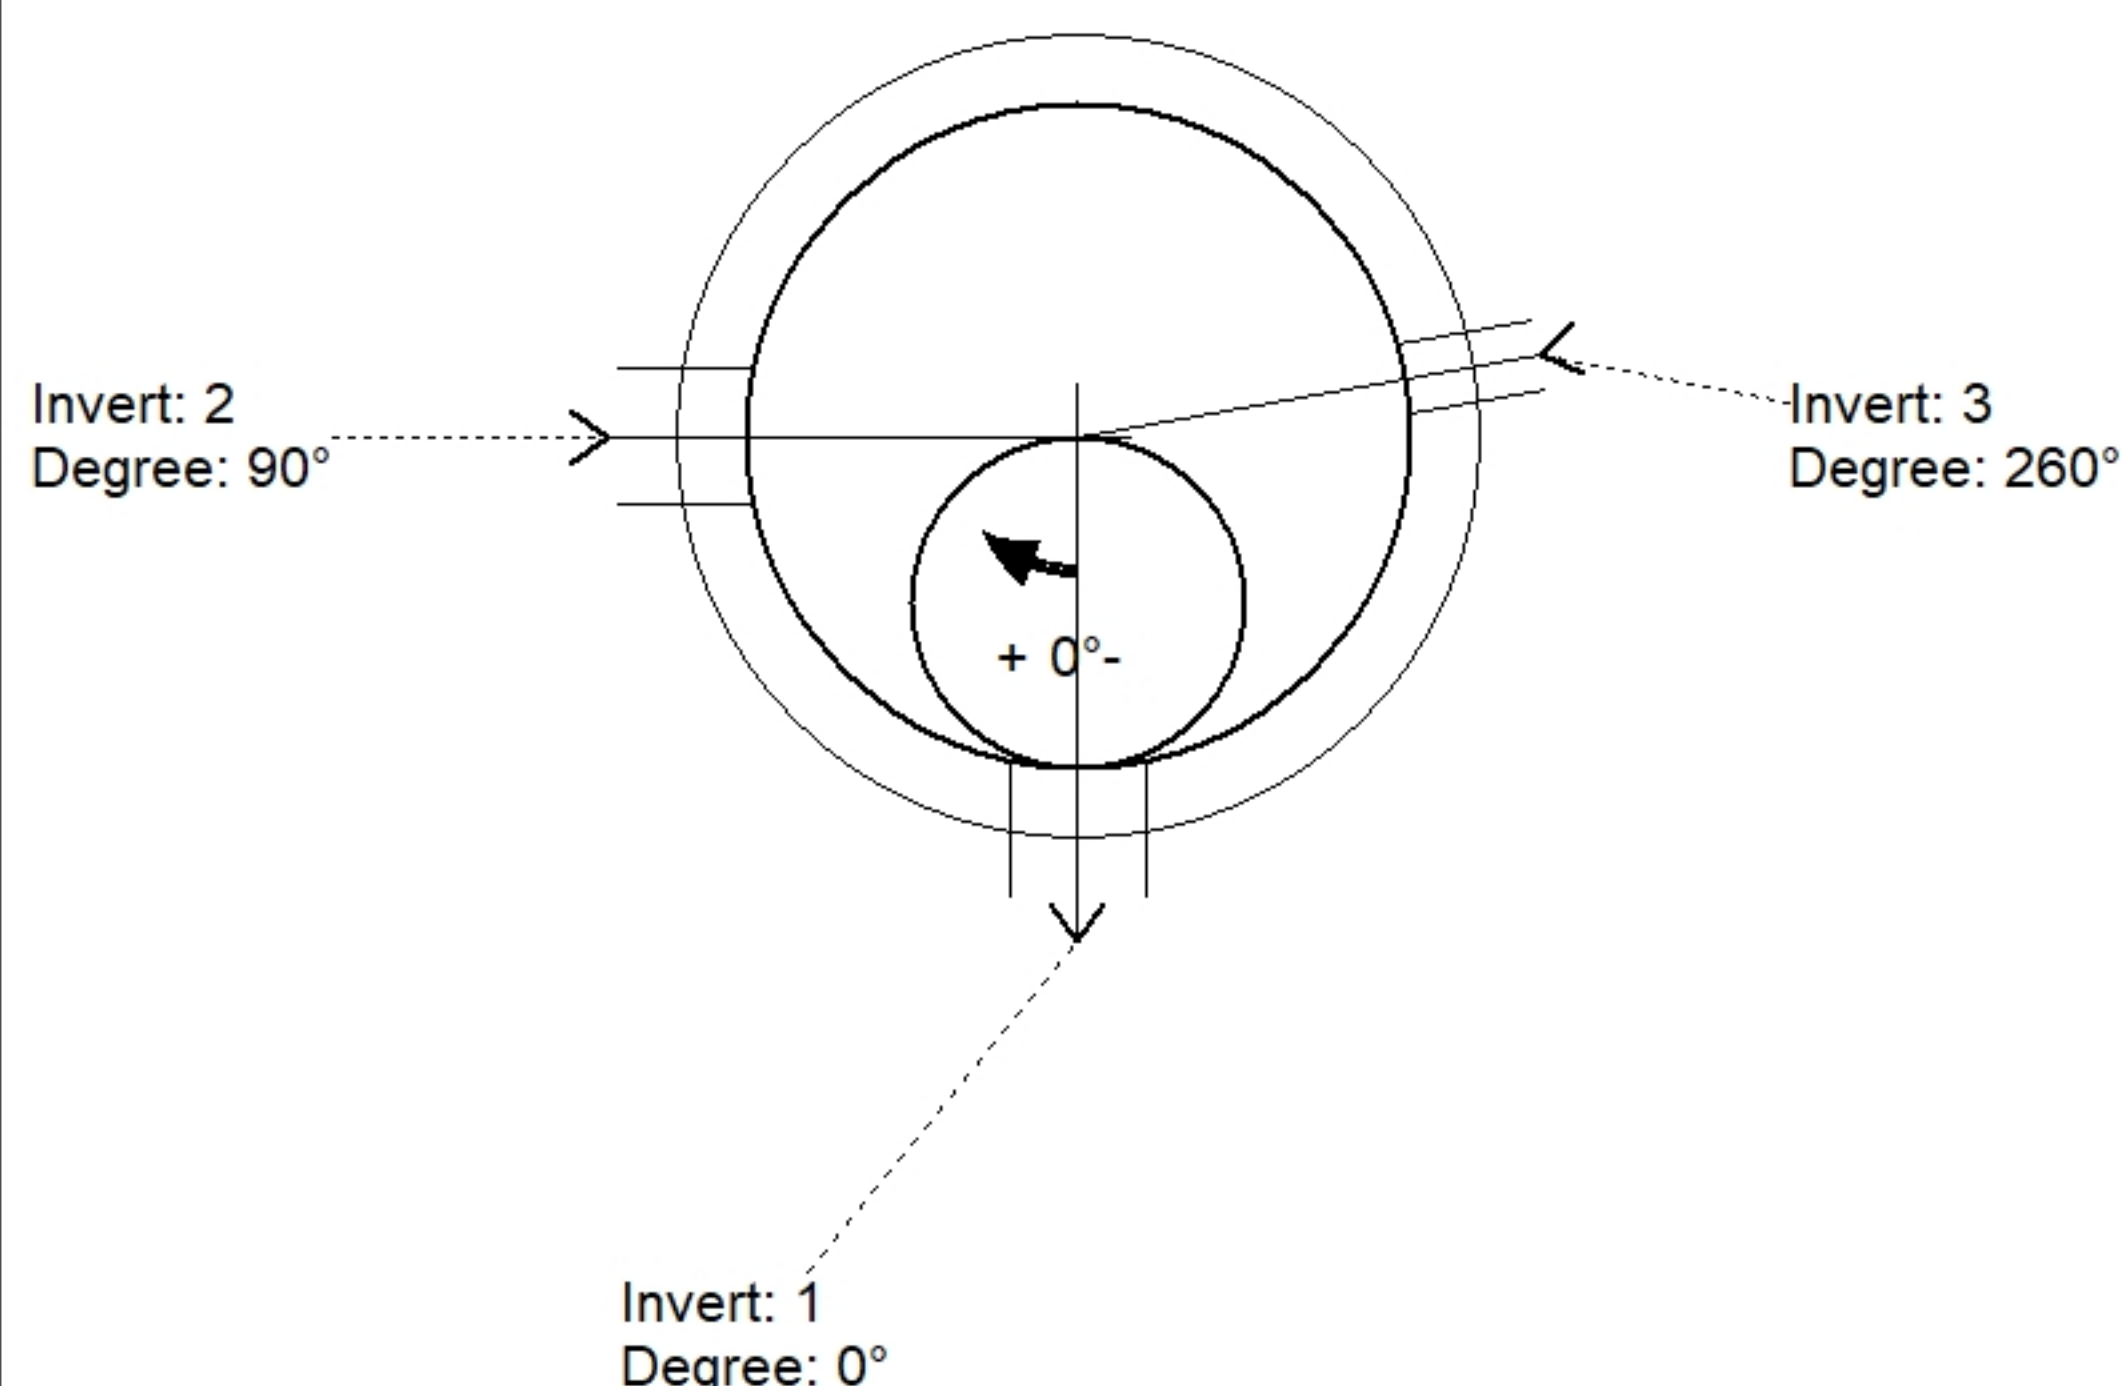

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	936.26'							
Reducer								
Invert 1	927.3'	0°	8" PVC SDR35	8.5"	9.75"	A-Lok 0285	1.125"	P1
Invert 2	927.4'	90°	8" PVC SDR35	8.5"	9.75"	A-Lok 0285	2.325"	P1
Invert 3	929.47'	260°	4" PVC SDR35	4.25"	5"	A-Lok 0140	27.54"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

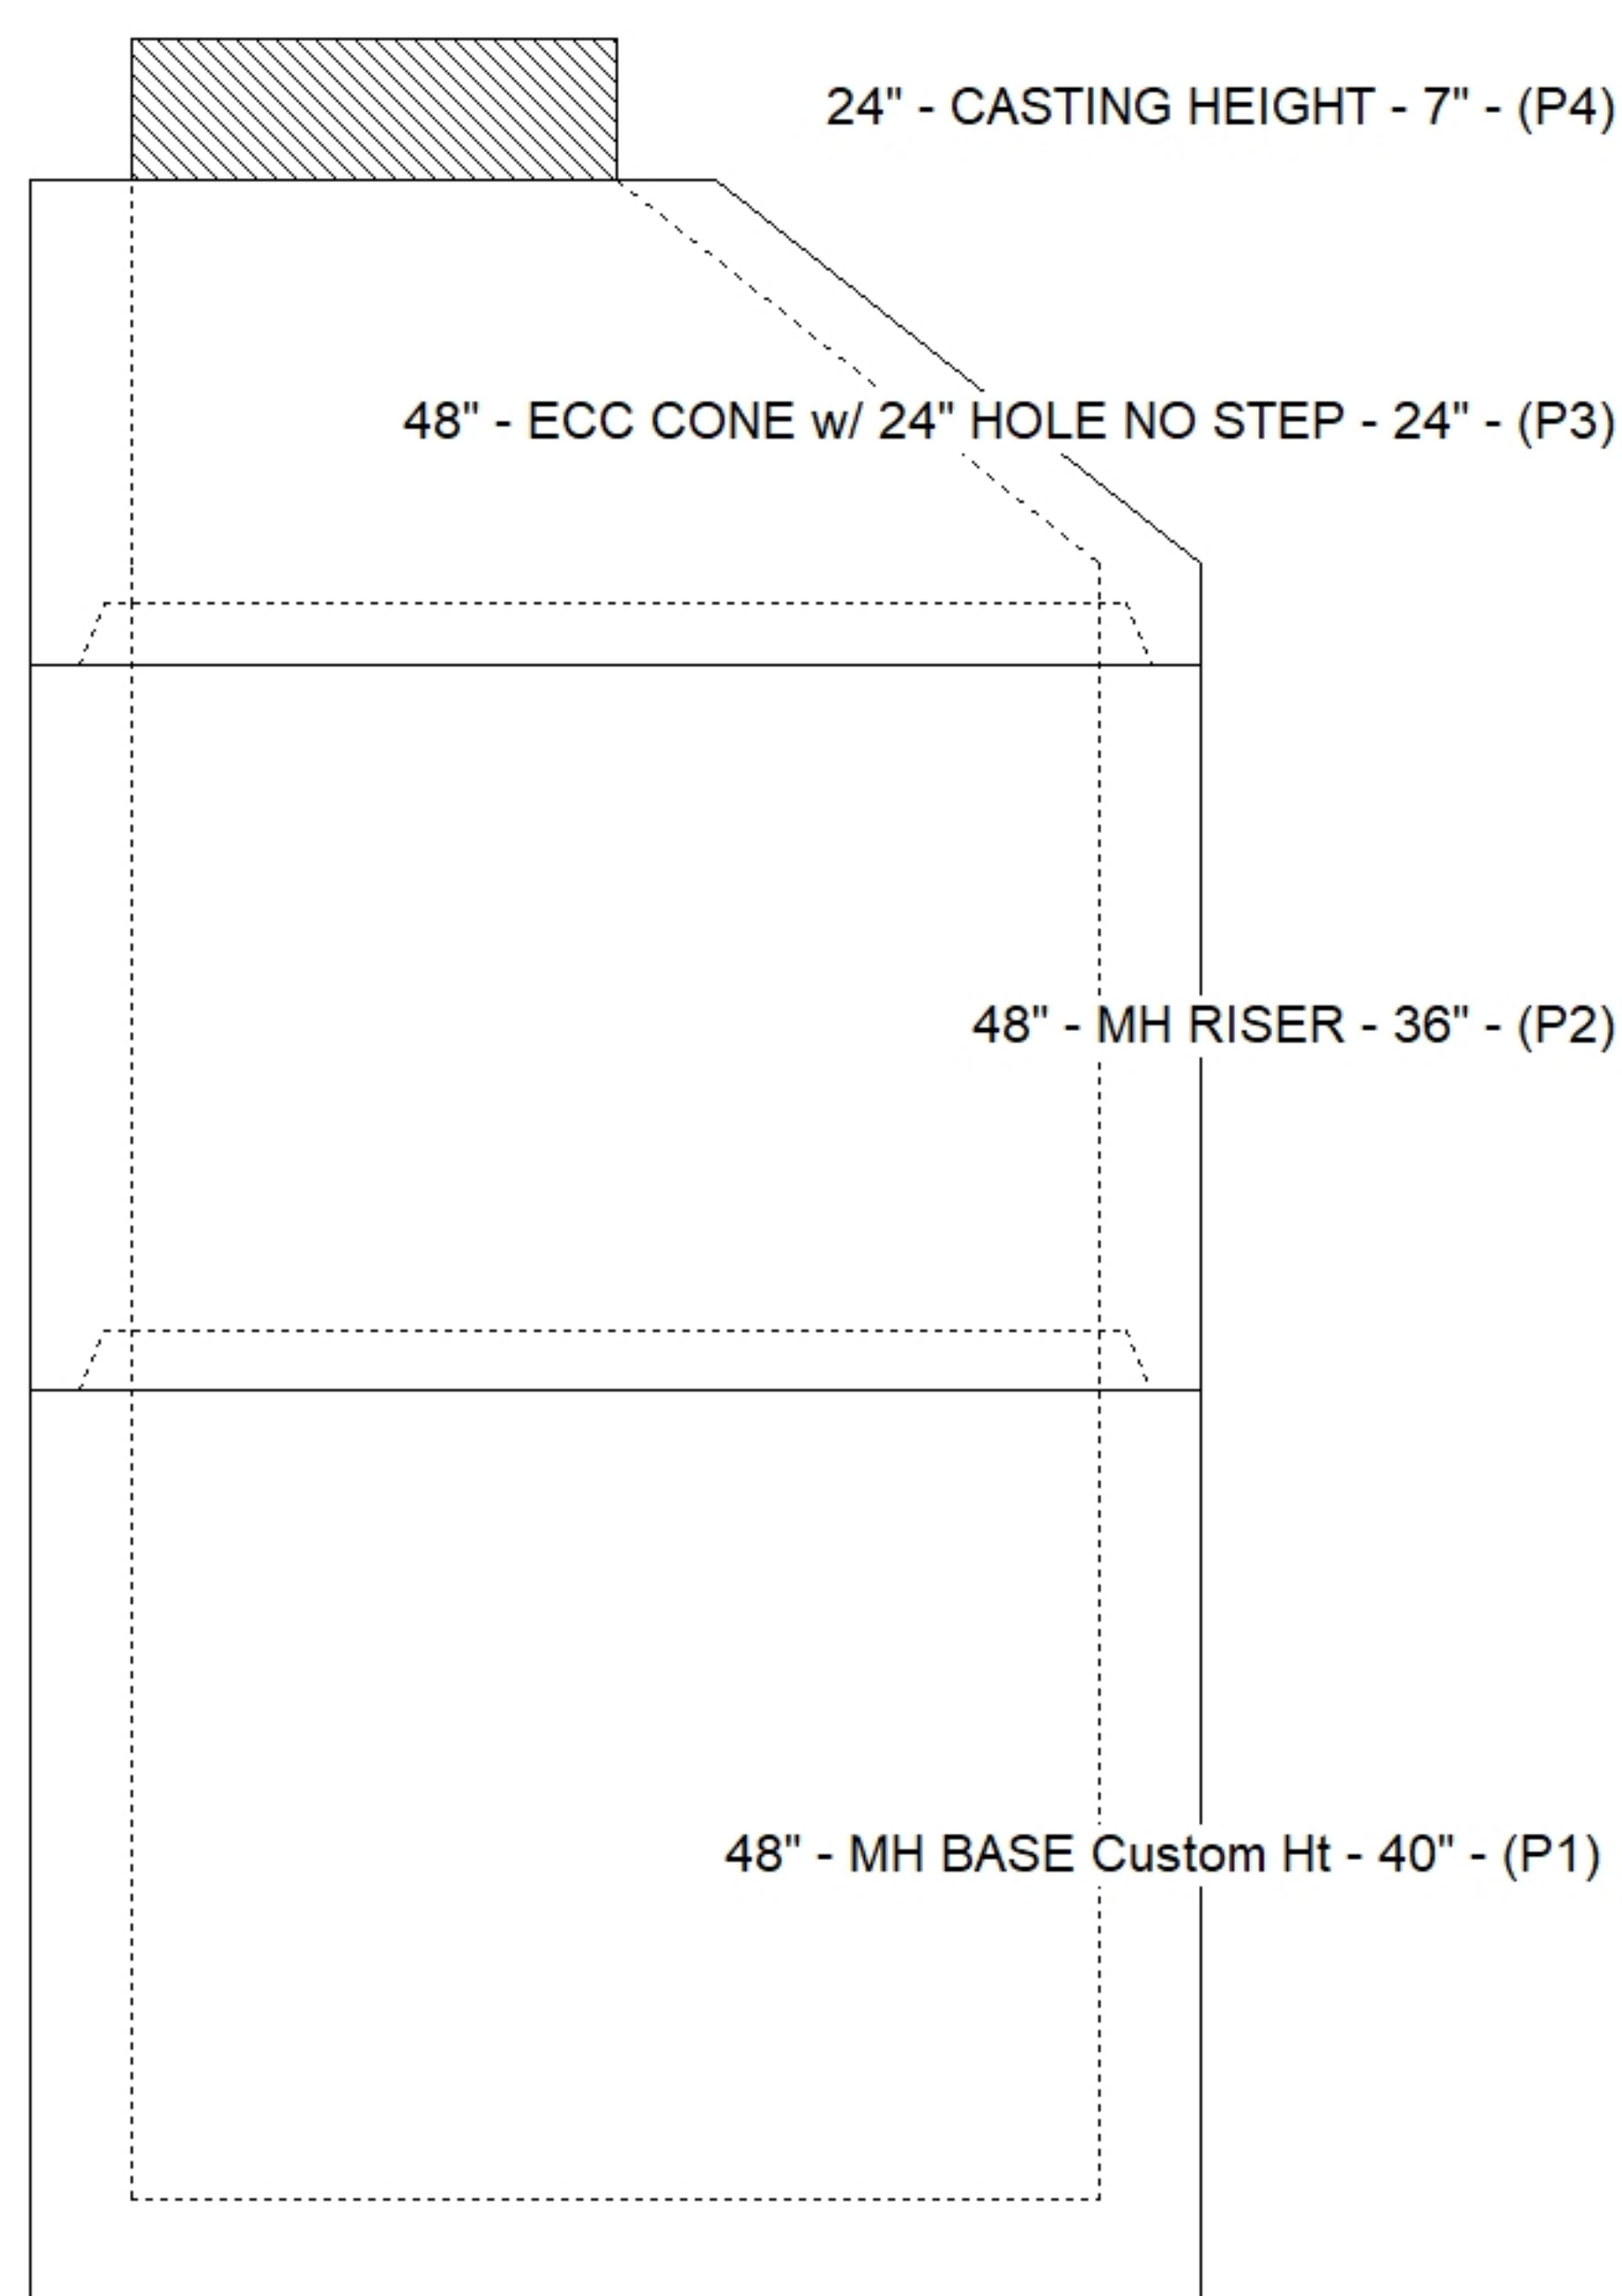

Default - Interior Dimensions

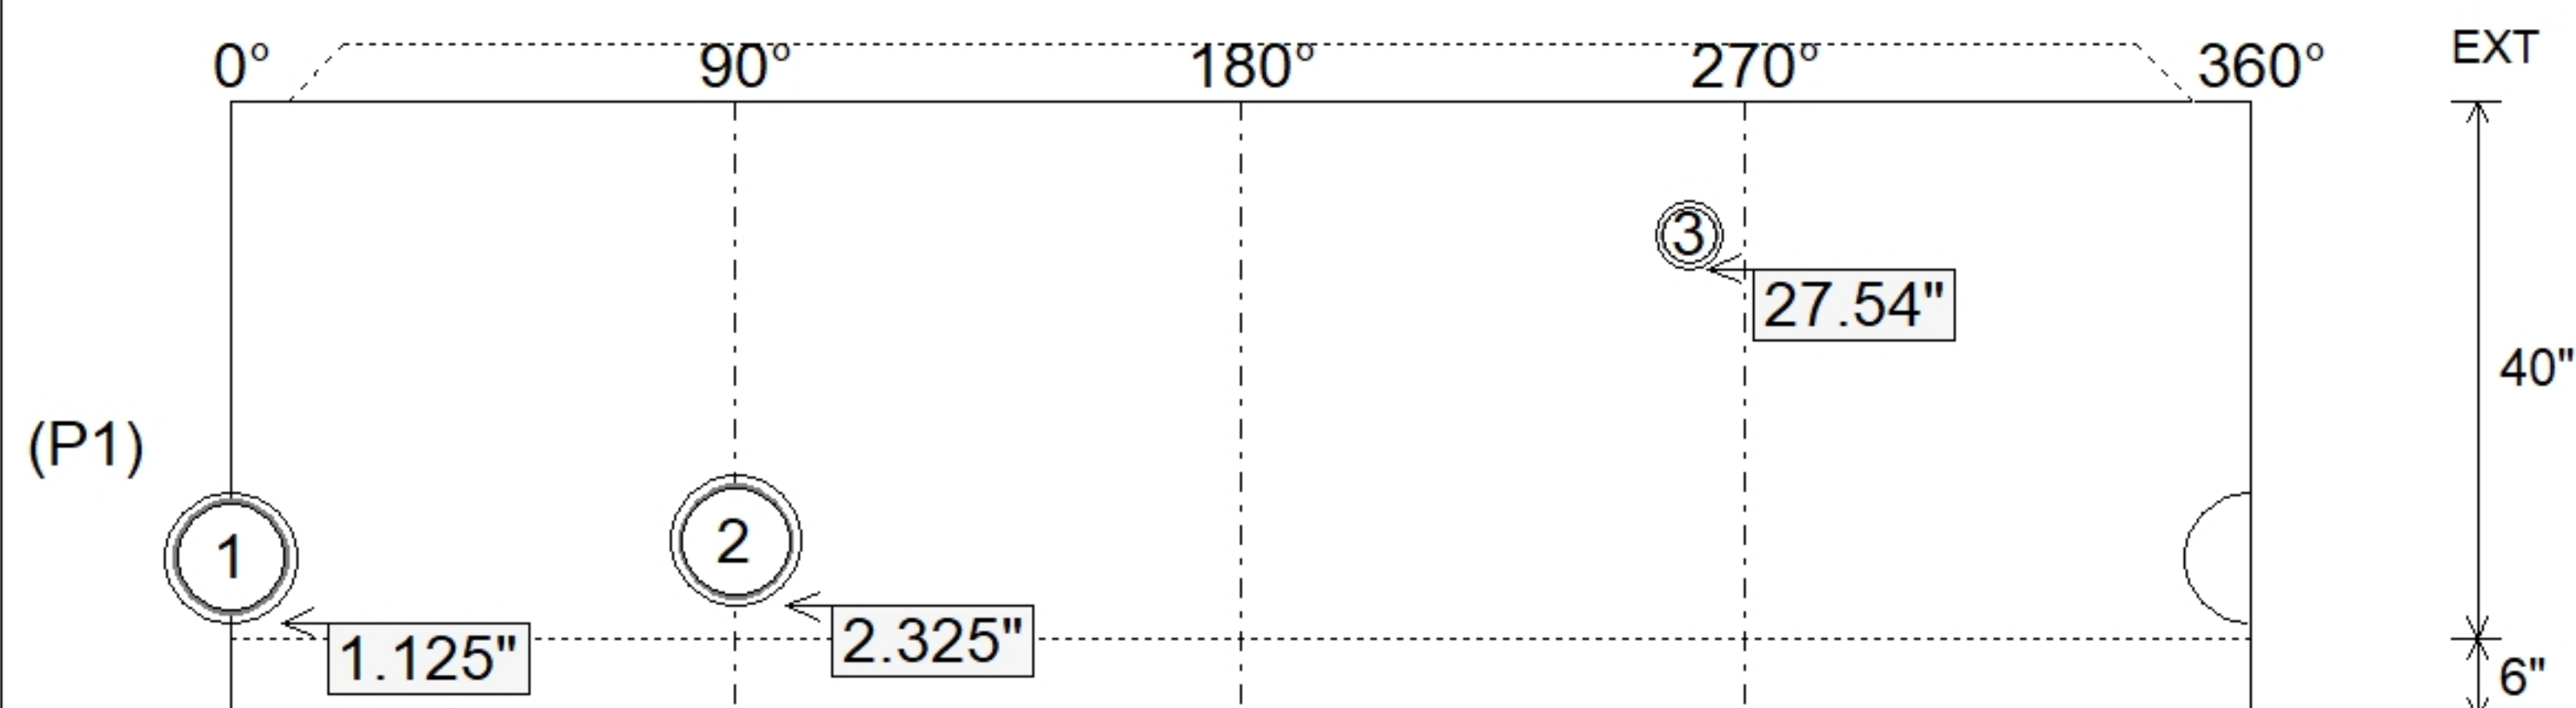

Submittal Drawing
8/31/2026 4:01:05 PM

SUBMITTAL
APPROVED BY:
