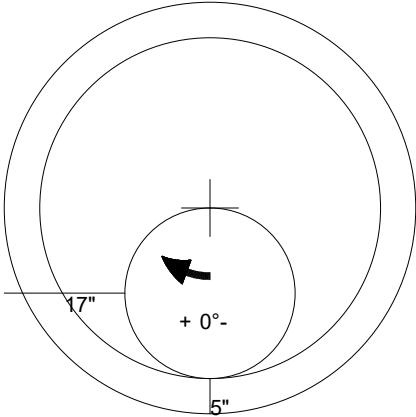



Job Name: 26-1822 - Project Versailles		Plant: 100		Tech: Jared - F		
Job Location: Versailles, KY		8/26/2026 3:50:01 PM		PC: E. Bradley		
Contractor: KY Earthworks						
Structure ID: T1 SS-MH						
P4 MH048CN24-S		ECC CONE w/ 24" HOLE NO STEP F/G				
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 24" P3) 48" - MH RISER NO STEPS T/G - 48" P2) 48" - MH RISER NO STEPS T/G - 60" P1) 48" - MH BASE NO STEP T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0350		0 lb 1550 lb 3353 lb 4192 lb 3334 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb ----- Structure Total: 14142 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
						
						
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove		Wall Thickness: 5"		Height (Ext): 24"
						Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
