



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:45:47 PM		Tech: Jared - F PC: E. Bradley					
Structure ID: T3 SS-MH												
P1 MH048BA30					MH BASE NO STEP T/n							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 24" P2) 48" - MH RISER NO STEPS T/G - 60" P1) 48" - MH BASE NO STEP T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0350					0 lb 1550 lb 4192 lb 3334 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb ----- 10789 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 932.79' Rim to Invert: 10.1' Slack: 2.2" Sump: 2" Step Position: 0°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1	922.69'	0°	0"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	1.125"	0"		
Invert 2	922.89'	180°	91.125"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	3.5"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

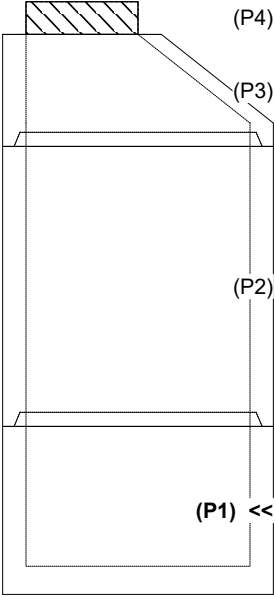

(P4)
(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

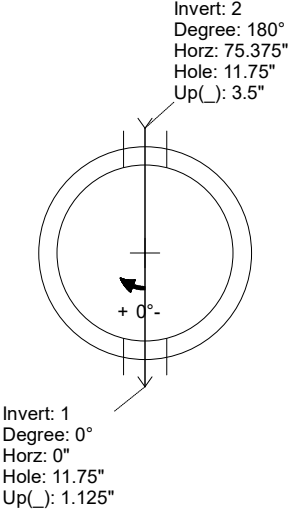

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 11.75"
Up(_): 3.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 11.75"
Up(_): 1.125"


UPSIDE-DOWN VIEW (int. dimensions)

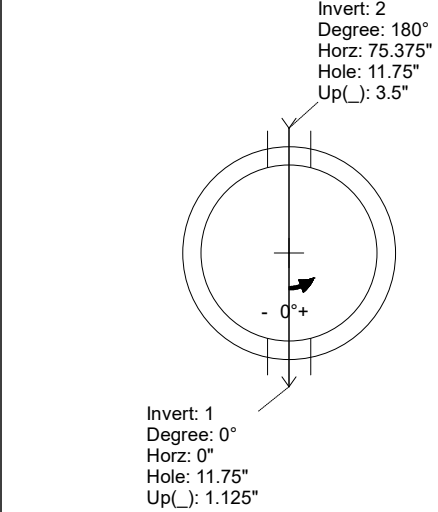

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 11.75"
Up(_): 3.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 11.75"
Up(_): 1.125"

INSIDE WALL DIMENSIONS



(P1)

360° 270° 180° 90° 0°

6" 30" EXT

3.5" 1.125" 75.375" 0"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3334 lb Volume (Net): 0.85cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:45:47 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: T3 SS-MH											
P1 MH048BA30			MH BASE NO STEP T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 24" P2) 48" - MH RISER NO STEPS T/G - 60" P1) 48" - MH BASE NO STEP T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0350					0 lb 1550 lb 4192 lb 3334 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb ----- 10789 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 932.79' Rim to Invert: 10.1' Slack: 2.2' Sump: 2' Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	922.69'	0°	0"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	1.125"	0"	
Invert 2	922.89'	180°	91.125"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	3.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

FOR INVERT ONLY

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 11.75"
Up(): 3.5"


Invert: 1
Degree: 0°
Horz: 0"
Hole: 11.75"
Up(): 1.125"




UPSIDE-DOWN VIEW (int. dimensions)

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 11.75"
Up(): 3.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 11.75"
Up(): 1.125"



INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3334 lb Volume (Net): 0.85cu.yd
----------------------------------	---------------------------------	--	--	--
