



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:45:46 PM		Tech: Jared - F PC: E. Bradley			
Structure ID: T4 SS-MH										
P1 MH048BA36		MH BASE NO STEP T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 42" P1) 48" - MH BASE NO STEP T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0350 1) A-Lok - 0285					0 lb 270 lb 3000 lb 3722 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb 1 lb ----- Structure Total: 8706 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 931.04' Rim to Invert: 7.34' Slack: 1.08" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	923.7'	0°	0"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	1.125"	0"
Invert 2	923.9'	88°	44.5"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	3.5"	0"
Invert 3	923.9'	168°	85"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	3.5"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

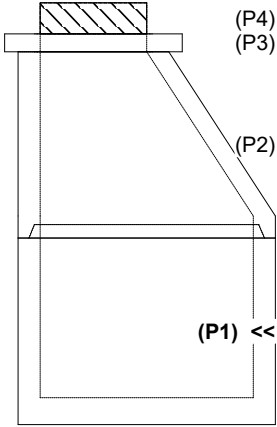

(P4)
(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

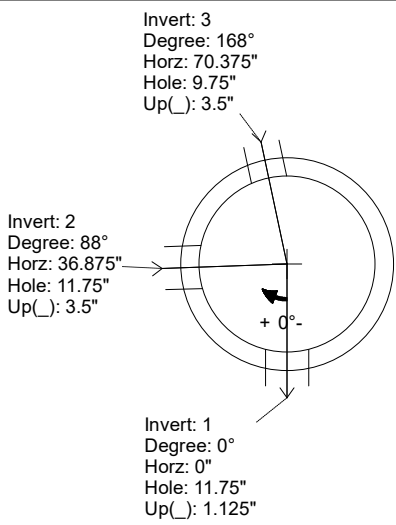


Invert: 3
Degree: 168°
Horz: 70.375"
Hole: 9.75"
Up(): 3.5"

Invert: 2
Degree: 88°
Horz: 36.875"
Hole: 11.75"
Up(): 3.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 11.75"
Up(): 1.125"

UPSIDE-DOWN VIEW (int. dimensions)

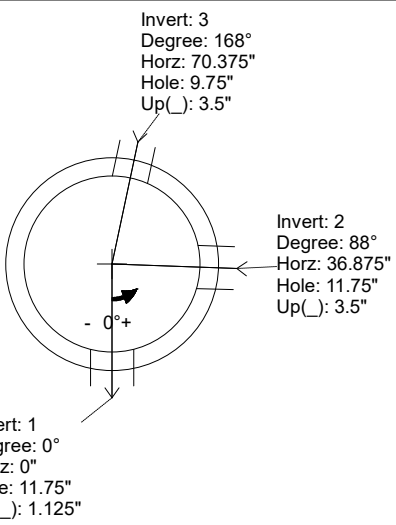


Invert: 3
Degree: 168°
Horz: 70.375"
Hole: 9.75"
Up(): 3.5"

Invert: 2
Degree: 88°
Horz: 36.875"
Hole: 11.75"
Up(): 3.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 11.75"
Up(): 1.125"

INSIDE WALL DIMENSIONS

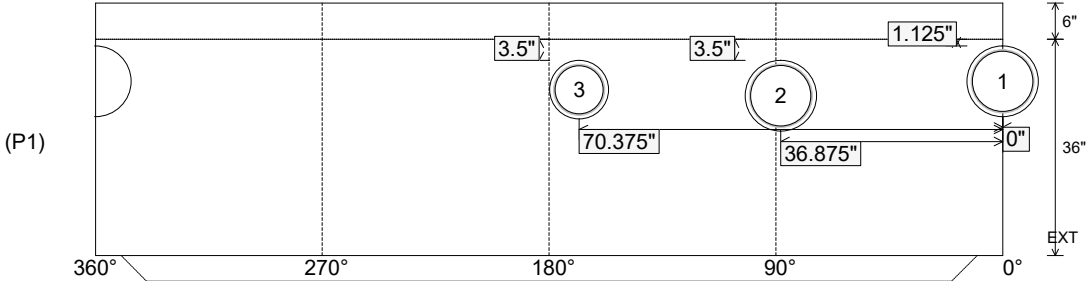

(P1)

360° 270° 180° 90° 0°

6" 36" EXT


3.5" 3.5" 1.125"

70.375" 36.875" 0"


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3722 lb Volume (Net): 0.95cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 8/26/2026 3:45:46 PM		Tech: Jared - F PC: E. Bradley					
Structure ID: T4 SS-MH												
P1 MH048BA36		MH BASE NO STEP T/n										
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 42" P1) 48" - MH BASE NO STEP T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0350 1) A-Lok - 0285					0 lb 270 lb 3000 lb 3722 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb 1 lb ----- Structure Total: 8706 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS 4. CASTING BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 931.04' Rim to Invert: 7.34' Slack: 1.08" Sump: 2" Step Position: 0°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	923.7'	0°	0"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	1.125"	0"		
Invert 2	923.9'	88°	44.5"	10" PVC SDR35	10.5"	A-Lok 0350	11.75"	11.871"	3.5"	0"		
Invert 3	923.9'	168°	85"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	3.5"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												


RIGHT-SIDE UP VIEW (int. dimensions)

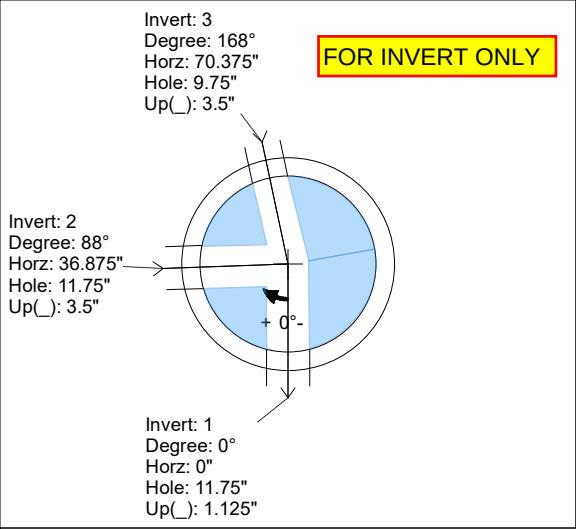

UPSIDE-DOWN VIEW (int. dimensions)

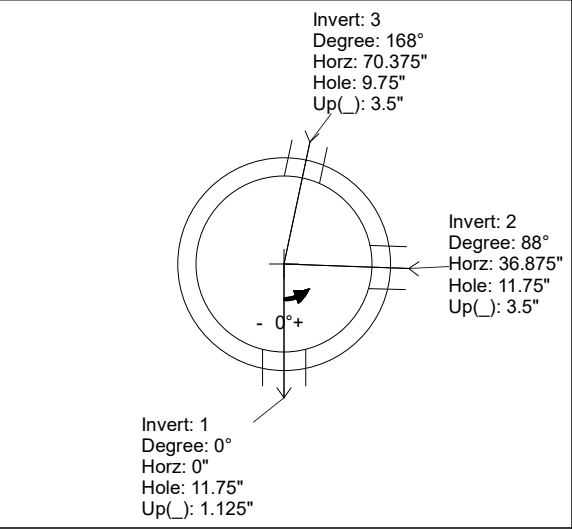

INSIDE WALL DIMENSIONS

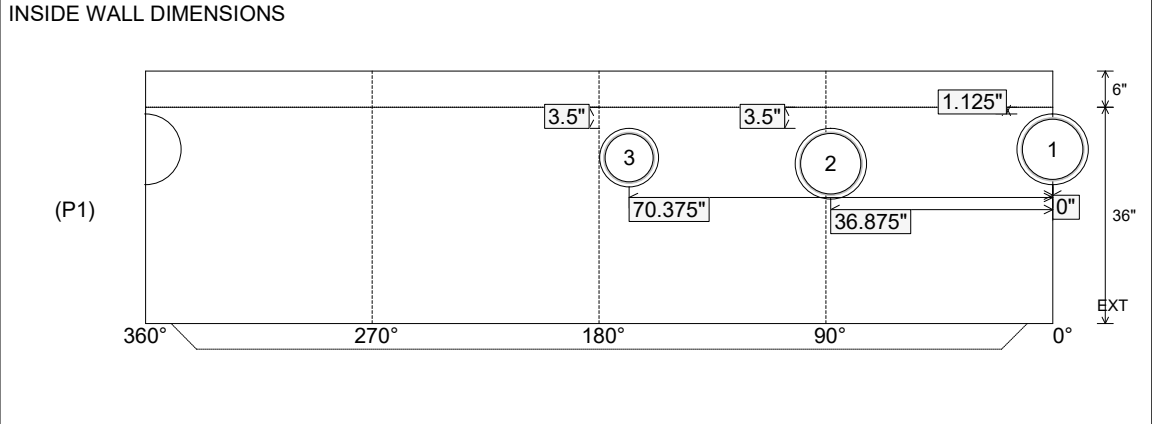

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3722 lb Volume (Net): 0.95cu.yd
----------------------------------	---------------------------------	--	--	--
