

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Slack: 0.72"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 72" - MH FLAT TOP w/24"x36" Hole - 15"
P1) 72" - MH BASE - 60"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 72" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 56
5) MH Step ML-10-TDS-NCR - 10"



0 lb
4530 lb
9413 lb
442 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 14385 lb

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	930.51'							
Reducer								
Invert 1	923.95'	0°	48" HDPE	53.5"	56"	Hole 56	0.05"	P1
Invert 2	923.95'	138°	48" HDPE	53.5"	56"	Hole 56	0.05"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

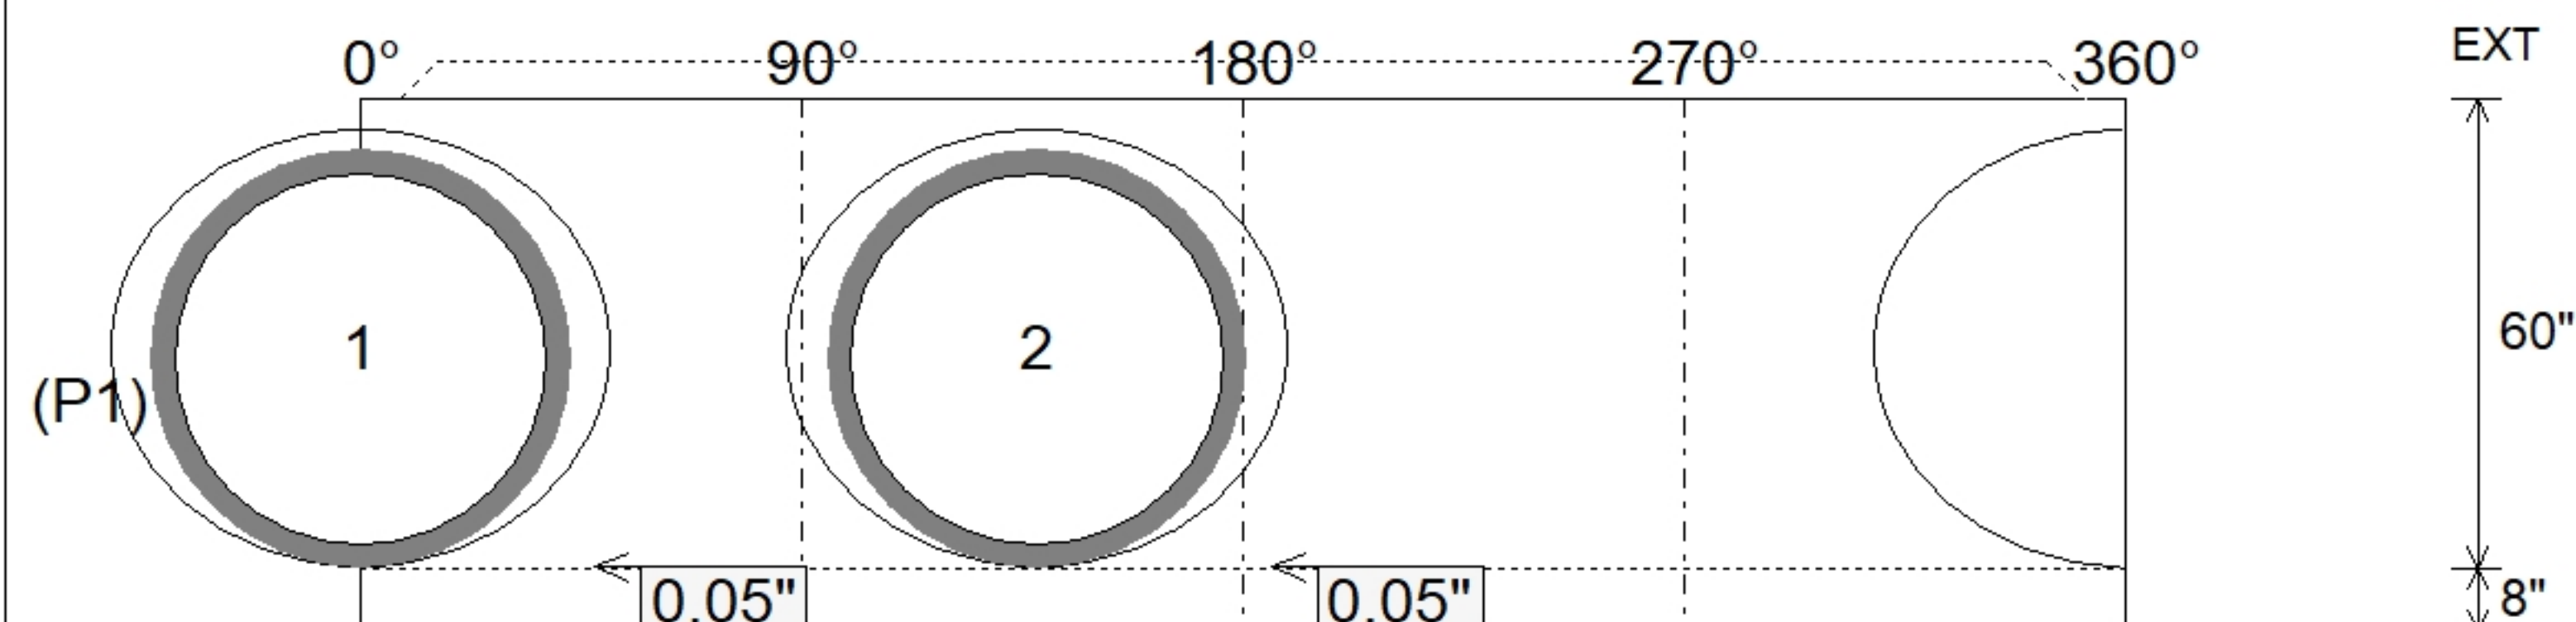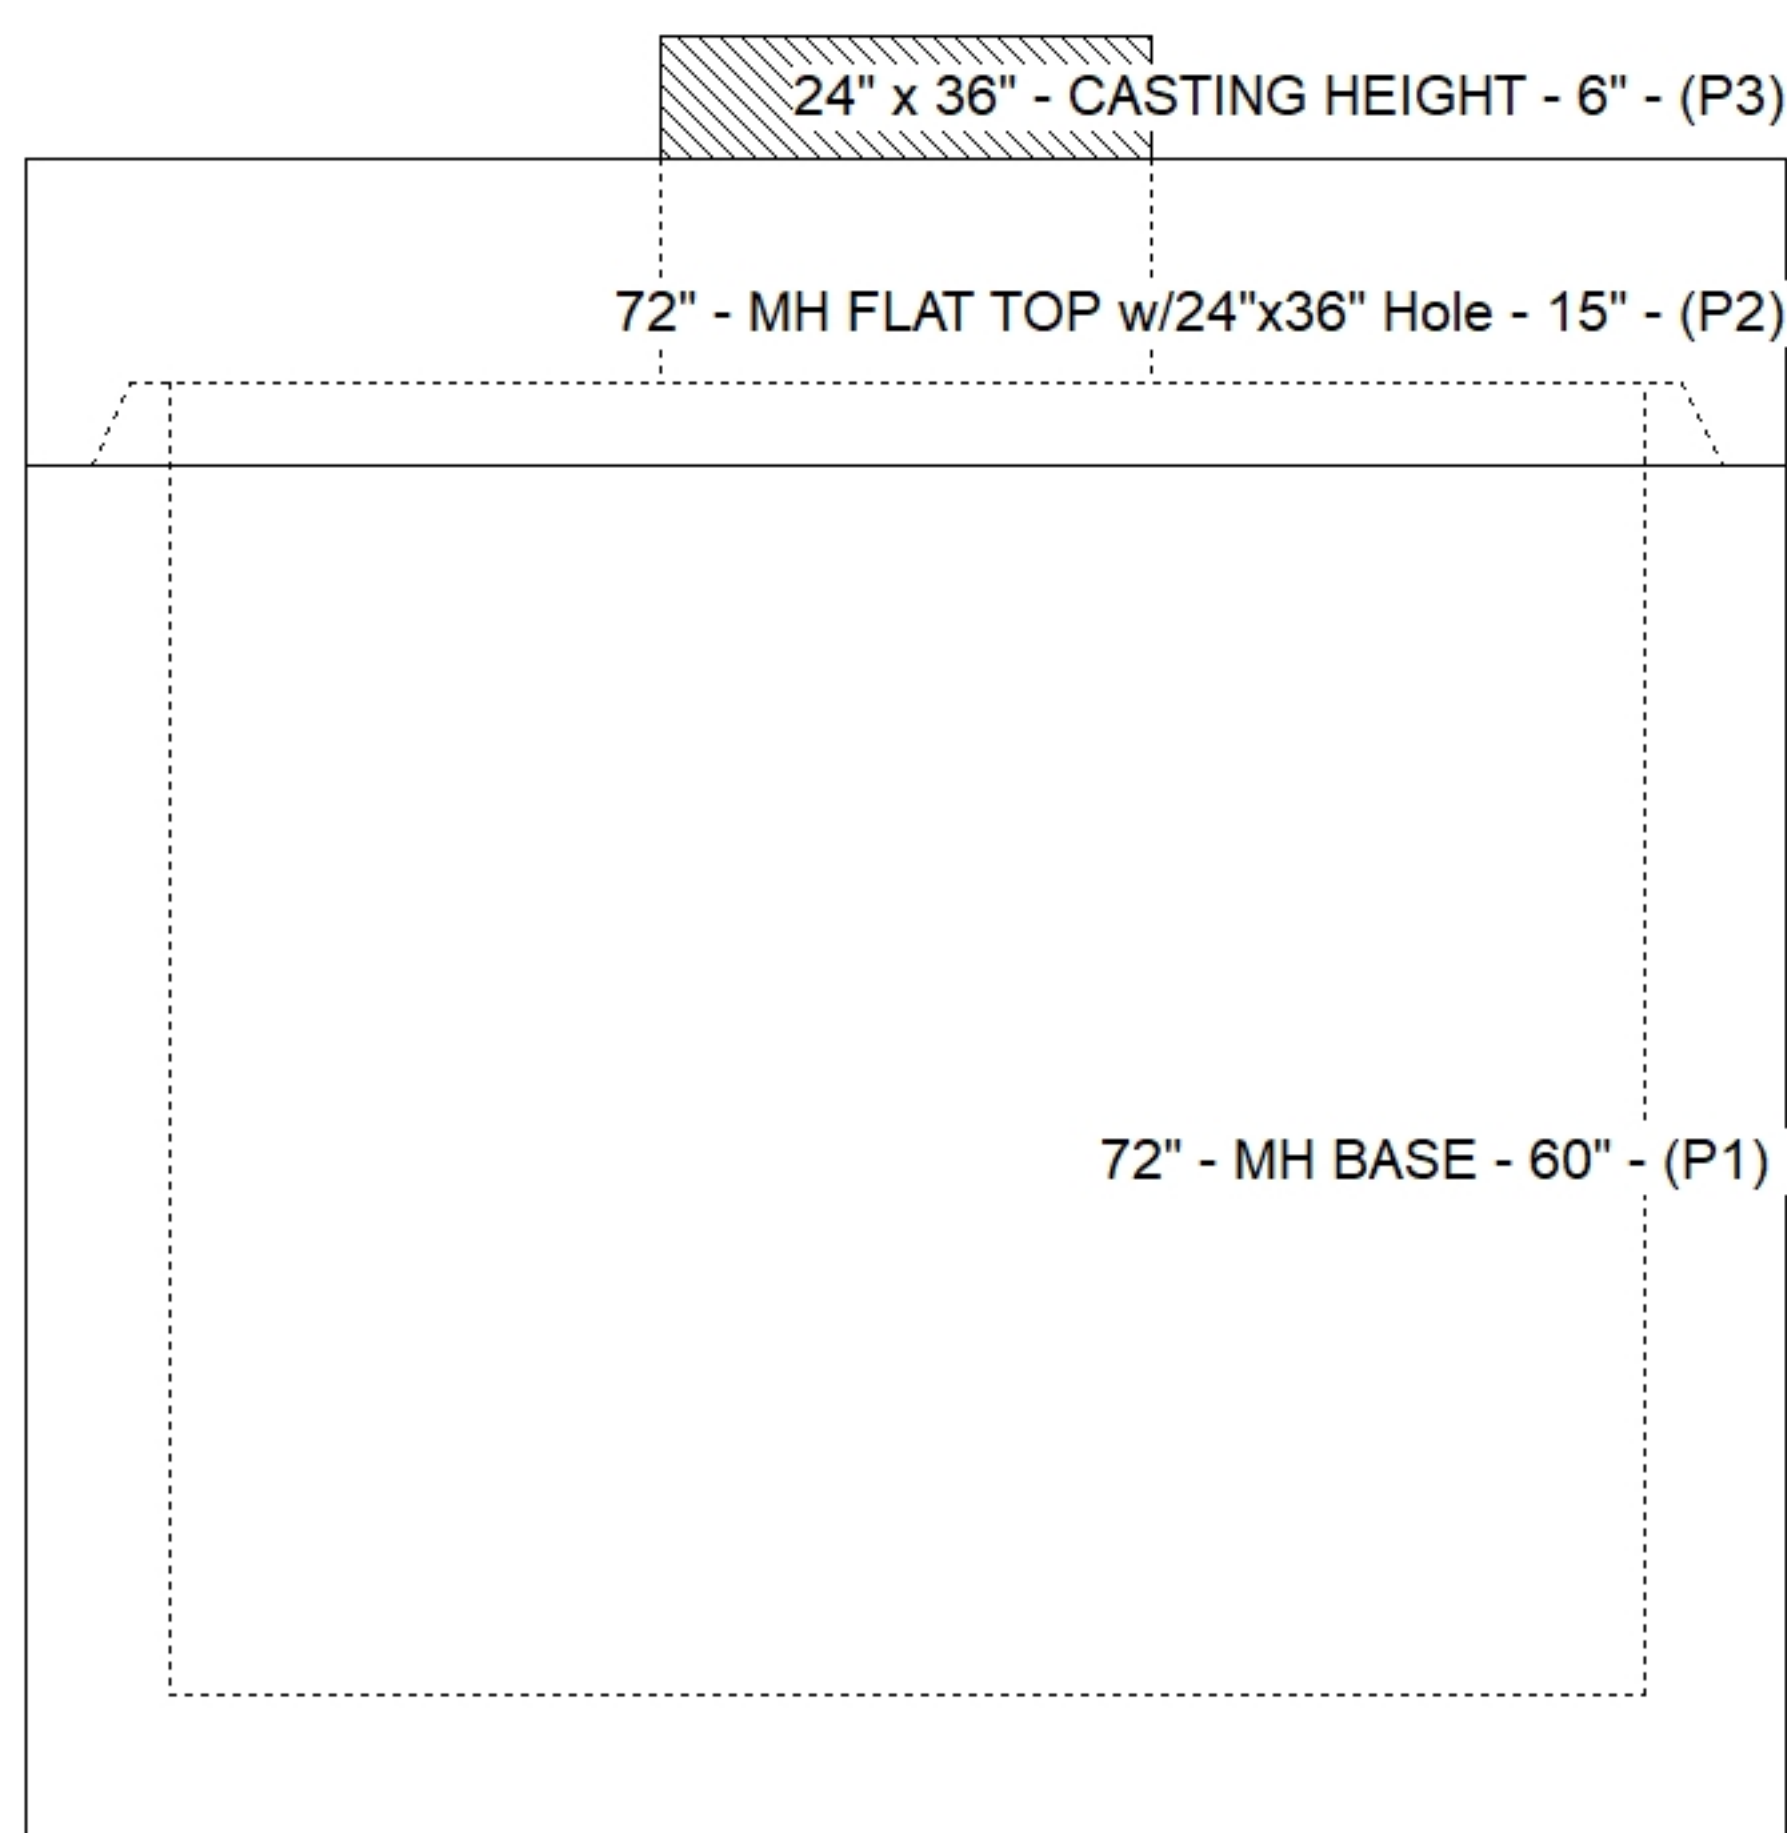

SUBMITTAL
APPROVED BY:
