



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/28/2026 2:21:29 PM		Tech: Jared - F PC: E. Bradley			
Structure ID: A3.10 ST-CI										
P1 MH072BAVF		MH BASE Custom Ht T/n								
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 72" - MH FLAT TOP w/24"x36" Hole F/G - 15" P1) 72" - MH BASE Custom Ht T/n - 79" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 72" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 56 1) Hole - 24 6) MH Step ML-10-TDS-NCR - 10"					0 lb 4530 lb 11913 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 16885 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT) - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 932.92' Rim to Invert: 8.17' Slack: 1.04" Sump: 3" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	924.75'	0°	0"	48" HDPE	53.5"	Hole 56	56"	64.161"	0"	0"
Invert 2	924.75'	180°	135.125"	48" HDPE	53.5"	Hole 56	56"	64.161"	0"	0"
Invert 3	926.99'	270°	202.625"	18" HDPE	21.2"	Hole 24	24"	24.468"	28.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

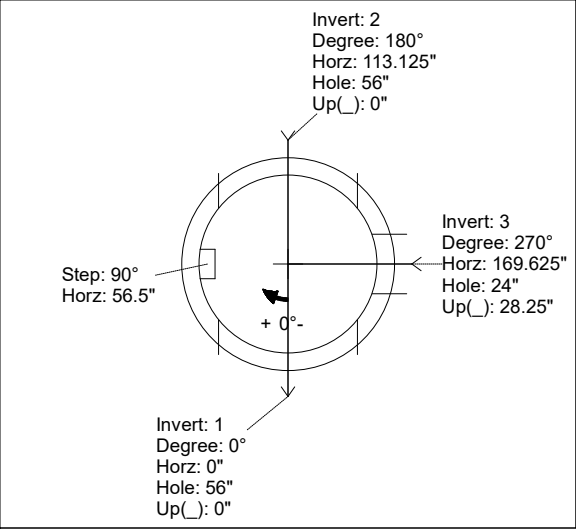

UPSIDE-DOWN VIEW (int. dimensions)

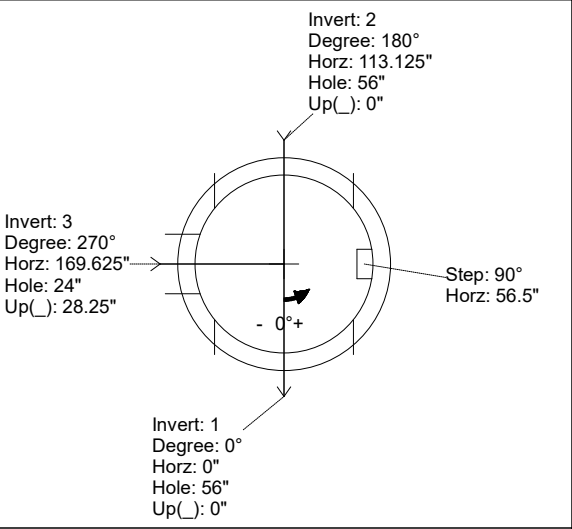

INSIDE WALL DIMENSIONS

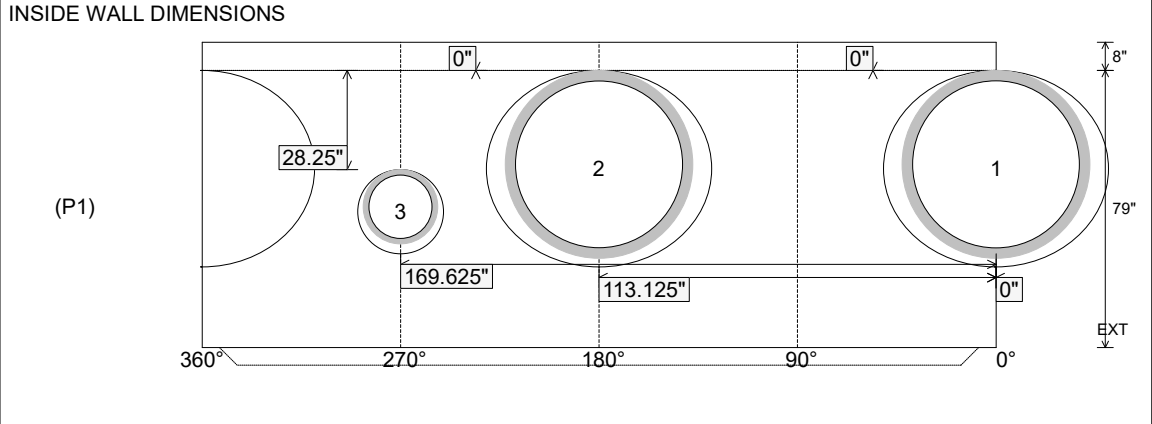

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 7" Floor Height: 8"	Height (Int): 79" Height (Ext): 87"	Weight (Net): 11913 lb Volume (Net): 3.04cu.yd
----------------------------------	---------------------------------	--	--	---
