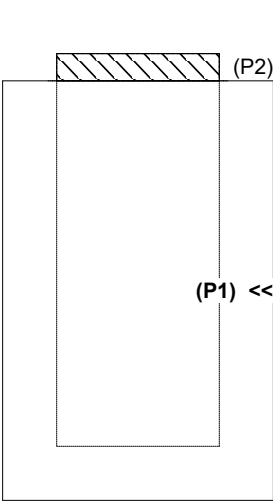
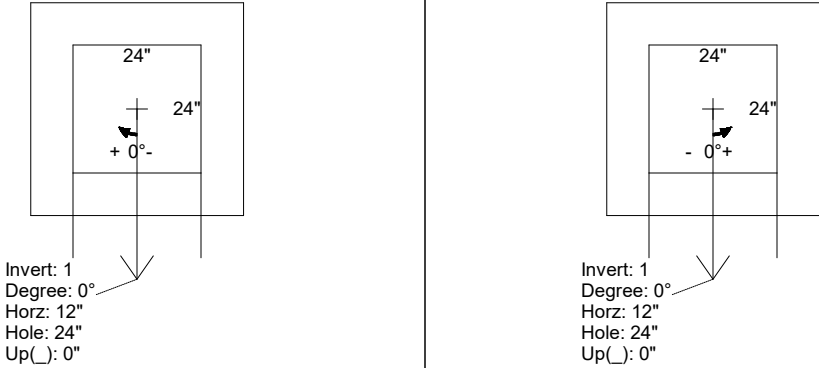
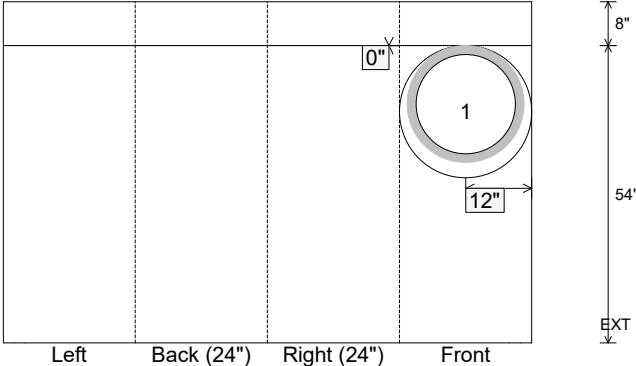


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:27:08 AM		Tech: Jared - F PC: E. Bradley					
Structure ID: A5.10 ST-YD											
P1 BX2424-08BA54				BOX BASE 8inW, 8inF F/n							
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF F/n - 54" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24				0 lb 5486 lb 182 lb 0 lb 0 lb ----- 5668 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 932.5'				Rim to Invert: 4.86'		Slack: 1.92"		Sump: 1.6"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	927.64'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 54" Height (Ext): 62"		Weight (Net): 5486 lb Volume (Net): 1.4cu.yd		
