



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:27:09 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A5.2 ST-YD										
P1 MH048BA54				MH BASE T/n						
P3) 24" x 24" - CASTING HEIGHT - 4" P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12" P1) 48" - MH BASE T/n - 54" 1) CASTING - HOE 280T F/G 1) 48" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24 4) MH Step ML-10-TDS-NCR - 10" Structure Total: 6587 lb						0 lb 1500 lb 4905 lb 182 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 933.7' Rim to Invert: 5.88' Slack: 2.16" Sump: 1.6" Step Position: 90										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	927.82'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

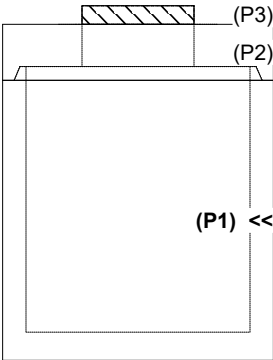


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

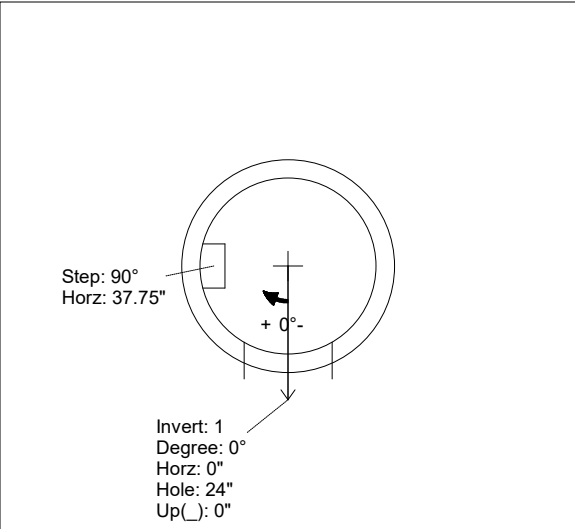

UPSIDE-DOWN VIEW (int. dimensions)

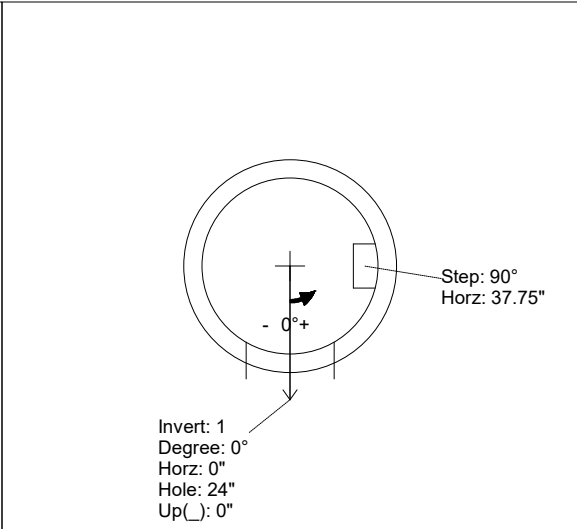

INSIDE WALL DIMENSIONS

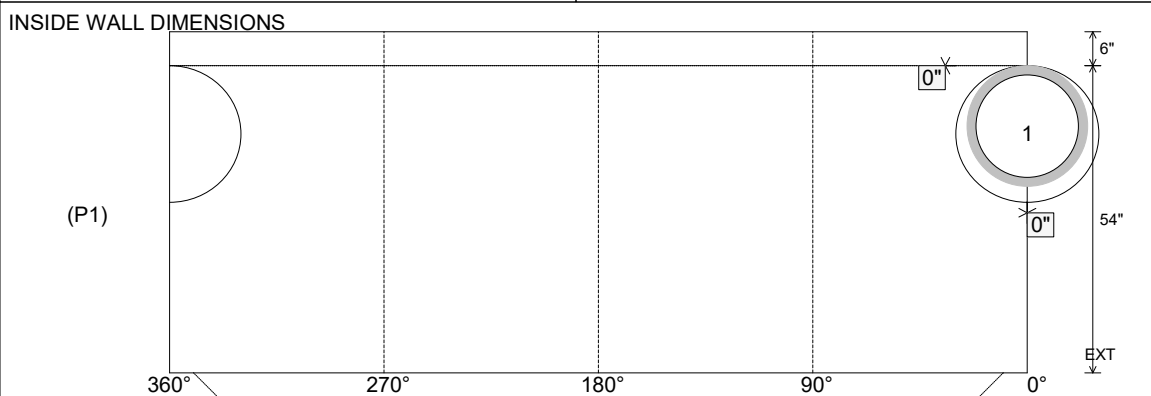

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 54" Height (Ext): 60"	Weight (Net): 4905 lb Volume (Net): 1.25cu.yd
----------------------------------	---------------------------------	--	--	--
