




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:27:07 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A6.10 ST-YD										
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 39" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24"						0 lb 4197 lb 182 lb 0 lb 0 lb ----- 0 lb Structure Total: 4379 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.		
Rim: 932.37' Rim to Invert: 3.58' Slack: 1.56" Sump: 1.6" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	928.79'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



Invert: 1
Degree: 0°
Horz: 12"
Hole: 24"
Up(): 0"



Invert: 1
Degree: 0°
Horz: 12"
Hole: 24"
Up(): 0"

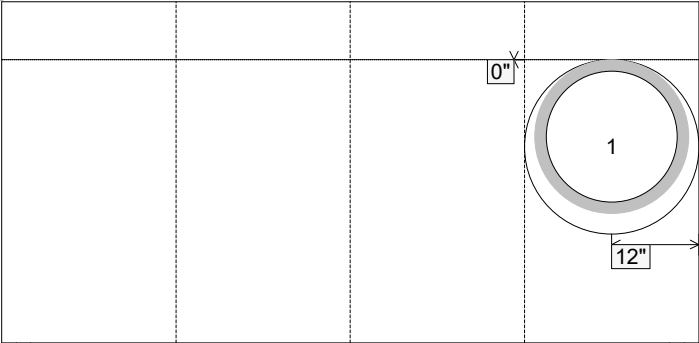

(P1)

8"
39"
12"
EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 39" Height (Ext): 47"	Weight (Net): 4197 lb Volume (Net): 1.07cu.yd
----------------------------------	-------------------------------	--	--	--
