

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Slack: 1.1"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
- P1) 48" - MH BASE Custom Ht - 35"
- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 48" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 30
- 1) Hole - 20
- 3) MH Step ML-10-TDS-NCR - 10"



0 lb
1300 lb
3324 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 5066 lb

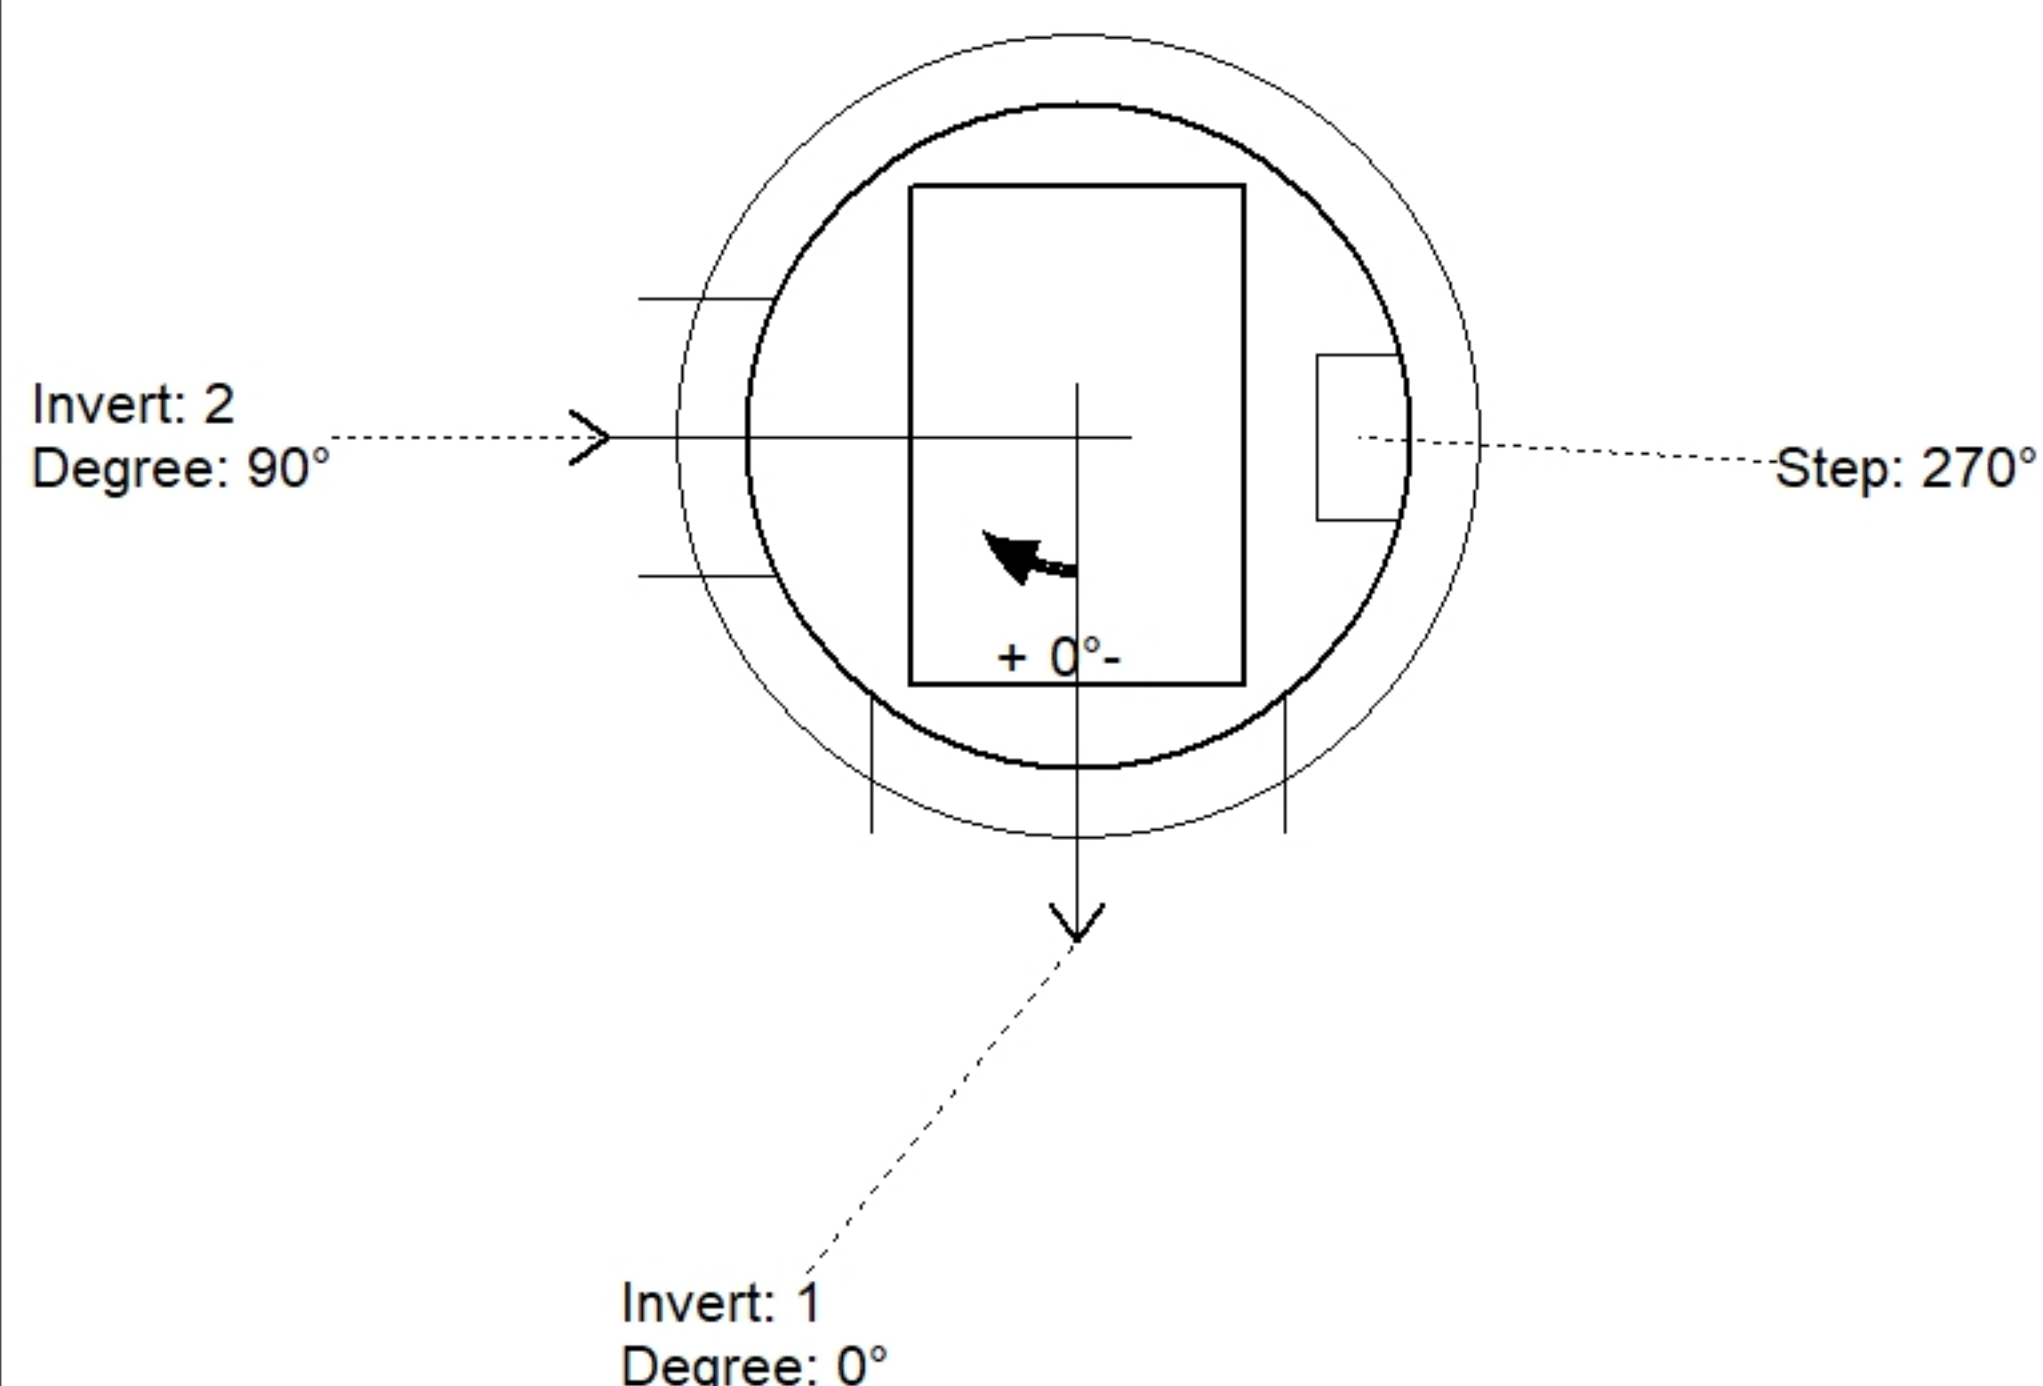

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	934.07'							
Reducer								
Invert 1	929.72'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	930.25'	90°	15" HDPE	17.6"	20"	Hole 20	6.96"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

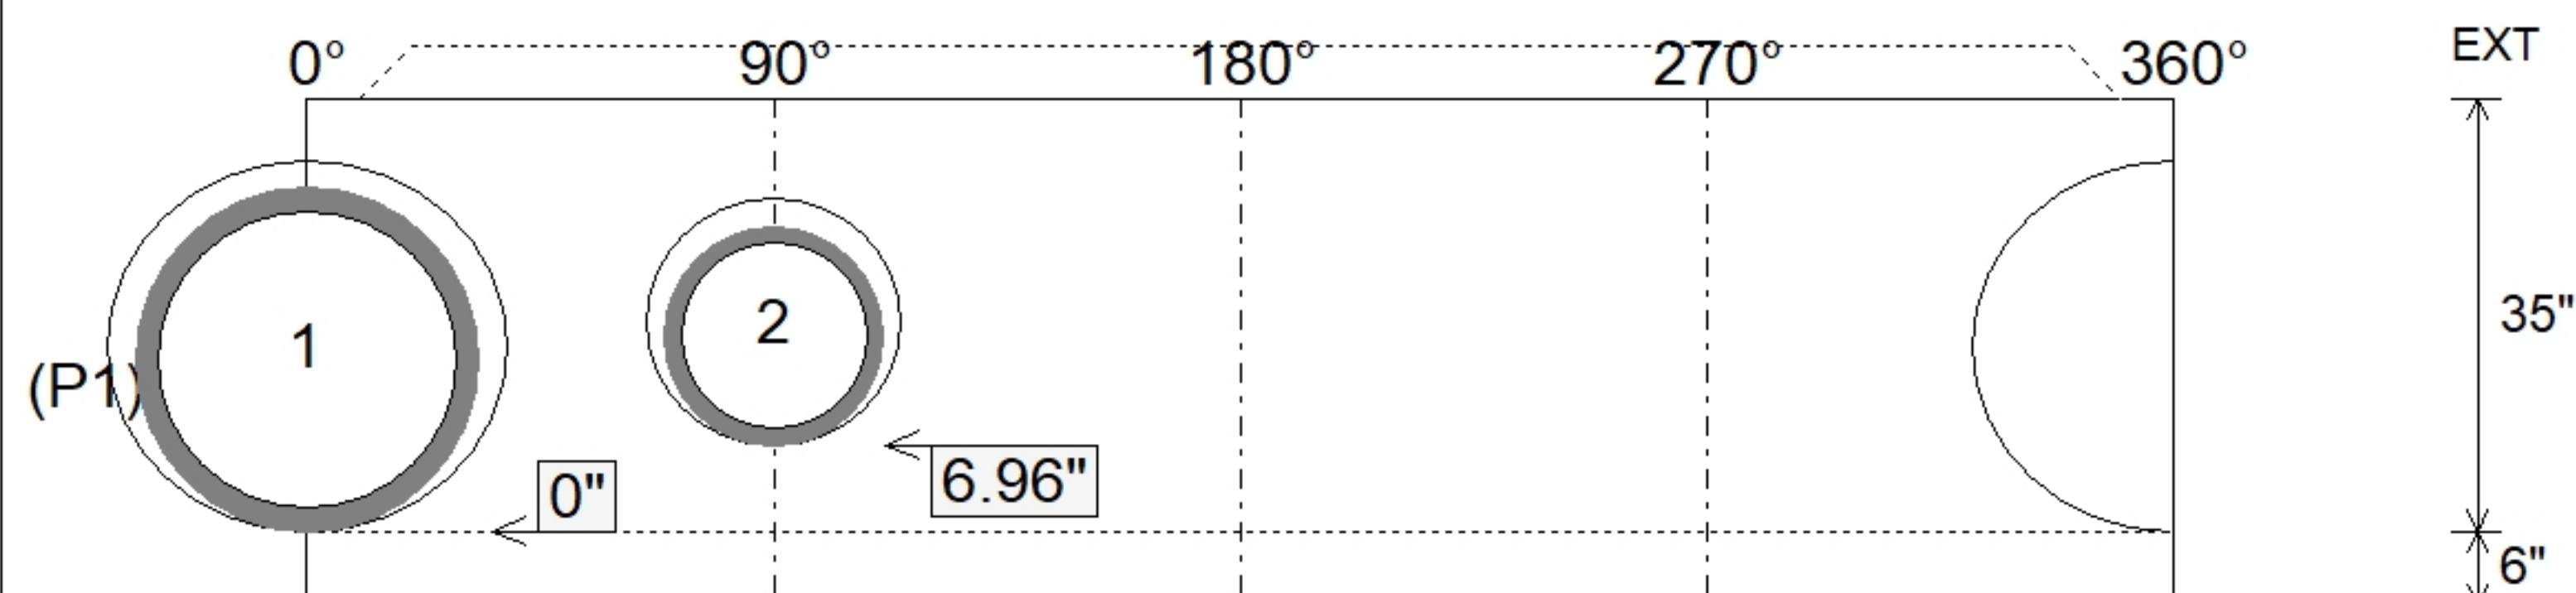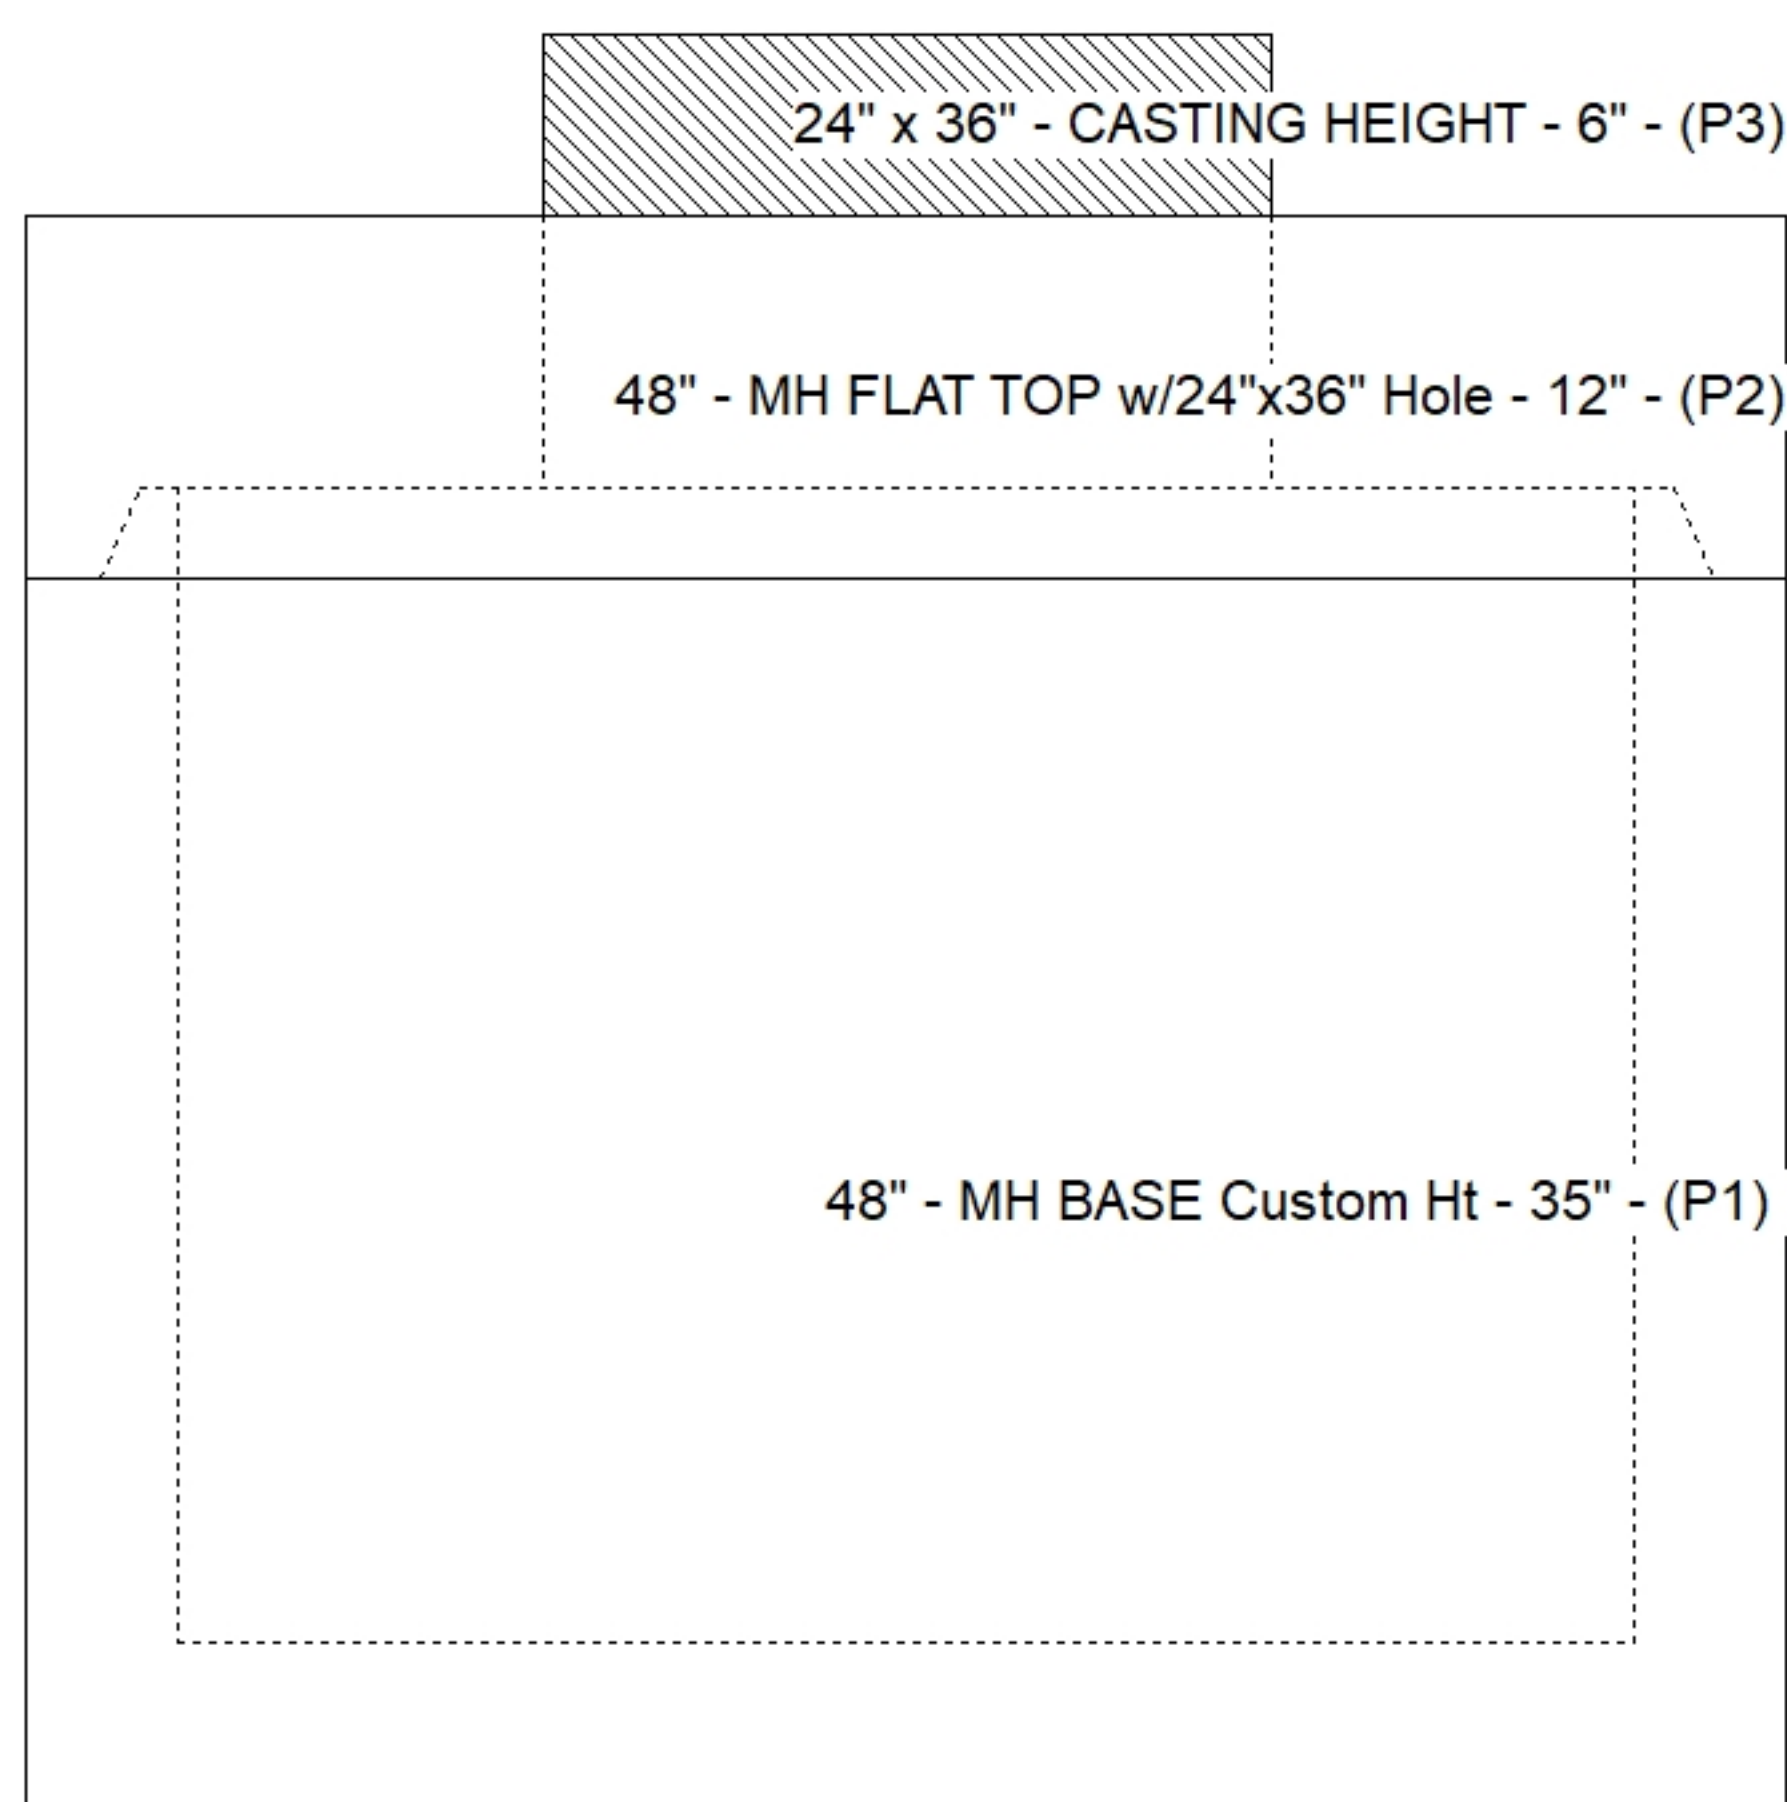

Submittal Drawing
9/29/2026 8:25:52 AM

SUBMITTAL
APPROVED BY:
