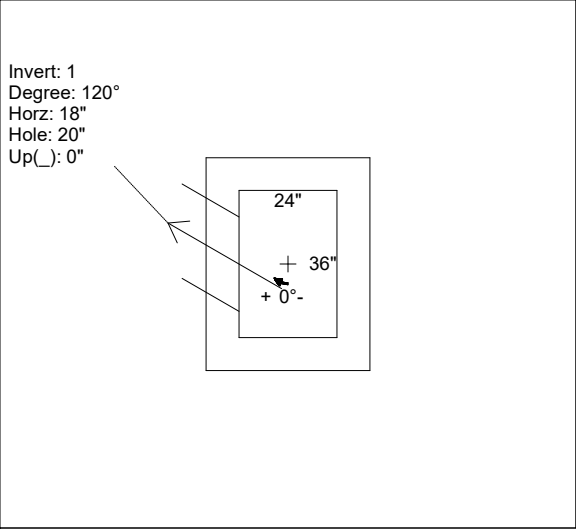
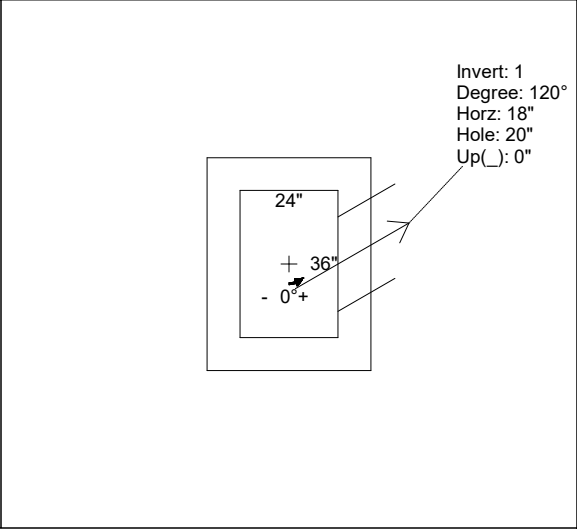
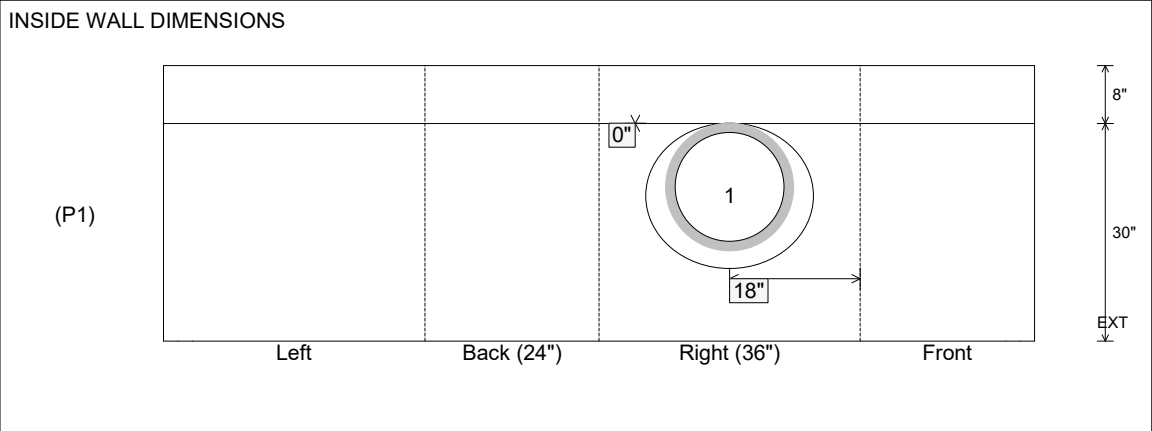


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:31:40 AM		Tech: Jared - F PC: E. Bradley					
Structure ID: A6.6 ST-CI											
P1 BX2436-08BA30				BOX BASE 8inW, 8inF F/n							
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 30" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 20				0 lb 4214 lb 442 lb 0 lb 0 lb ----- 0 lb Structure Total: 4656 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)) . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 934.66'				Rim to Invert: 3.05'		Slack: 1.85"		Sump: 1.25"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	931.61'	120°	30.625"	15" HDPE	17.6"	Hole 20	20"	23.094"	0"	-6"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 30" Height (Ext): 38"		Weight (Net): 4214 lb Volume (Net): 1.08cu.yd	
