

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 60"

Rim to Invert: 5.8'

Floor Height: 8"

Slack: 2.475"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


- P4) 24" x 36" - CASTING HEIGHT - 6"
- P3) 24" x 36" - GRADE RING - 3"
- P2) 60" - MH FLAT TOP w/24"x36" Hole - 13"
- P1) 60" - MH BASE - 48"
- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 60" - Conseal CS-102 1.00"
- 2) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 44
- 1) Hole - 30
- 1) Hole - 38
- 4) MH Step ML-10-TDS-NCR - 10"

0 lb
306 lb
3499 lb
5923 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 10170 lb

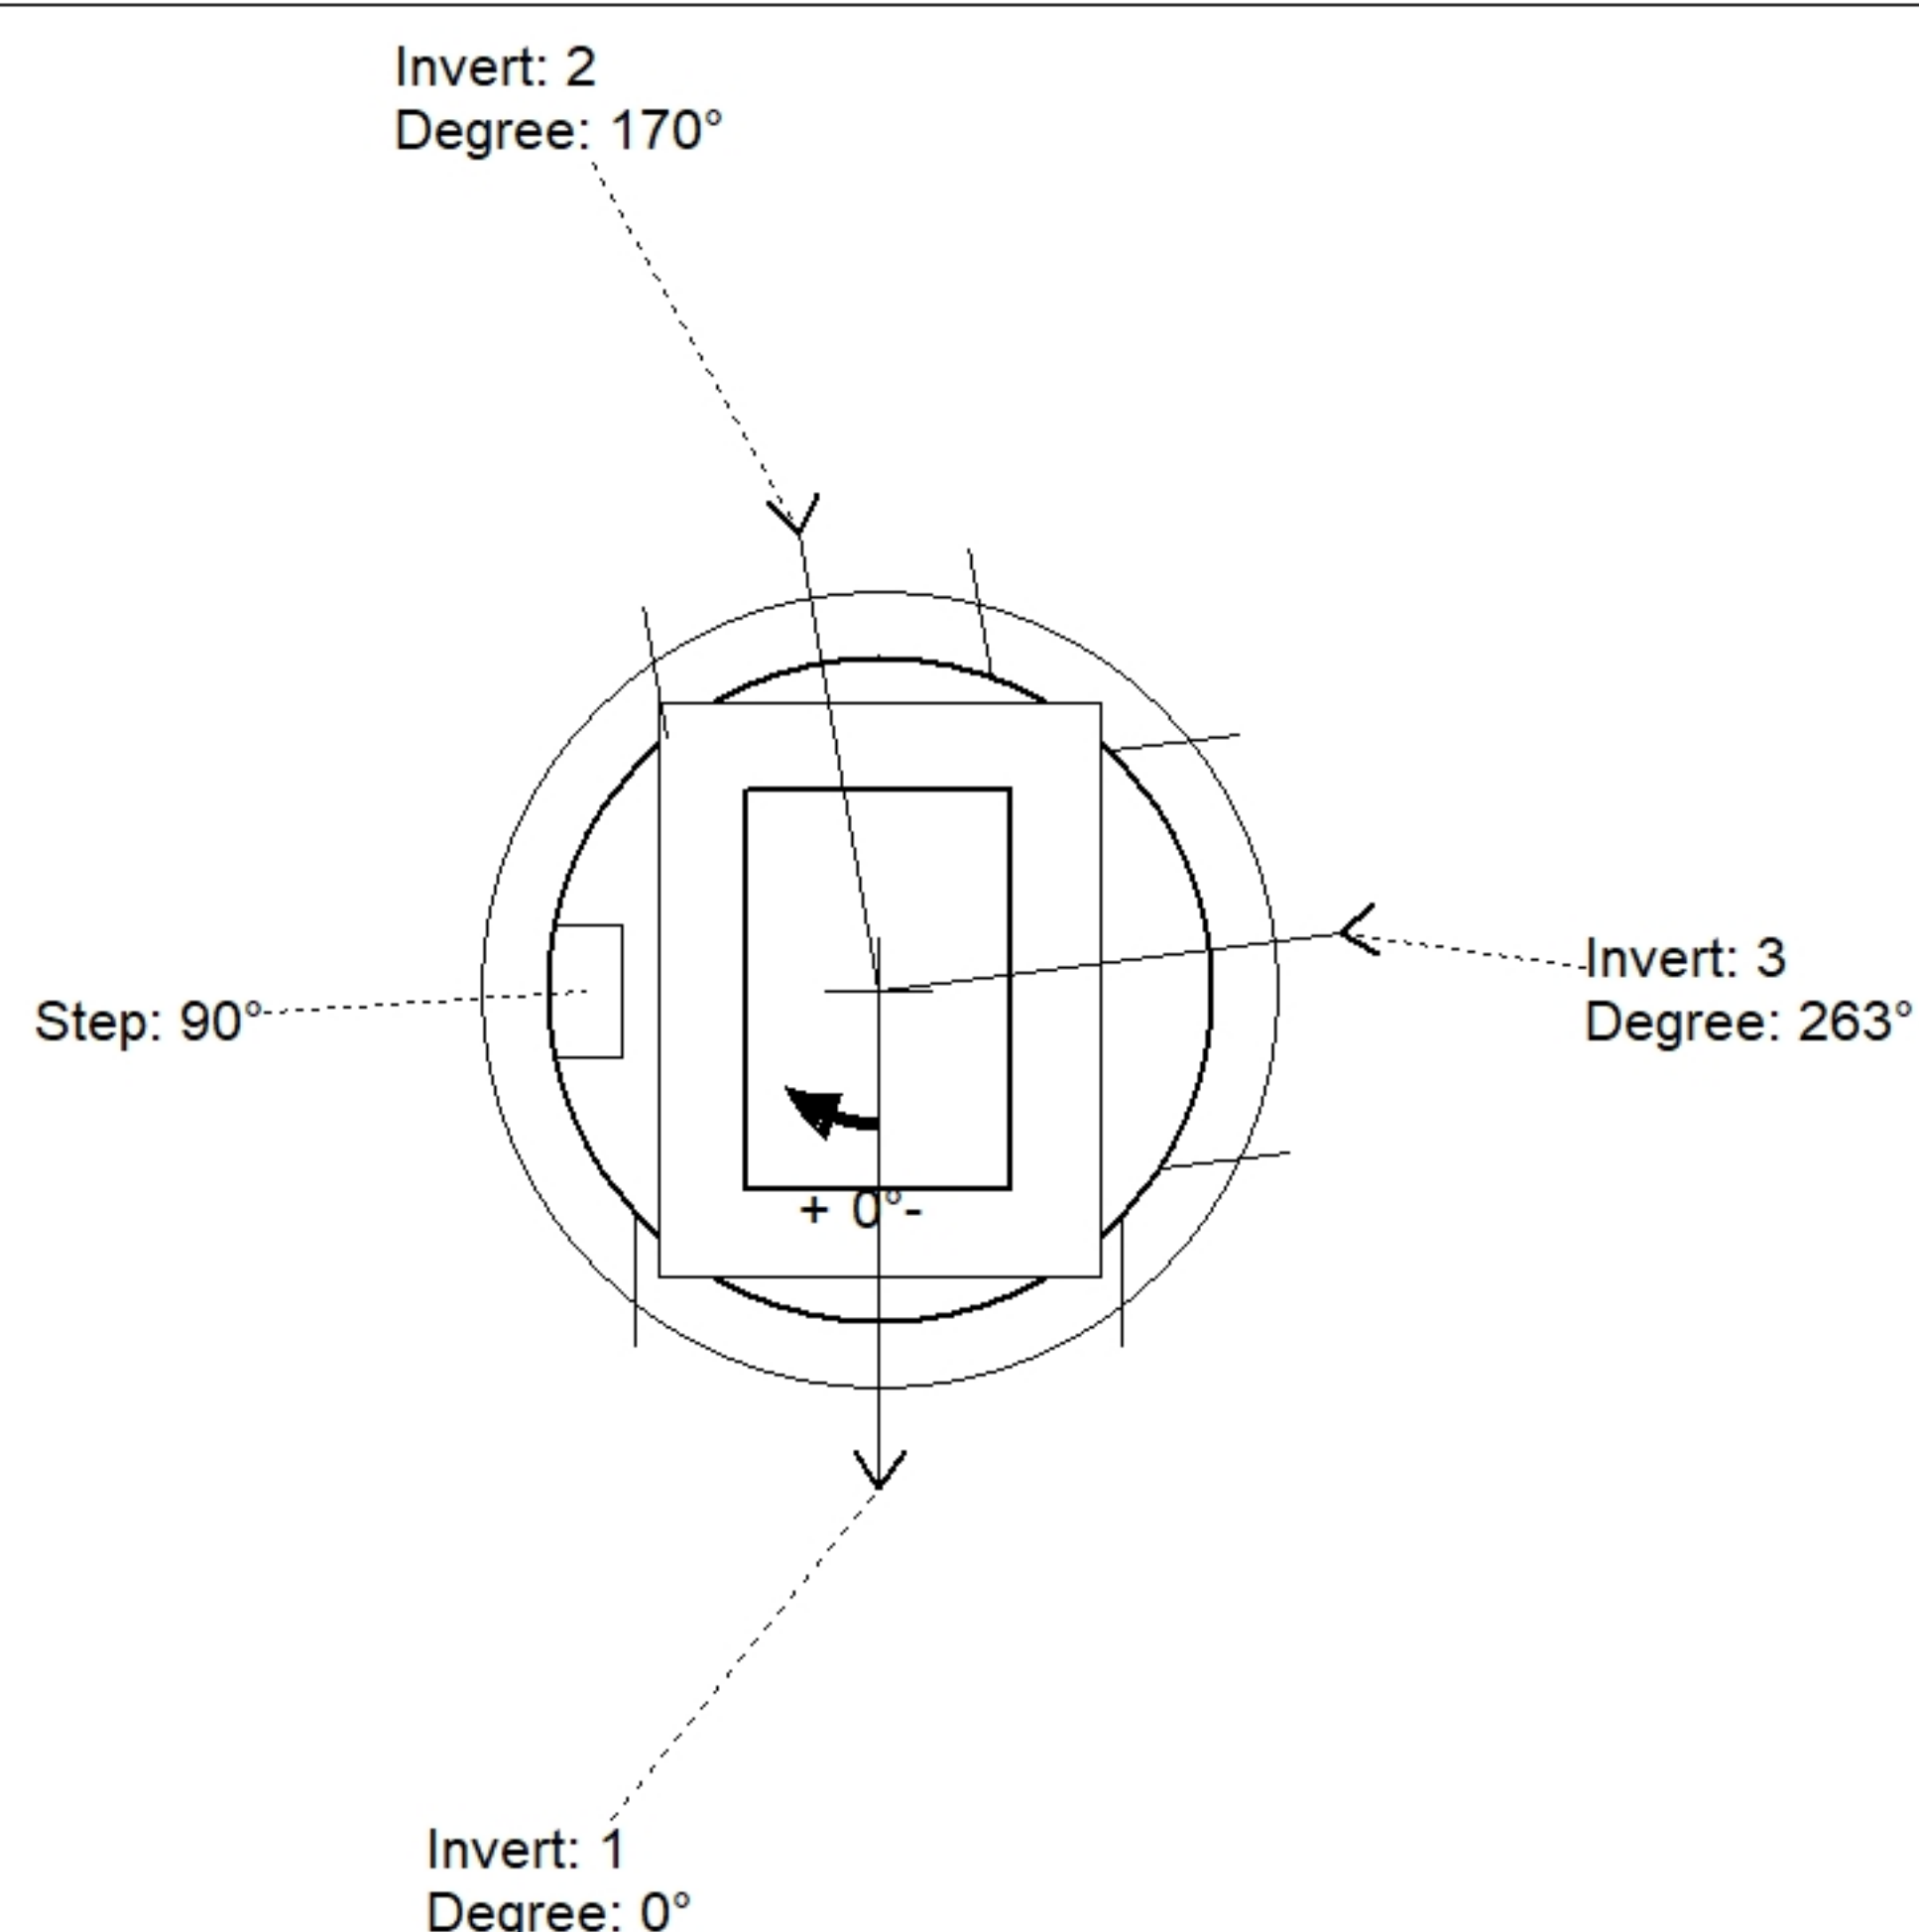

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	935.16'							
Reducer								
Invert 1	929.36'	0°	36" HDPE	41.7"	44"	Hole 44	0.025"	P1
Invert 2	929.36'	170°	24" HDPE	27.8"	30"	Hole 30	0.975"	P1
Invert 3	929.36'	263°	30" HDPE	35.1"	38"	Hole 38	0.325"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

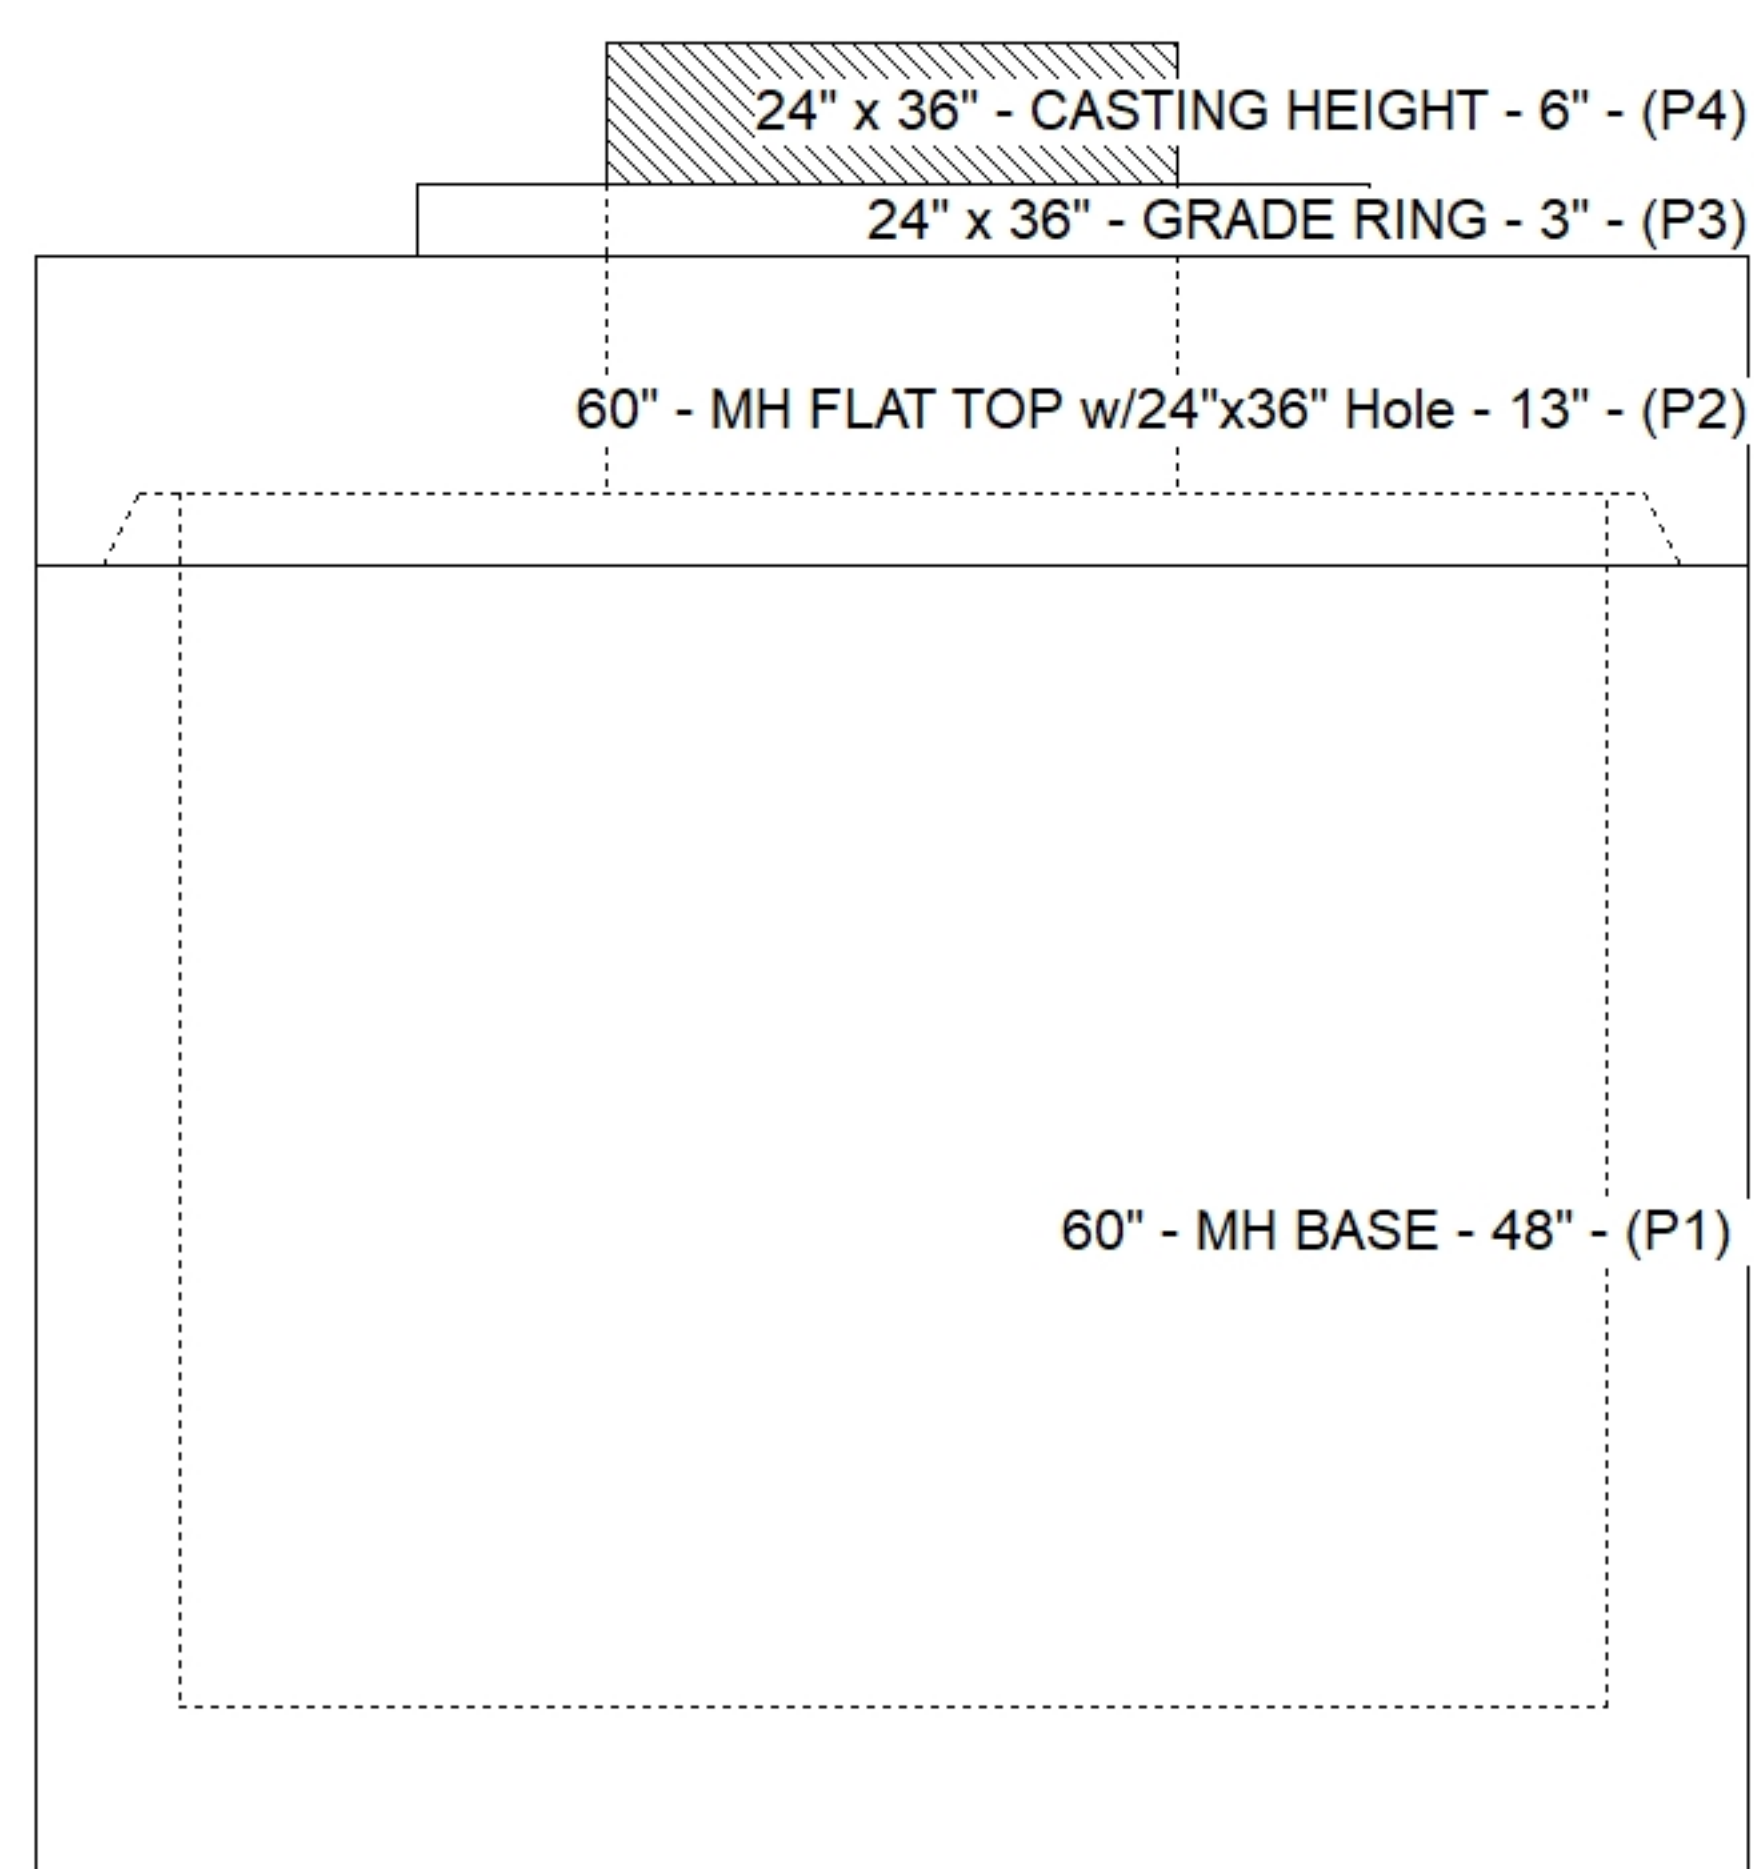

Default - Interior Dimensions

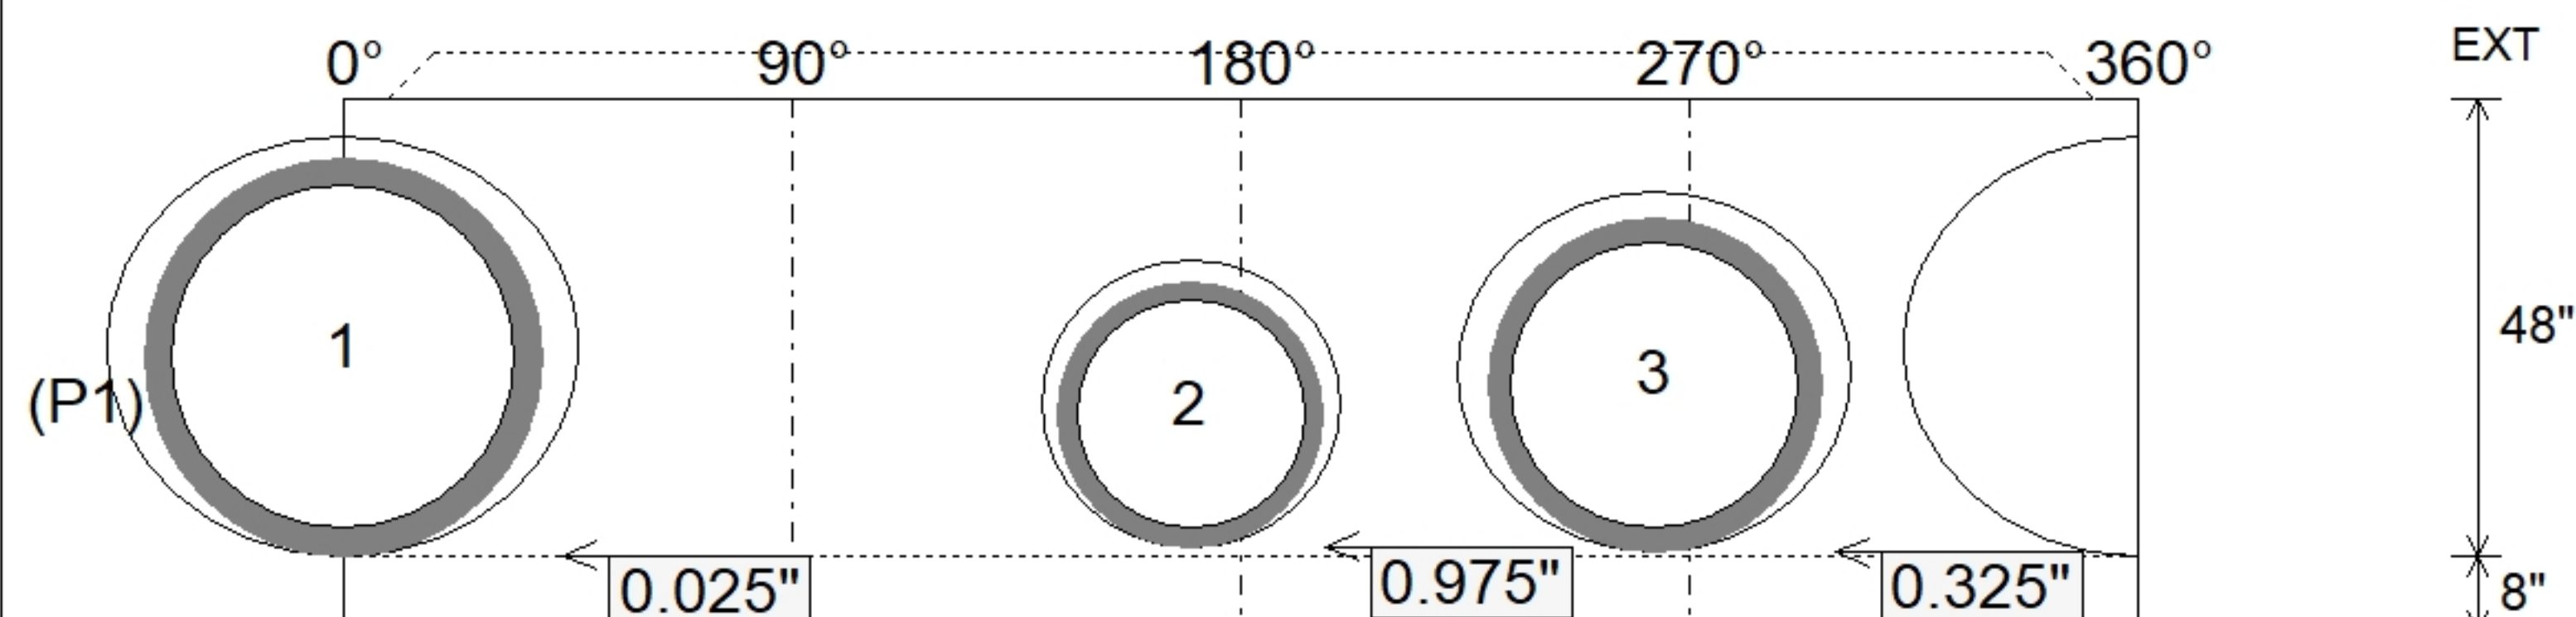

Submittal Drawing
9/29/2026 8:25:50 AM

SUBMITTAL
APPROVED BY:
