

Contractor: KY Earthworks

Plant: 100



Slack: 1.23"

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 60" - MH FLAT TOP w/24"x36" Hole - 8"
P1) 60" - MH BASE Custom Ht - 37"

- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 60" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) DOGHOUSE INVRTD - 38"x37"
- 2) Hole - 24
- 1) Hole - 20
- 3) MH Step ML-10-TDS-NCR - 10"



0 lb
2153 lb
5293 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 7889 lb

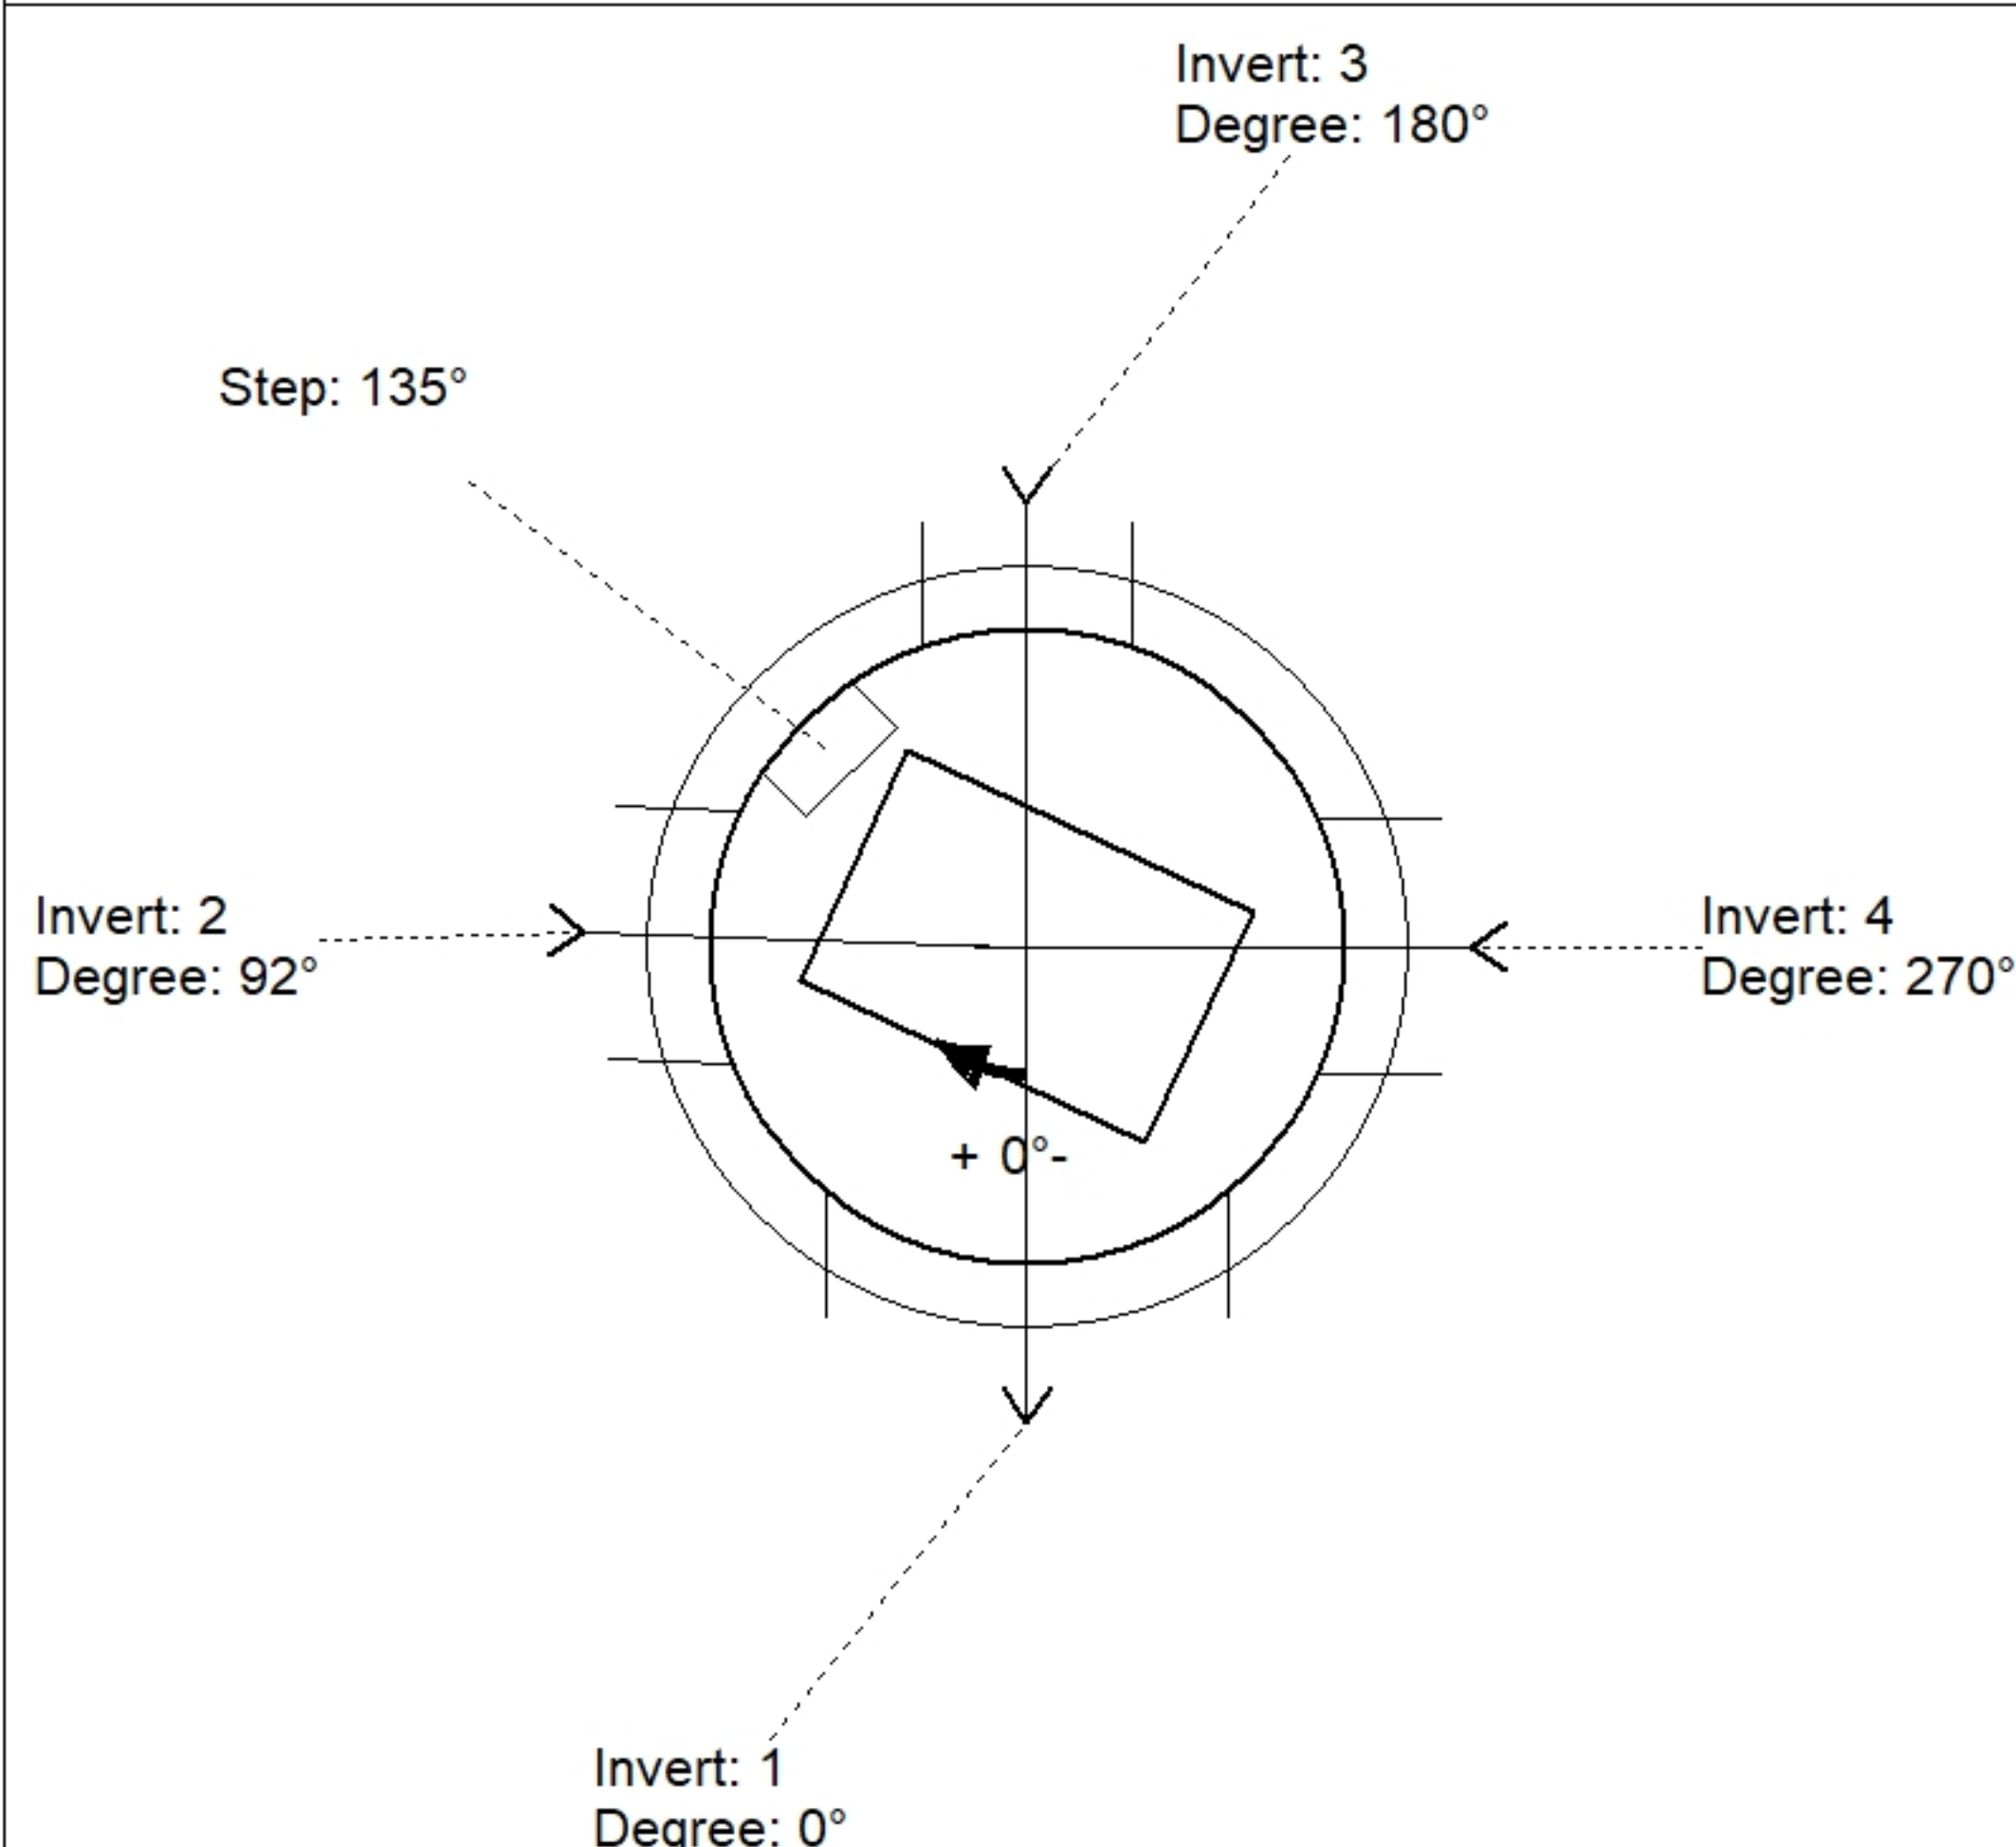

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	934.59'							
Reducer								
Invert 1	930.45'	0°	30" HDPE	35.1"	38" x 37"	DOGHOUSE INVRTD 38"x37"	0"	P1
Invert 2	930.58'	92°	18" HDPE	21.2"	24"	Hole 24	2.51"	P1
Invert 3	930.45'	180°	15" HDPE	17.6"	20"	Hole 20	1.25"	P1
Invert 4	930.58'	270°	18" HDPE	21.2"	24"	Hole 24	2.51"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

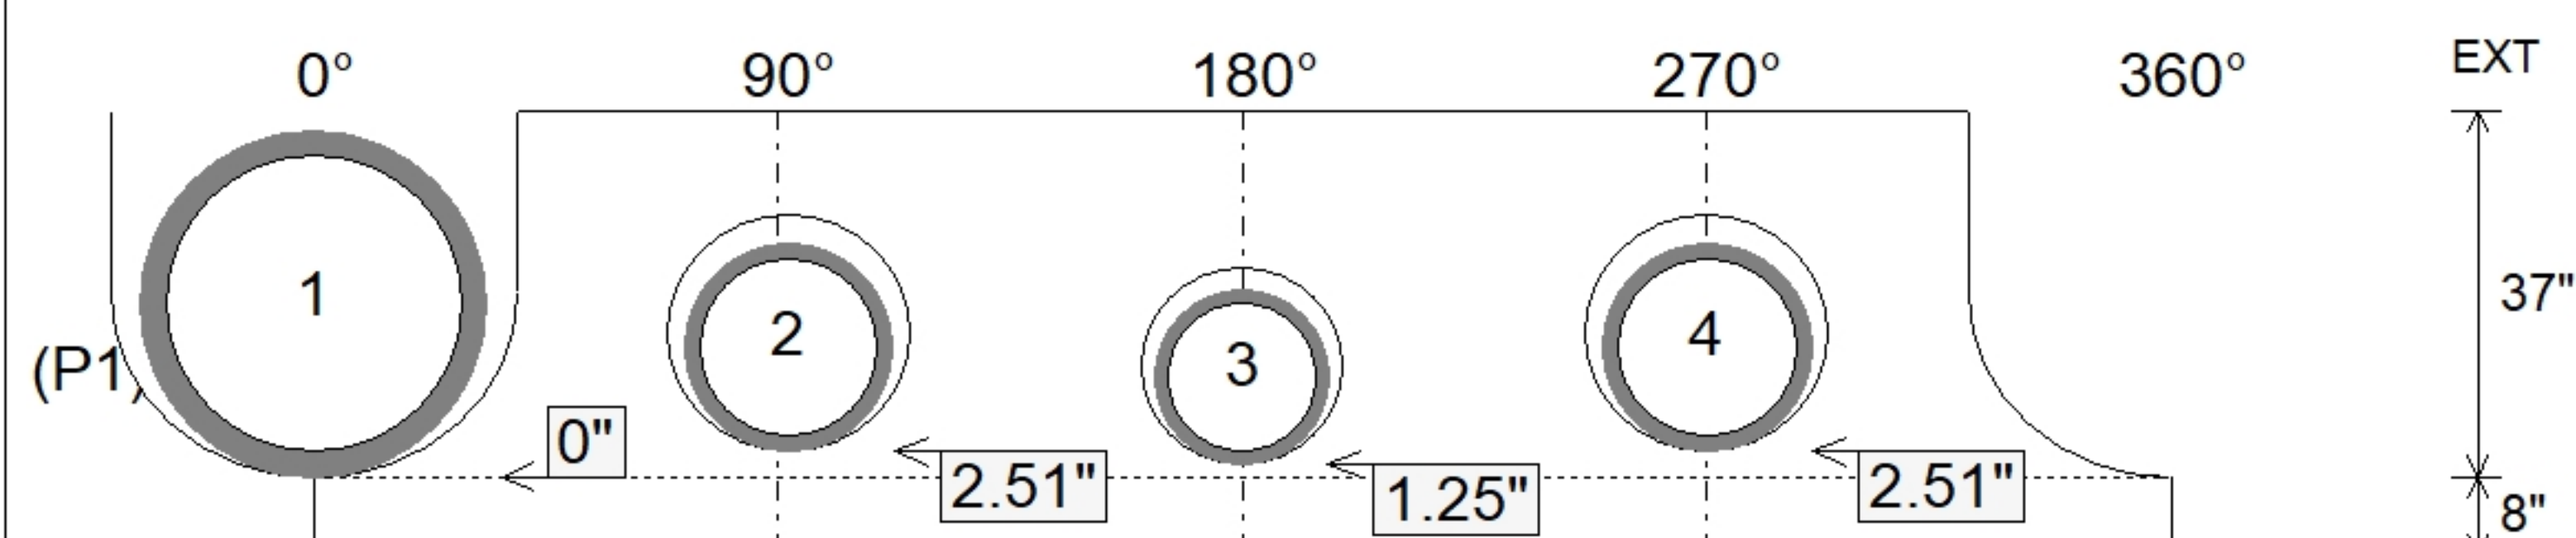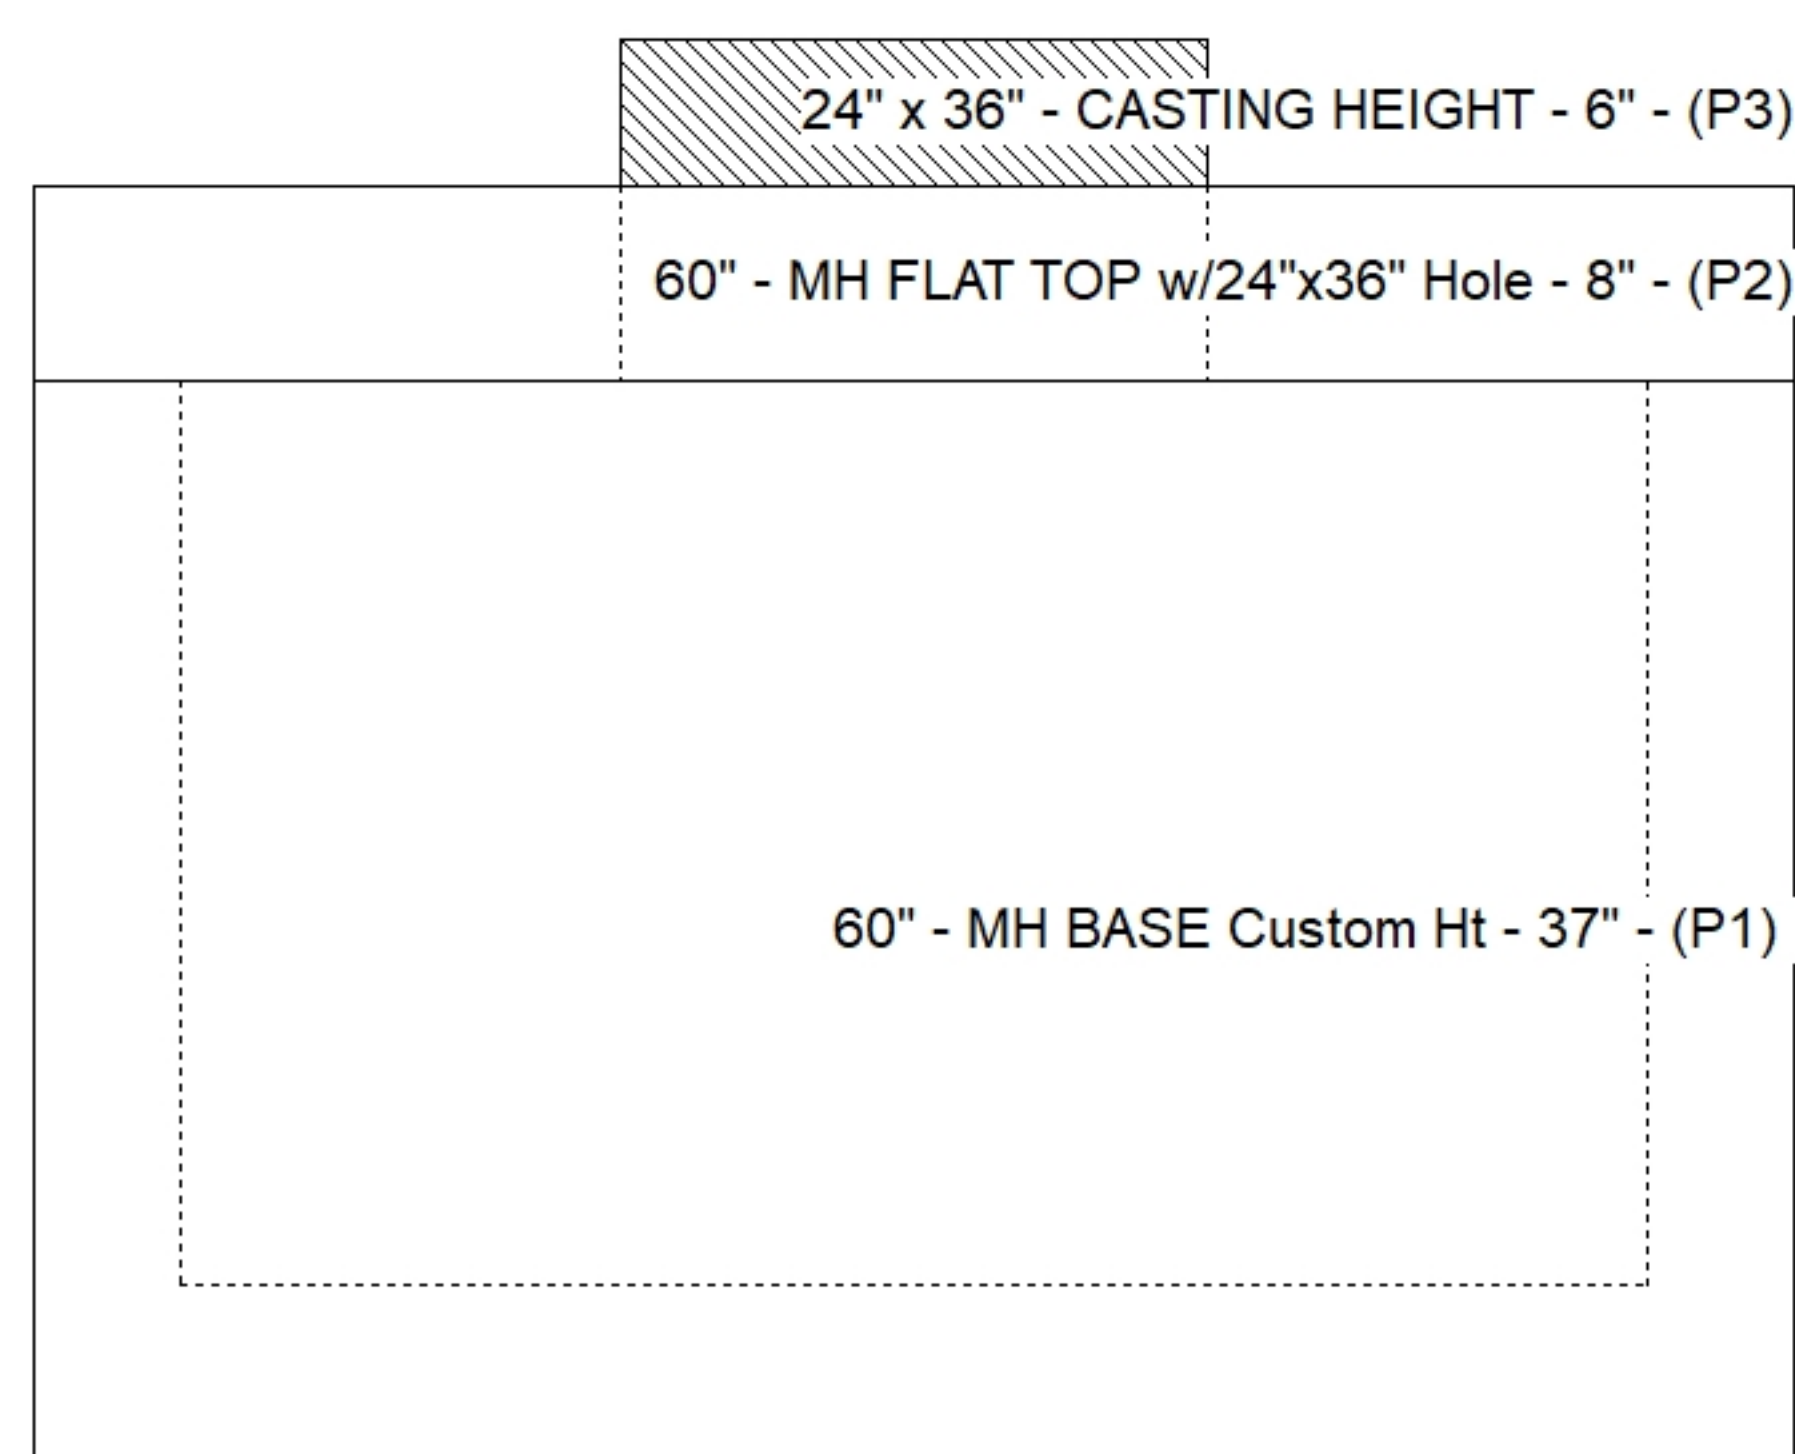

SUBMITTAL
APPROVED BY:
