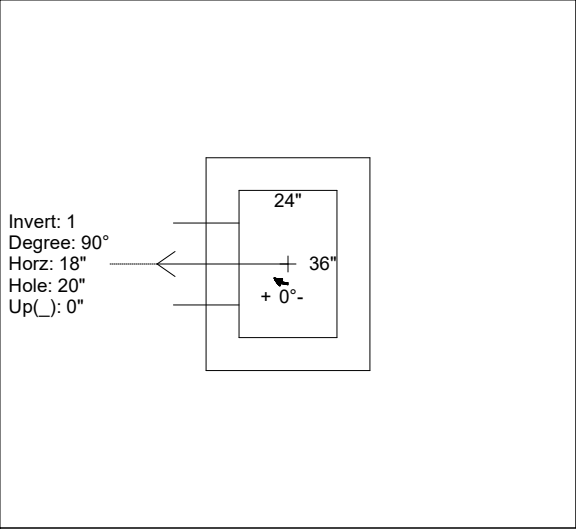
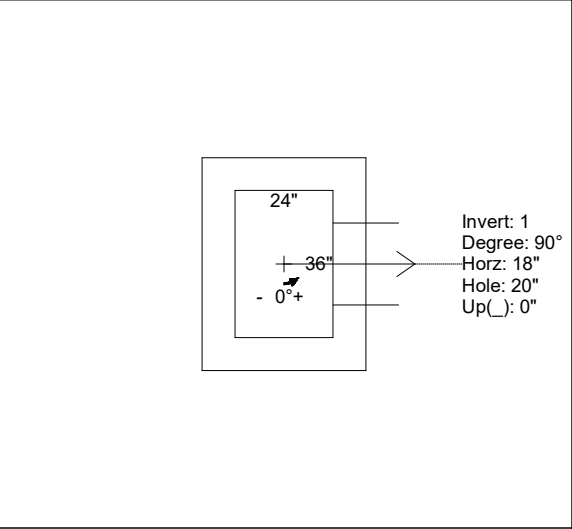
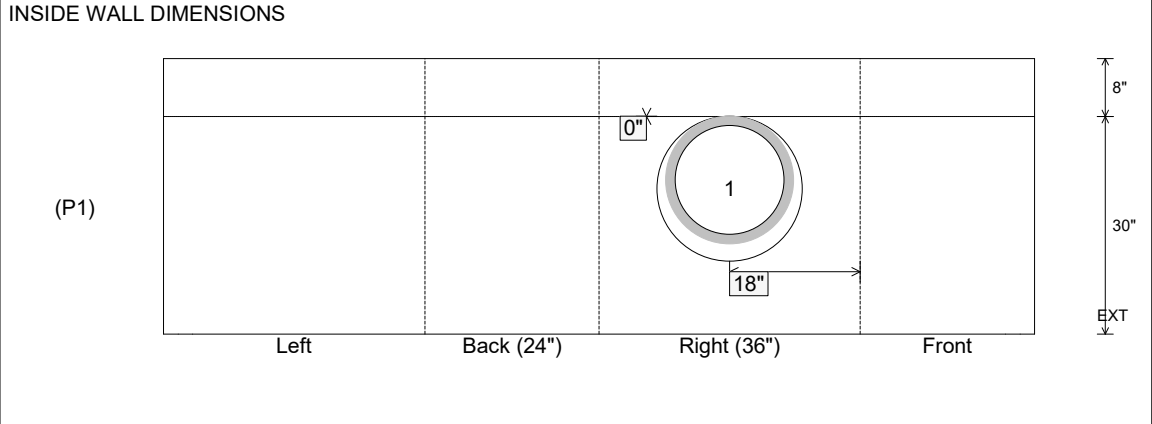


Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:31:33 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: A8.5 ST-CI										
P1 BX2436-08BA30 BOX BASE 8inW, 8inF F/n										
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 30" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 20					0 lb 4247 lb 442 lb 0 lb 0 lb ----- 0 lb Structure Total: 4689 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 934.34' Rim to Invert: 3.04' Slack: 1.73" Sump: 1.25" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	931.3'	90°	26"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 										
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 30" Height (Ext): 38"		Weight (Net): 4247 lb Volume (Net): 1.08cu.yd	
