



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:27:02 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: C3 ST-YD										
P1 MH048BA42		MH BASE T/n								
P4) 24" x 24" - CASTING HEIGHT - 4" P3) 24" x 24" - GRADE RING F/F - 3" P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12" P1) 48" - MH BASE T/n - 42" 1) CASTING - HOE 280T F/G 1) 48" - Conseal CS-102 1.00" 2) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 30 3) MH Step ML-10-TDS-NCR - 10"					0 lb 258 lb 1500 lb 3632 lb 182 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5572 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 931.15' Rim to Invert: 5.08' Slack: 1.86" Sump: 1.9" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	926.07'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"
Invert 2	926.07'	180°	91.125"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

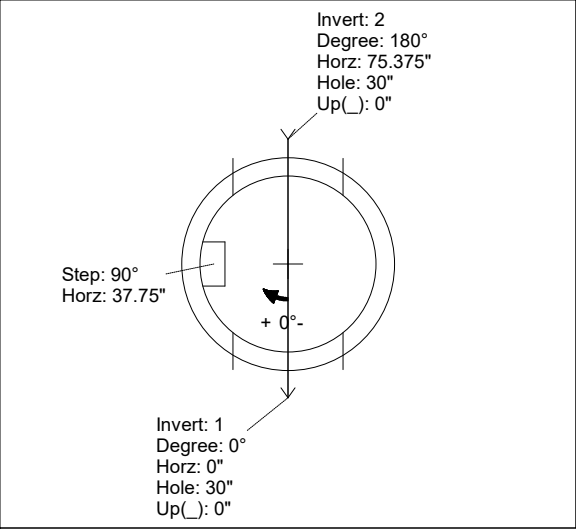

UPSIDE-DOWN VIEW (int. dimensions)

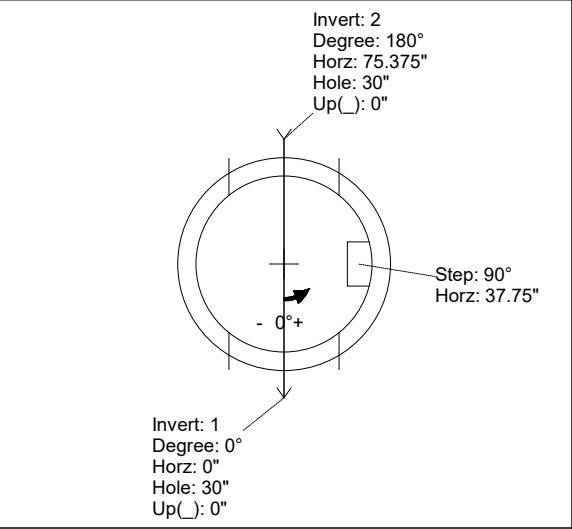

INSIDE WALL DIMENSIONS

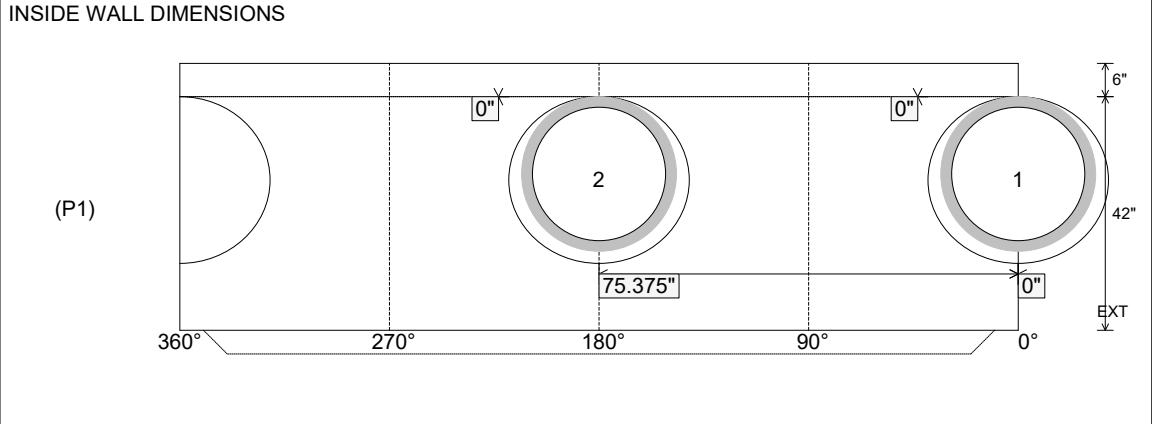

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 42" Height (Ext): 48"	Weight (Net): 3632 lb Volume (Net): 0.93cu.yd
----------------------------------	---------------------------------	--	--	--
