




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:31:29 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: C4 ST-CI										
P1 BX2436-08BA42					BOX BASE 8inW, 8inF F/n					
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 42" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 30 1) Hole - 32					0 lb 4667 lb 442 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5109 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 930.13' Rim to Invert: 3.87' Slack: 1.44" Sump: 3" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	926.26'	270°	26"	24" HDPE	27.8"	Hole 30	30"	30"	1.125"	0"
Invert 2	926.26'	90°	26"	24" RCP B WALL	30"	Hole 32	32"	32"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

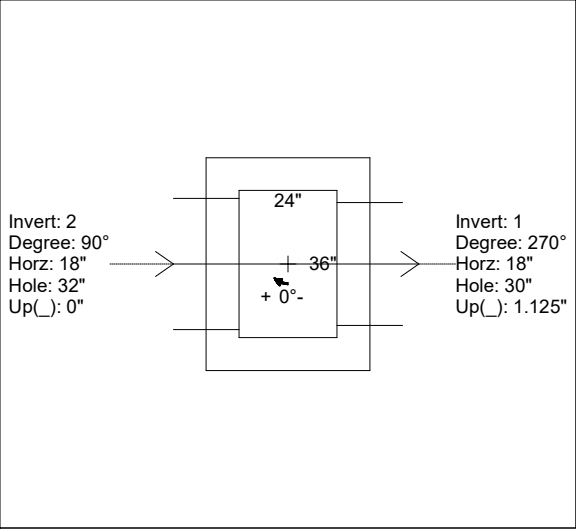


RIGHT-SIDE UP VIEW (int. dimensions)

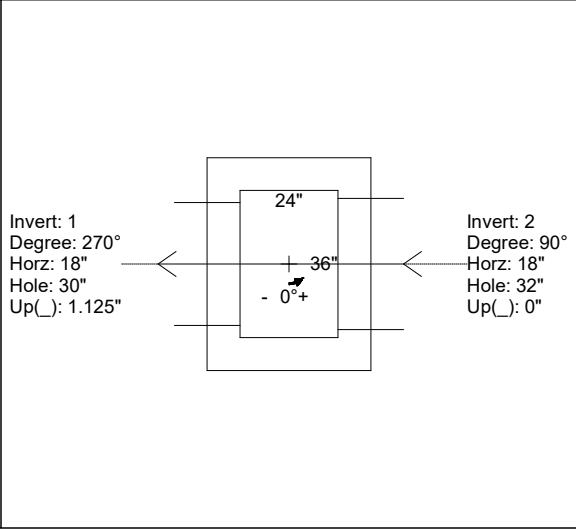

UPSIDE-DOWN VIEW (int. dimensions)

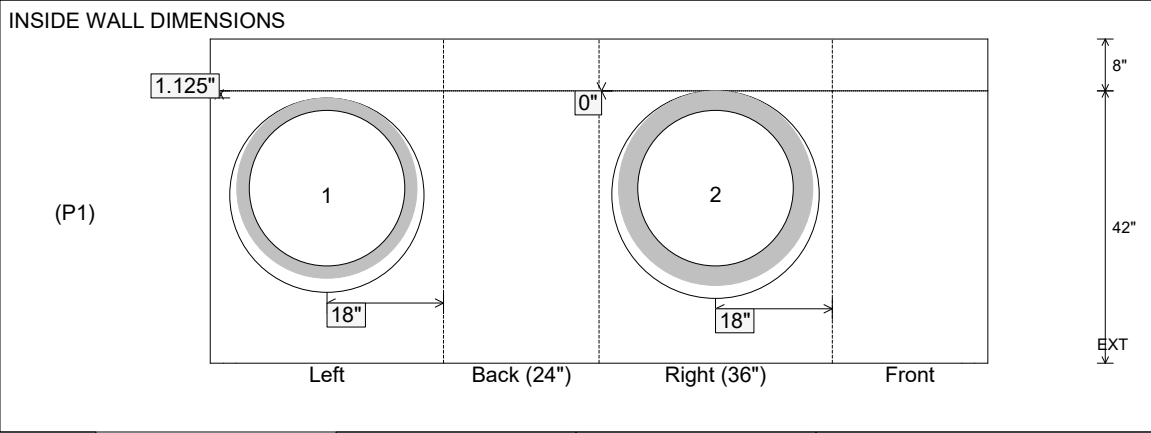

INSIDE WALL DIMENSIONS

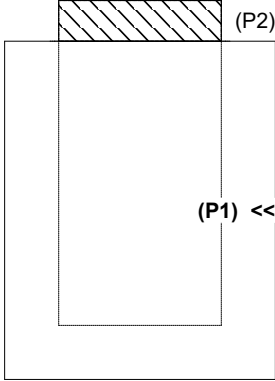

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 42" Height (Ext): 50"	Weight (Net): 4667 lb Volume (Net): 1.19cu.yd
----------------------------------	-------------------------------	--	--	--
