




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:27:01 AM		Tech: Jared - F PC: E. Bradley					
Structure ID: C6 ST-YD											
P1 MH048BAVF				MH BASE Custom Ht F/n							
P3) 24" x 24" - CASTING HEIGHT - 4" P2) 48" - MH FLAT TOP w/24"x24" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 37" 1) CASTING - HOE 280T F/G 1) 48" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 30						0 lb 1214 lb 3283 lb 182 lb 0 lb 0 lb 0 lb ----- Structure Total: 4679 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 930.5'				Rim to Invert: 3.93'		Slack: 1.06"		Sump: 1.9"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	926.57'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 2	926.57'	180°	91.125"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

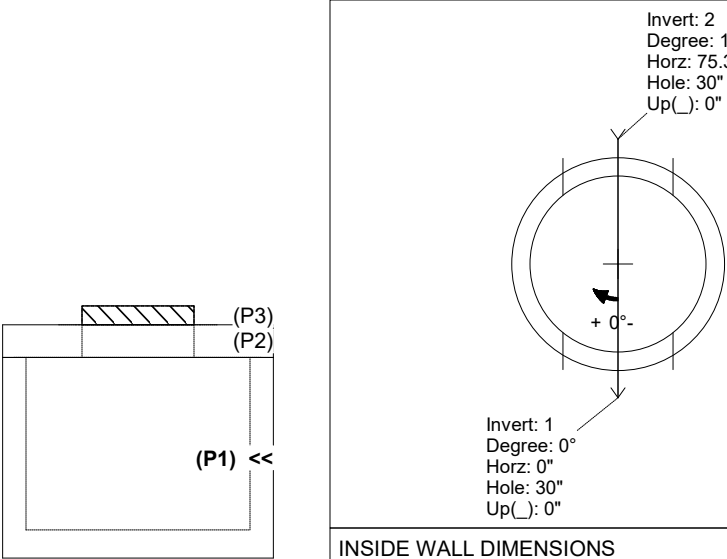

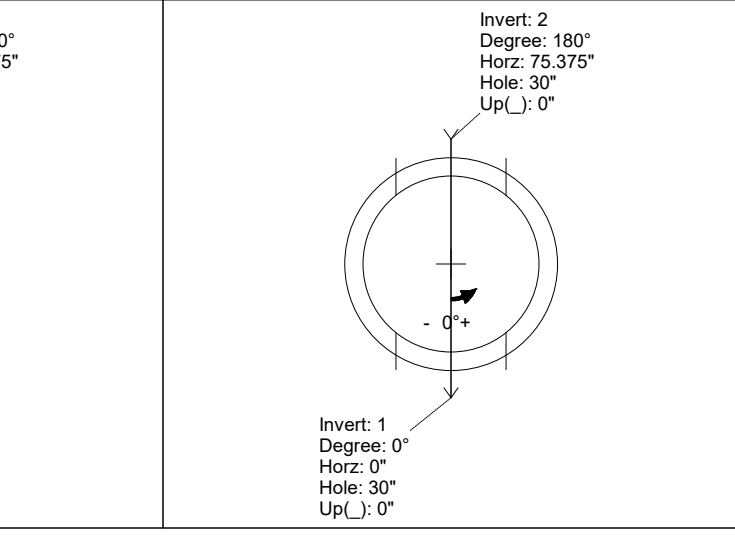

INSIDE WALL DIMENSIONS

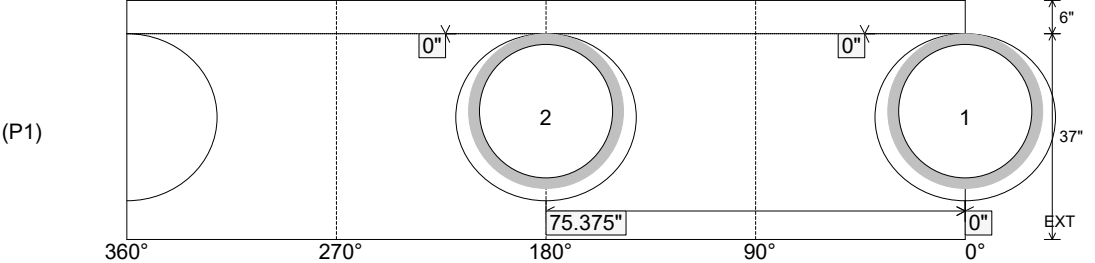

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 37" Height (Ext): 43"	Weight (Net): 3283 lb Volume (Net): 0.84cu.yd
----------------------------------	-------------------------------	--	--	--
