

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100




Slack: 1.68"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

- P4) 24" x 24" - CASTING HEIGHT - 4"
- P3) 24" x 24" - GRADE RING - 3"
- P2) 72" - MH FLAT TOP w/24"x24" Hole - 15"
- P1) 72" - MH BASE - 84"
- 1) CASTING - HOE 280T F/G
- 1) 72" - Conseal CS-102 1.00"
- 2) 24" x 24" - Conseal CS-102 1.00"
- 1) Hole - 50
- 1) Hole - 44
- 1) Hole - 46
- 7) MH Step ML-10-TDS-NCR - 10"


0 lb
258 lb
4772 lb
12898 lb
182 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 18110 lb

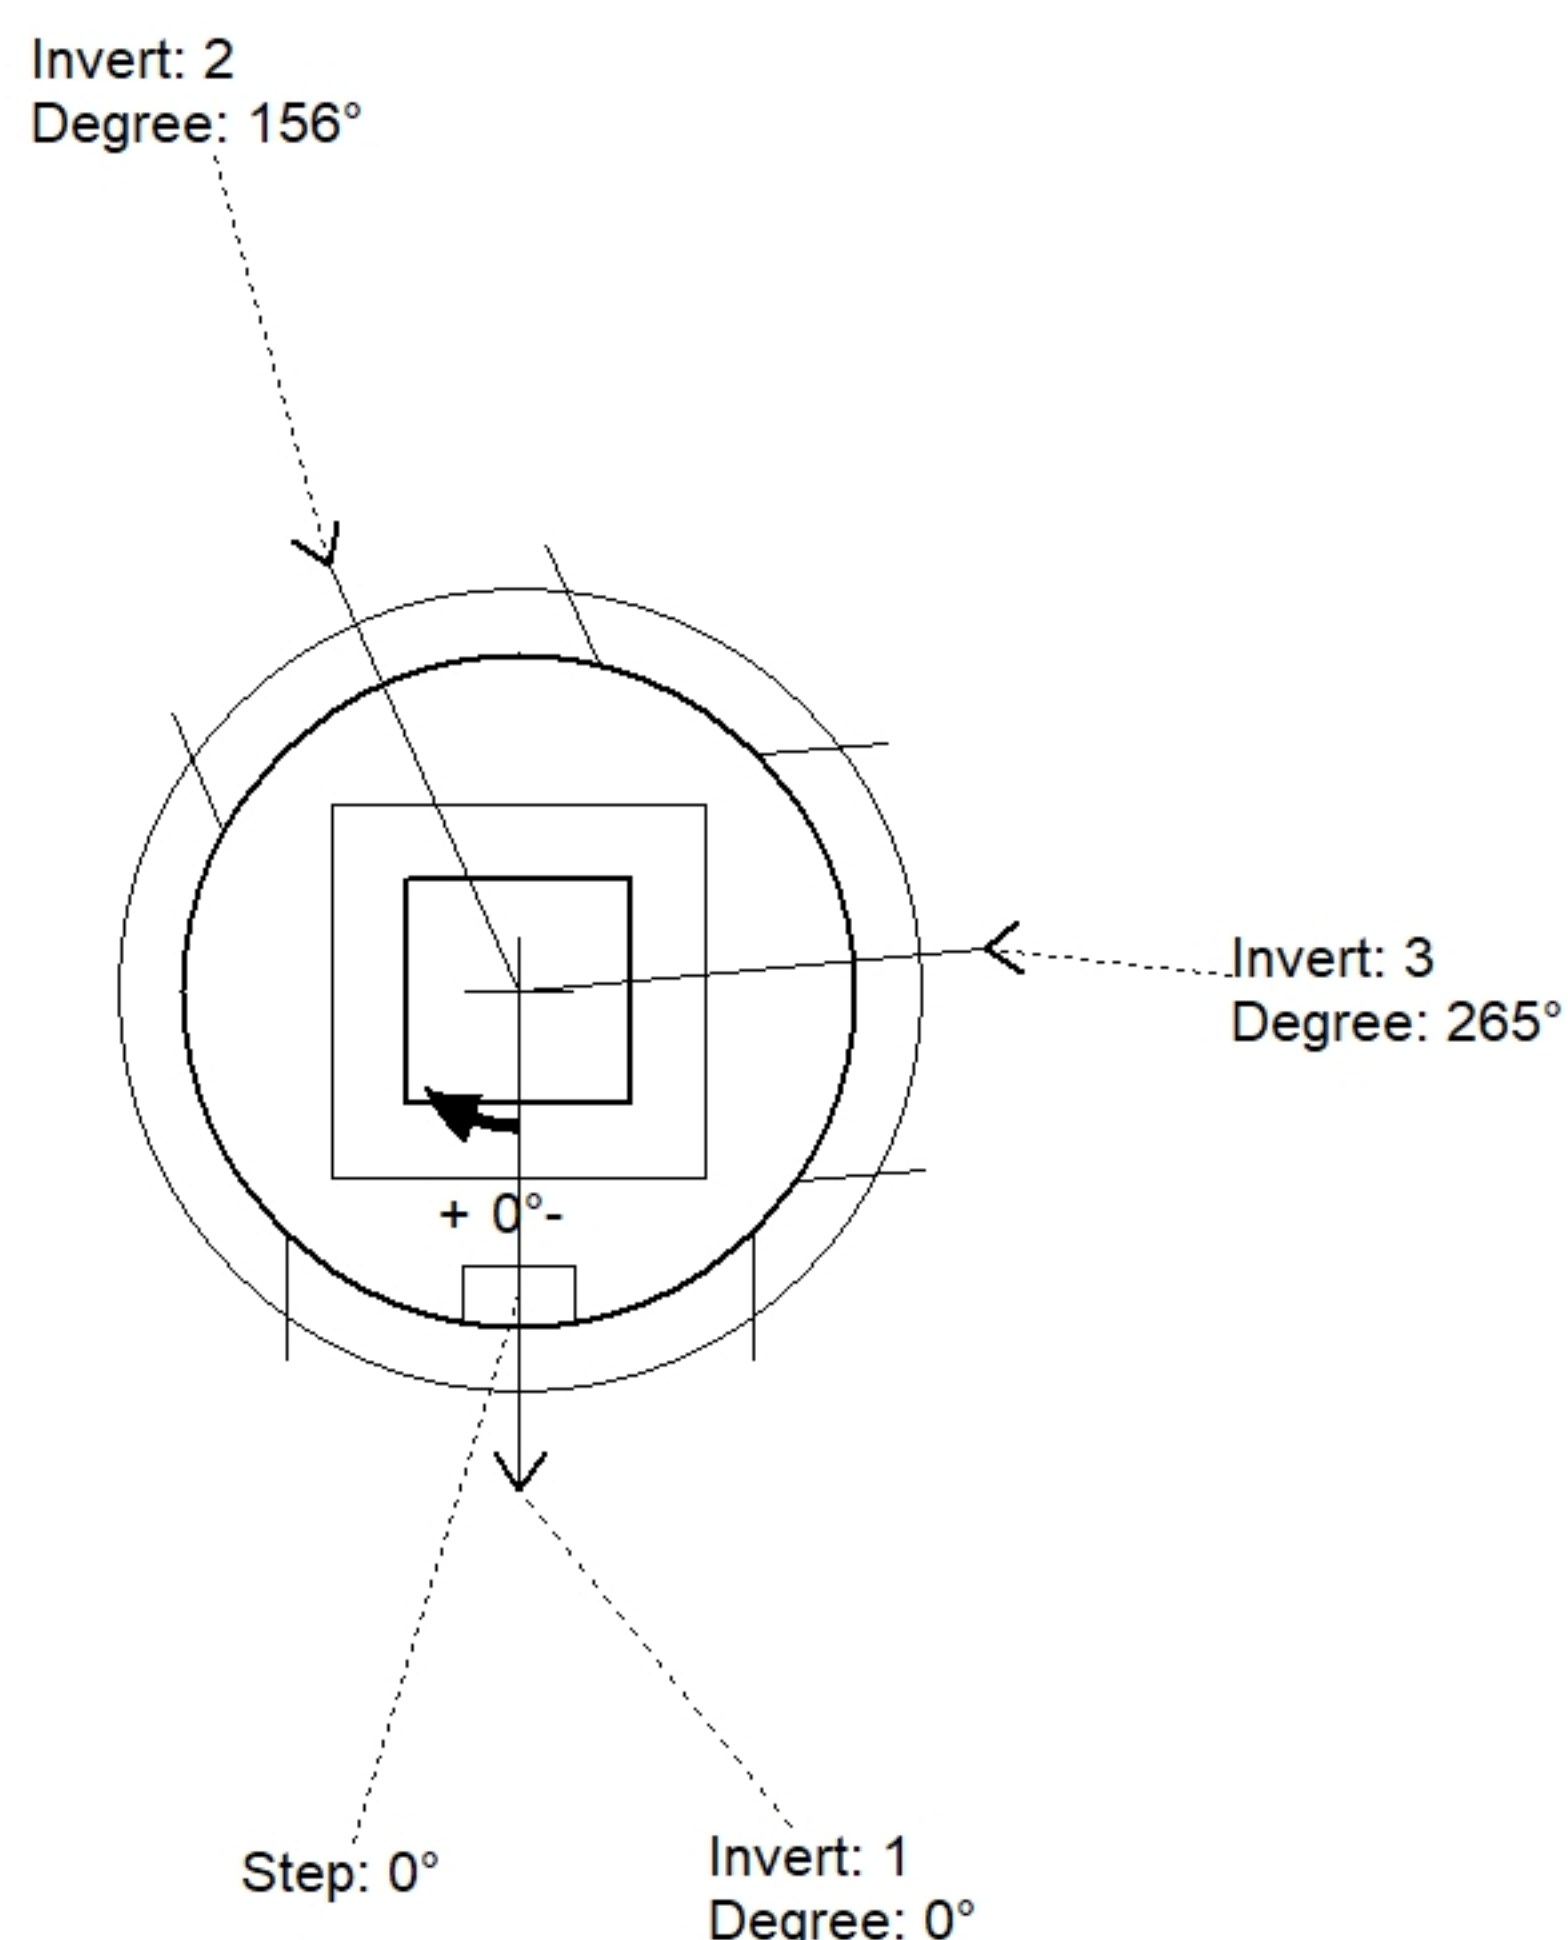

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	934.52'							
Reducer								
Invert 1	925.85'	0°	42" HDPE	47.7"	50"	Hole 50	0.49"	P1
Invert 2	925.85'	156°	36" HDPE	41.7"	44"	Hole 44	0.79"	P1
Invert 3	925.88'	265°	36" RCP B WALL	44"	46"	Hole 46	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

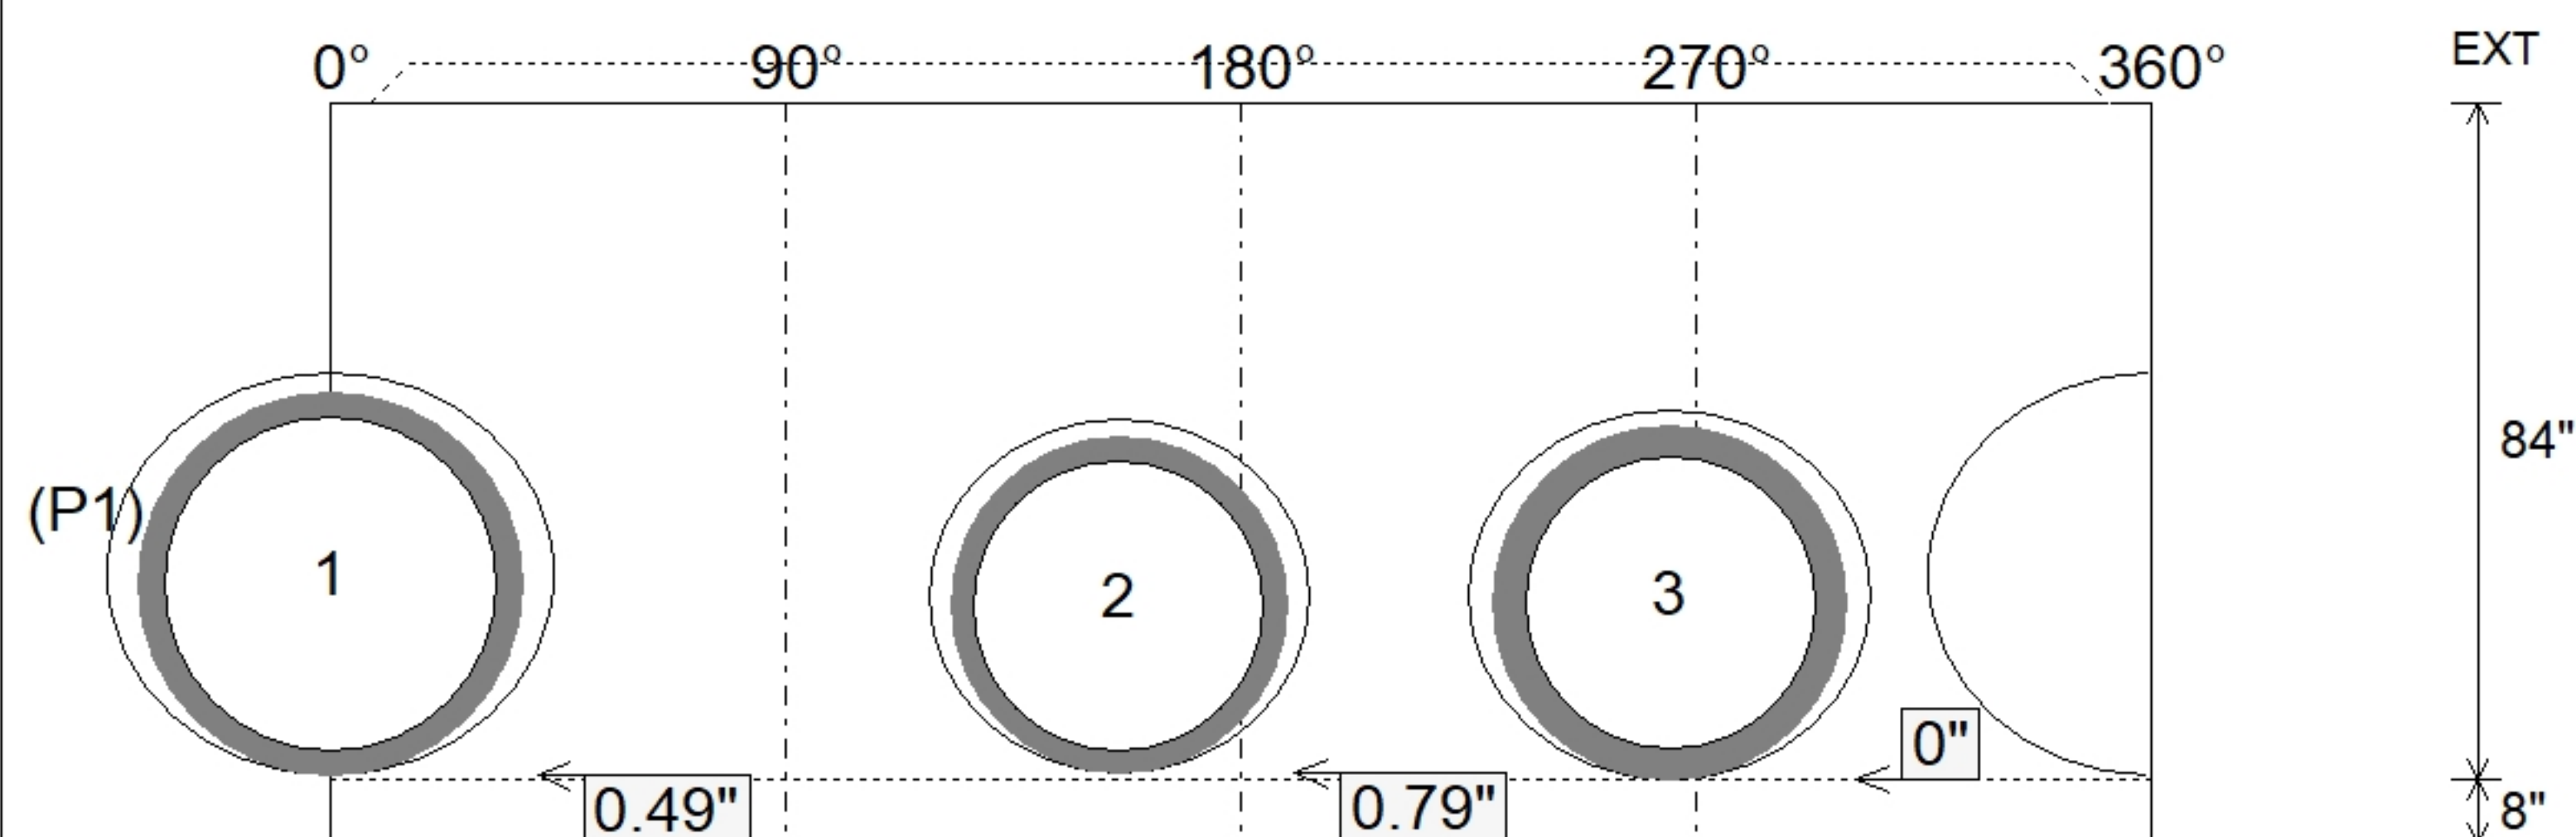

SUBMITTAL
APPROVED BY:
