




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:31:21 AM		Tech: Jared - F PC: E. Bradley						
Structure ID: F4.3 ST-CI												
P1 MH048BA36				MH BASE T/n								
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P1) 48" - MH BASE T/n - 36" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 32 1) Hole - 14 3) MH Step ML-10-TDS-NCR - 10"						0 lb 1300 lb 3178 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4920 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 933.05'				Rim to Invert: 4.4'		Slack: 1.8"		Sump: 3"		Step Position: 225°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	928.65'	0°	0"	24" RCP B WALL	30"	Hole 32	32"	35.027", 22.58"	0"	0"		
Invert 2	928.75'	68°	34.375"	10" HDPE	11.4"	Hole 14	14"	14.207"	3.5"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

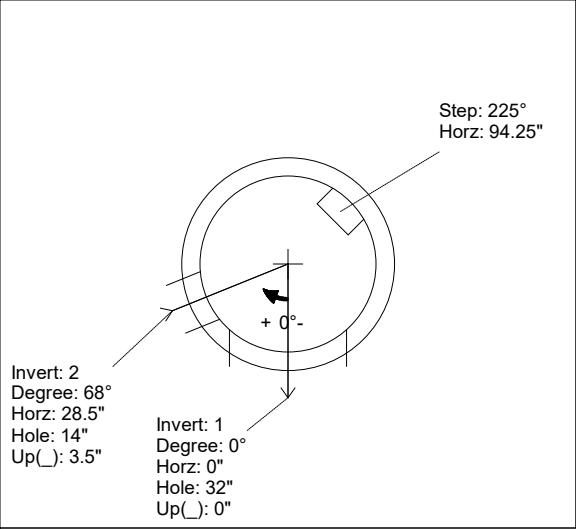

RIGHT-SIDE UP VIEW (int. dimensions)

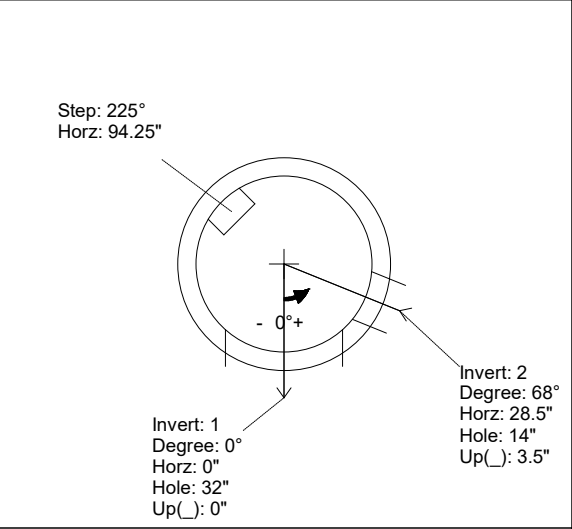

UPSIDE-DOWN VIEW (int. dimensions)

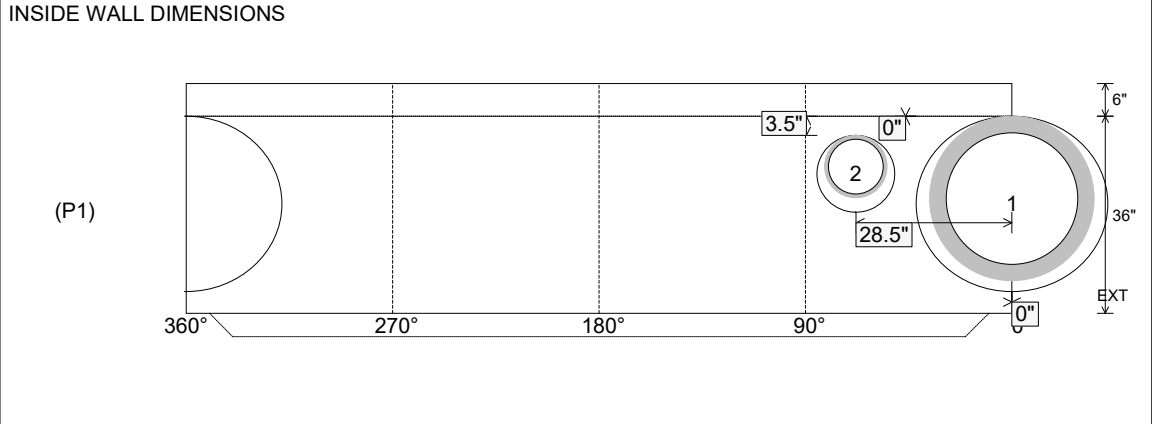

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3178 lb Volume (Net): 0.81cu.yd
----------------------------------	---------------------------------	--	--	--
