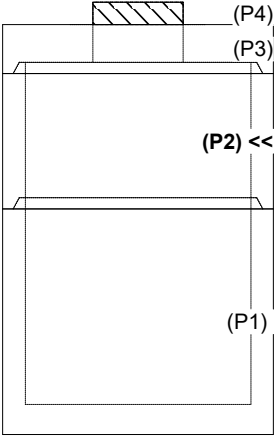




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks				Plant: 100 9/24/2026 11:34:25 AM		Tech: Jared - F PC: E. Bradley					
Structure ID: F5 ST-CI											
P2 MH060RS36				MH RISER T/G							
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 60" - MH FLAT TOP w/24"x36" Hole F/G - 13" P2) 60" - MH RISER T/G - 36" P1) 60" - MH BASE Custom Ht T/n - 52" 1) CASTING - HOE 525 LV SET (F/G/H) 2) 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 44 7) MH Step ML-10-TDS-NCR - 10"						0 lb 3499 lb 3758 lb 6369 lb 442 lb 0 lb 0 lb 0 lb 0 lb ----- 14068 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 935.01' Rim to Invert: 8.77' Slack: 1.115" Sump: 2.875" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 3758 lb Volume (Net): 0.96cu.yd	
