




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:31:15 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: F9.1 ST-CI											
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht F/n											
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 38" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 32 1) Hole - 26					0 lb 4466 lb 442 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 4908 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 933.68' Rim to Invert: 3.52' Slack: 1.24" Sump: 3" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	930.16'	270°	26"	24" RCP B WALL	30"	Hole 32	32"	32"	0"	0"	
Invert 2	930.66'	180°	20"	18" RCP B WALL	23"	Hole 26	26"	25"	6.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

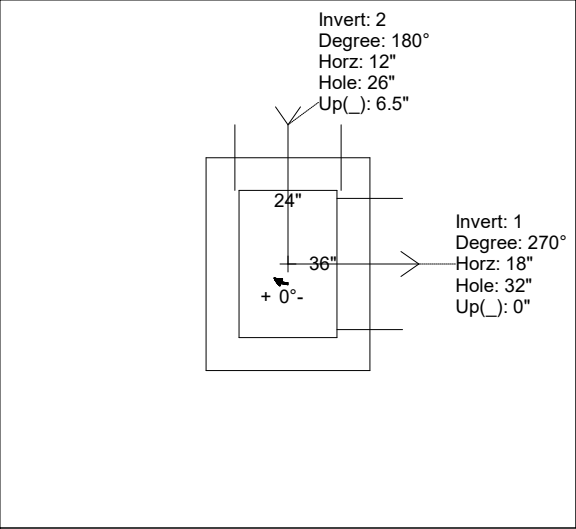

RIGHT-SIDE UP VIEW (int. dimensions)

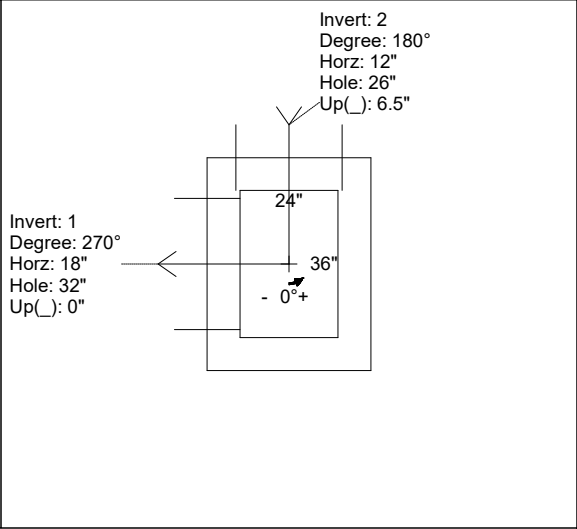

UPSIDE-DOWN VIEW (int. dimensions)

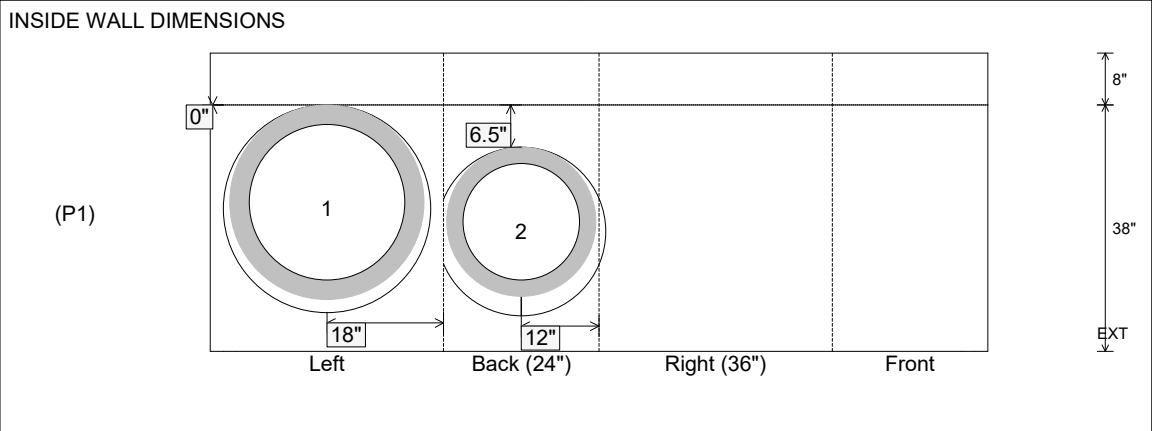

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 38" Height (Ext): 46"	Weight (Net): 4466 lb Volume (Net): 1.14cu.yd
----------------------------------	-------------------------------	--	--	--
